Social Monitoring Report

Bi-annual Social Monitoring Report April 2015

PAK: MFF – Power Distribution Enhancement Investment Program (Tranche 3)

Prepared by Islamabad Electric Supply Company, Federal Capital for the Asian Development Bank.

NOTES

- (i) The fiscal year (FY) of the Government of the Islamic Republic of Pakistan and its agencies ends on 30 June.
- (ii) In this report "\$" refer to US dollars.

This social monitoring report is a document of the Borrower. The views expressed herein do not necessarily represent those of ADB's Board of Directors, Management, or staff, and may be preliminary in nature.

In preparing any country program or strategy, financing any project, or by making any designation of or reference to a particular territory or geographic area in this document, the Asian Development Bank does not intend to make any judgments as to the legal or other status of any territory or area.





Bi-annual Social Safeguards Monitoring Report

Project Number:

2972 - PK, Tranche - III

{July - December, 2014}

Islamic Republic of Pakistan

Power Distribution Enhancement Investment Project (PDEIP) – Tranche – III Multi – Tranche Financing Facility (MFF)

Financed by the ASIAN DEVELOPMENT BANK

Prepared by

Environment & Social Safeguards Section –Management Unit Office of the Chief Engineer (Development)
ISLAMABAD ELECTRIC SUPPLY COMPANY (IESCO)
IESCO Head Office,
Street 40, G – 7 / 4, Islamabad, Pakistan.

For

Islamabad Electric Supply Company (IESCO)
Pakistan Electric Power Company (PEPCO)

This report does not necessarily reflect the views of ADB or the Government concerned, and ADB and the Government cannot be held liable for its contents.

Asian Development Bank

ABBREVIATIONS

ADB Asian Development Bank

AJK Azad Jammu & Kashmir

AHs Affected Households

E&SS Environmental and Social Safeguard

EA Executing Agency

EIA Environmental Impact Assessment

EPA Environmental Protection Agency

GOP Government of Pakistan

GRC Grievance Redress Committee

GS Grid Substation

IA Implementing Agency

IESCO Islamabad Electric Supply Company

Km Kilometer

KV Kilo - Volt

LARP Land Acquisition and Resettlement Plan

m² Square meter

MOW&P Ministry of Water and Power

MFF Multi - Tranche Financing Facility

PAPs Project Affected Persons

PDEIP Power Distribution Enhancement Investment Program

PEPCO Pakistan Electric Power Company

PMU Project Management Unit

MU Management Unit

ROW Right of Way

TL Transmission Line

TABLE OF CONTENTS

ABBRI	EVIATIONS	2
TABLE	OF CONTENTS	3
1: IN	TRODUCTION	4
1.1	IESCO	4
1.2	Directorate of CE (Development) / Management Unit (MU)	4
1.3	Environmental & Social Safeguard Section – Management Unit	4
1.4	Scope of the Work	5
1.5	Social Documentation, Approval & Disclosure	5
2. PF	ESENT STATUS OF THE PROJECT	7
2.1	Present Status of Civil Work.	7
2.2	Project Impacts	7
2.2	Replacement of Sangjani - Zeropoint 132 KV Transmission Line	7
2.2	Replacement of Burhan- New Wah 132 KV Transmission Line	7
2.3	2.3 Replacement of existing New Rawat – Sowan 132 KV T / Line	8
2.2	2.4 132 KV Chakri Road Grid Station & Feeding Transmission Line	8
2.2	2.5 132 KV Sangjani Grid Station & Feeding Transmission Line	8
2.2	2.6 KTM (I-16) - Chakri Road 132 KV Transmission Line	8
2.2	2.7 In & Out construction at Chakri Sub-Station 132 KV T / Line	9
2.2	2.8 Construction of Bara Kahu Grid Station and feeding 132 KV T/ Line	9
2.3	Awareness & Trainings.	9
ANNE	K - A 10	
IESC	O JURISDICTION MAP	10
ANNE	K-B 11	
ORC	ANIZATIONAL STRUCTURE OF MU – IESCO	11
ANNE	K-C 12	
DET	AIL SCOPE OF WORK OF TRANCHE - III SUBPROJECT	12

1: INTRODUCTION

1.1 IESCO

1. Islamabad Electric Supply Company Ltd. (IESCO) is a public utility company, having more than 02 Million consumers and provides service to 04 Nos. Northern Districts of the Punjab Province (Rawalpindi, Attock, Jhelum and Chakwal); Capital Territory (Islamabad); and Southern parts of Azad Jammu & Kashmir (AJK). IESCO jurisdiction map is placed at **Annex - A**.

1.2 Directorate of CE (Development) / Management Unit (MU)

- 2. To carry out and handle investment projects IESCO has established Management Unit (MU) under the supervision of Chief Engr. (Development). The MU comprises of four sections. The organizational structure of MU IESCO and main responsibilities of each section are given in Annex-B.
 - i) Planning Scheduling & Coordination
 - ii) Procurement
 - iii) Project Finance
 - iv) Environment & Social Safeguard

1.3 Environmental & Social Safeguard Section - Management Unit

3. The Environmental & Social Safeguard (E&SS) Section of MU, IESCO provides an overall supervision and advisory services during the Pre - Construction phase, Construction phase & Post - Construction phase of the project. The unit also assists and advises GSC Directorate, Construction Directorate and other IESCO departments on environmental and social matters overall. Organizational structure of E&SS - MU IESCO is attached as below.

Management Structure of E&SS - MU - IESCO.



1.4 Scope of the Work

4. IESCO Tranche – III subproject includes 03 No. constructions of new grid stations, 04 Nos. Extension, 09 Nos. Augmentation, 05 Nos. Transmission Lines (New), and 03 No. Transmission Lines (Remodelling). The detailed scope of work of Tranche - III subprojects is attached at **Annex - C**.

1.5 Social Documentation, Approval & Disclosure

- 5. The Short Land Acquisition and Resettlement Plans (LARPs) of following Transmission Lines & Grid Stations of Tranche-III as approved by ADB are available on IESCO website (in English and Urdu) for public information:
 - i. Replacement of Sangjani Zeropoint 132 KV Transmission Line.
 - ii. Replacement of Burhan- New Wah 132 KV Transmission Line.
 - iii. Replacement of existing New Rawat Sowan 132 KV T/ Line.
 - iv. 132 KV Chakri Road Grid Station & Feeding Transmission Line.
 - v. 132 KV Sangjani Grid Station & Feeding Transmission Line
 - vi. KTM Chakri Road 132 KV Transmission Line
 - vii. In & Out construction at Chakri Sub-Station 132 KV Transmission Line

The detail of documents prepared for the project are tabulated below:

				Documen	Documents Submission Date	Date		LARPs		
Proj. No	Project Name	IP Checlist	IR Checklist	REA	331	agg	LARP	Approved by ADB on	Award Date	Current Status
Grid S	Grid Stations									
11	Chakri Road	210	210	26/07/2012	28/09/2012	NA	19/09/2012	12/11/2012		
12	Bhara Kahu)Z 't⁄ð)Z 'Þ?	26/07/2012	07/09/2012	09/09/2012	NA			i) Sites Being Finalized
13	Sangjani 2	չ չվու	չ չվու	26/07/2012	28/09/2012	NA	28/09/2012	12/11/2012		II) Approval of BER awaited from BOD IESCO/ADB
Transn	Transmission Lines	uo p	uo p							
4	Replacement of Sangjani Zeropoint T Line with new Double Circuit	I bmitte	əttimd	26/07/2012	30/09/2012	NA	28/09/2012	12/11/2012	19/03/2014	
15	Feed for Barakhu GS	ns I	ıns ı	26/07/2012	07/09/2012	09/09/2012	NA		19/03/2014	
91	Feed from Chakri Road GS for Adyala	pue	pue	26/07/2012	28/09/2012	NA	19/09/2012	12/11/2012	19/03/2014	Work yet to get started.
17	Feed for 132 Kv Sangjani-2 GS	sto	sto	26/07/2012	28/09/2012	NA	28/09/2012	12/11/2012	19/03/2014	
81	KTM- Chakri Road T/Line	oje	əļo.	26/07/2012	30/09/2012	NA	28/09/2012	12/11/2012	19/03/2014	
61	Replacement of Burhan- N/Wah Cct 1 &2	-bı	-bu	26/07/2012	30/09/2012	NA	28/09/2012	12/11/2012		
110	Replacement of existing New Rewat – Sowan with new line on same route	qns III	qns III	26/07/2012	30/09/2012	NA	28/09/2012	12/11/2012		
111	In /Out at Chakri 132kV substation.	-əy:	-əy:	26/07/2012	30/09/2012	NA	28/09/2012	12/11/2012		
Extension	ion	ue.	ue.							
112	Rajjar	1T 10	ıT ło	2.		7.	NA			
113	Fateh jang	o əį	o əj				NA			
114	F-11	oų/	оцл				NA			
115	Sowan	טג א	N JC	o b -92	13- 13-	are ioni	NA			
Augme	Augmentation	of b	oł b	ietr	u	ietr				
116	Kamalabad (T2 and T3)	are	are	meı	oite	ueu	NA			
117	KTM (T3)	rep	ı.eb	เลิก	qua	เลิก	AN			
118	New Wah (T2)	d 1s	d 1s	A 8	gma	A 8	NA			
119	Jhelum (T1)	cklis	cklis	uo	'n∀	uo	NA			
121	Cantt Repco (T1)	әҷ	эцс	isus	8	isua	NA			
122	Zero Point (T2)) di) BI	Exte		Exte	NA			
123	I-10 (T2)	əu	əu	1		1	NA			
124	I-8 (T2)	0	0				NA			
125	Chaklala			ns		ns	NA			

2. PRESENT STATUS OF THE PROJECT

2.1 Present Status of Civil Work.

6. The civil works of following 132 KV T/lines sub-projects of Tr – III have been awarded, but the physical execution is yet to get underway. The detail of works awarded is provided below in table 2.1.

Table 2.1: Contract details

No.	Package	Lot No.	Description of Work	Awarded to	Contract Award Date	Civil work status
1	ICB-01/TR-III/ADB	П	 a) F/F 132 KV Chakri Road G/Station b) F/F 132 KV Sangjani-2 G/Station c) F/F 132 KV Bara Kahu G/Station. d) Replacement of Sangjani-Zero point 132 KV T/line. e) 132 KV KTM - Chakri 	M/s ICC (Pvt), Lahore.	19-03-2014	Work not yet started due to pending approvals of sub- contractors.

2.2 Project Impacts

2.2.1 Replacement of Sangjani - Zeropoint 132 KV Transmission Line

7. The 28 KM replacement of Sangjani – Zero Point 132 kV transmission line subproject is traversing i) government land, ii) three housing societies in Islamabad; iii) two villages of Islamabad and iv) Jangi Sydian village of district Rawalpindi. The transmission line route already exists and there will be one more tower/pole added between two existing towers without acquiring any additional land by affecting crops and trees of 41 households. None of the household will be displaced or lose more than 10% of their productive assets.

2.2.2 Replacement of Burhan- New Wah 132 KV Transmission Line

8. The replacement of Burhan – New Wah 132 kV transmission line subproject is located in Attock District of Punjab. The 13 Km transmission line will traverse Private cultivated and broken land, government land, one Housing

society and five villages, of District Attock. The transmission line route already exists but the construction activities will affect crops and trees of 18 households. No land will acquired permanently for this subproject. None of the household will be displaced or lose more than 10% of their productive assets.

2.2.3 Replacement of existing New Rawat - Sowan 132 KV T / Line

9. The New Rawat to Swan 132kV transmission line subproject is located in Islamabad. The construction activities of transmission line will temporarily affect crops and trees of 07 households. None of the household will be displaced or lose more than 10% of their productive assets.

2.2.4 132 KV Chakri Road Grid Station & Feeding Transmission Line

10. The grid station will be constructed on IESCO's own 30 kanal Land situated on chakri road located at about 20 km from Rawalpindi Sadar. To feed this Grid Station a new 10 km transmission line (TL) will be constructed. There is no land acquisition process involved in this subproject. The transmission line will traverse through private barren and cultivated land of five villages by temporarily affecting crops and tress. None of the household will be displaced or lose more than 10% of their productive assets.

2.2.5 132 KV Sangjani Grid Station & Feeding Transmission Line

11. The proposed grid station will be constructed in Multi Professional Housing Society (MPHS). The land has been acquired free of cost from the society. To feed this grid station a 02 Km long 132 KV transmission line will be constructed from the existing 220 KV grid station Sangjani. The construction activities will affect crops of 02 households. None of the household will be displaced or lose more than 10% of their productive assets.

2.2.6 KTM (I-16) - Chakri Road 132 KV Transmission Line

12. The KTM (I-16) - Chakri Road 132 kV transmission line subproject is located in Islamabad and Rawalpindi District of Punjab. The 10 Km transmission line will traverse through private barren and cultivated land of four villages. The construction activities of transmission line will temporarily

affect crops and trees of 12 households. None of the household will be displaced or lose more than 10% of their productive assets.

2.2.7 In & Out construction at Chakri Sub-Station 132 KV T/Line

13. The In & Out construction at Chakri Sub-Station 132 kV transmission line subproject is located in Rawalpindi District of Punjab. The 22 Km transmission line will traverse through private barren and cultivated land of seven villages. The construction activities of transmission line will temporarily affect crops and trees of 12 households. None of the household will be displaced or lose more than 10% of their productive assets.

2.2.8 Construction of Bara Kahu Grid Station and feeding 132 KV T/ Line


14. The old site has been changed, IESCO Sitting and Lay out Board has visited and selected a site near Bara Kahu, and the Management is in process of finalizing ToRs and land price with the private society for construction of the grid station. Subsequent DD/LARP will be prepared if required.

2.3 Awareness & Trainings.

15. To develop the in-house capacity, IESCO arranged a numbers of training for different cadres / staff of GSC Directorate, who are responsible for supervision of development projects. On site / on job trainings will be arranged during the execution of project activities regarding environmental issues, social issues, housekeeping, record keeping, communicable diseases especially HIV/AIDS, Hepatitis, Tuberculosis (TB) & Drugs, defensive driving, site restoration after the work and overall implementation of the Environmental Management Plan (EMP) of Tranche – III subproject.


ANNEX - A

IESCO JURISDICTION MAP

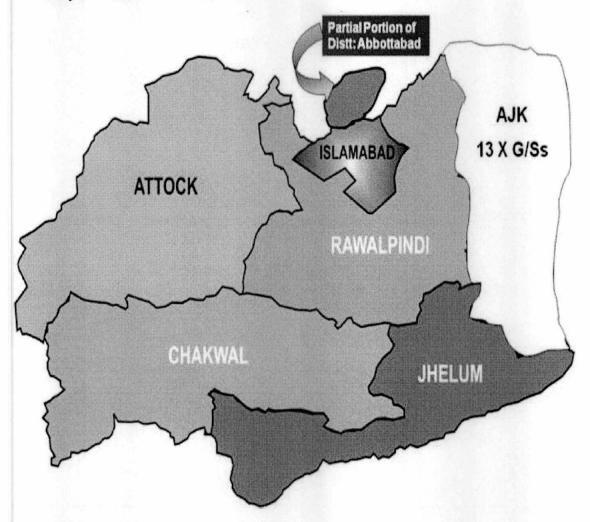

ANNEX - B

ORGANIZATIONAL STRUCTURE OF MU - IESCO

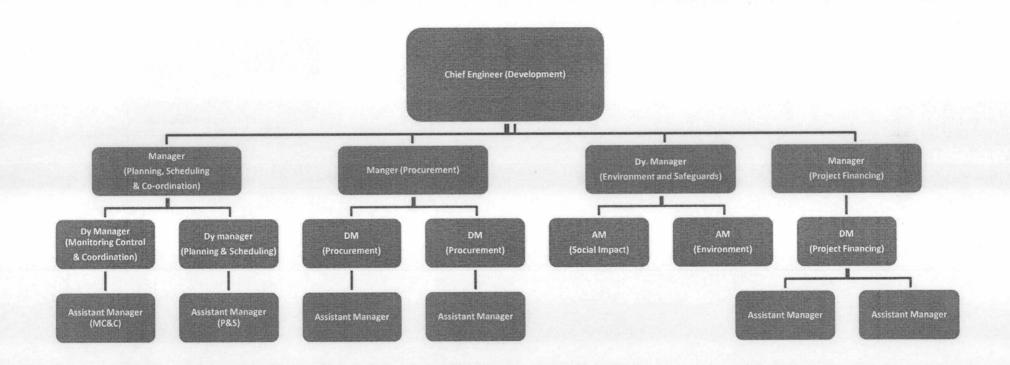

ANNEX - C

DETAIL SCOPE OF WORK OF TRANCHE - III SUBPROJECT

Scope of Tranche-III Projects

No.	Project Component					
	New Grid Station. 03 Nos.					
01.	i.	132 kV Bara Kahu Grid Station.				
	ii.	132 kV Chakri Road Grid Station.				
	iii.	132 kV Sangani - II Grid Station.				
	Exten	sion of Power Transformers	04Nos.			
	iv.	132 kV Rajjar Grid Station.				
02.	v.	132 kV Fateh Jang Grid Station.				
	vi.	132 kV F - 11 Grid Station.				
	vii.	132 kV Sowan Grid Station.				
	Augn	nentation of Power Transformers	09 Nos.			
	viii.	132 kV Kamalabad Grid Station.				
	ix.	132 kV KTM Grid Station.				
	x.	132 kV New Wah Grid Station.				
00	xi.	132 kV Jhelum Grid Station.				
03.	xii.	132 kV Rawalpindi Cantt (REPCO) Grid Stati	on.			
	xiii.	132 kV Zero Point Grid Station.				
	xiv.	132 kV I - 10 Grid Station.				
	xv.	132 kV I - 8 Grid Station.				
	xvi.	132 kV Chaklala Grid Station.				
	Trans	mission Lines (New)	04 Nos.			
	xvii.	. 132 kV Feed for Bara Kahu Grid Station Transmission Line.				
04.	xviii.	132 kV Feed for Chakri Road Grid Station Transmission Line.				
	xix.	132 kV Feed for Sangjani -II Grid Station Transmission Line.				
	xx. 132 kV KTM - Chakri Road Transmission Line.					
	Trans	mission Lines (Remodeling / Replacement)	04 No.			
	xxi. 132 kV Sangjani – Zero Point Transmission Line.					
05.	xxii.	132 kV Burhan - New Wah Transmission Line.				
	xxiii.	132 kV New Rewat - Sowan Transmission Line.				
	xxiv.	xiv. 132 kV in – out Construction at Chakri Grid Station T/ Line.				

Re: Fw: Loan 2972-PAK: PDEIP, Tranche 3 - Submission of Bi-annual Social Monitoring Report -

IESCO

Vergel M. Medina

to:

Liaqat Ali

17/04/2015 03:35 PM

Cc:

Adnan Tareen, Ehtesham Z. Khattak

Hide Details

From: Vergel M. Medina/CWRD/ADB To: Liaqat Ali/PRM/ADB@ADB

Cc: Adnan Tareen/CWRD/ADB@ADB, Ehtesham Z. Khattak/PRM/ADB@ADB

Security:

To ensure privacy, images from remote sites were prevented from downloading. Show Images

Dear Liagat,

The Bi-annual SMR for IESCO is ready for disclosure. Many thanks.

Best Vergel

----Liaqat Ali/PRM/ADB wrote: ----

To: Vergel M. Medina/CWRD/ADB@ADB

From: Liaqat Ali/PRM/ADB Date: 03/25/2015 11:49AM

Cc: Adnan Tareen/CWRD/ADB@ADB, Ehtesham Z. Khattak/PRM/ADB@ADB

Subject: Fw: Loan 2972-PAK: PDEIP, Tranche 3 - Submission of Bi-annual Social Monitoring

Report - IESCO

Dear Vergel:

As advised by Mike I am forwarding the below Bi-annual Social Monitoring Report for IESCO for your review and comments, if any.

Thanks and regards,

Liaqat Ali, Project Analyst, Pakistan Resident Mission

Level 8, North, Serena Office Complex, G-5, Islamabad/Pakistan

Tele: (92-51) 2600351-69/2087210 Fax: (92-51) 2600365-66/2087397-98

email: lali@adb.org.

---- Forwarded by Liagat Ali/PRM/ADB on 25/03/2015 08:46 AM ----

From: Liagat Ali/PRM/ADB

To: Michael J. Beauchamp/CWRD/ADB@ADB

Cc: Adnan Tareen/CWRD/ADB@ADB, Ehtesham Z. Khattak/PRM/ADB@ADB

Date: 17/02/2015 01:22 PM

Subject: Fw: Loan 2972-PAK: PDEIP, Tranche 3 - Submission of Bi-annual Social Monitoring

Report - IESCO

Der Mike:

The last one please.

Regards,

Liaqat Ali, Project Analyst, Pakistan Resident Mission

Level 8, North, Serena Office Complex, G-5, Islamabad/Pakistan

Tele: (92-51) 2600351-69/2087210 Fax: (92-51) 2600365-66/2087397-98

email: lali@adb.org.

---- Forwarded by Liagat Ali/PRM/ADB on 17/02/2015 01:22 PM ----

From: Liagat Ali/PRM/ADB

To: Michael J. Beauchamp/CWRD/ADB@ADB,

Cc: Adnan Tareen/CWRD/ADB@ADB, Ashfaq Khokhar/PRM/ADB@ADB, Nianshan

Zhang/PRM/ADB@ADB

Date: 03/02/2015 01:38 PM

Subject: Fw: Loan 2972-PAK: PDEIP, Tranche 3 - Submission of Bi-annual Social Monitoring

Report - IESCO

Dear Beauchamp:

As advised below by Mr. Khokhar I understand you have been assigned Loan 2972. Please review the social monitoring report below submitted by IESCO and provide your comments, if any, or approve the report for disclosure.

Regards,

Liaqat Ali, Project Analyst, Pakistan Resident Mission

Level 8, North, Serena Office Complex, G-5, Islamabad/Pakistan

Tele: (92-51) 2600351-69/2087210 Fax: (92-51) 2600365-66/2087397-98

email: lali@adb.org.

---- Forwarded by Liagat Ali/PRM/ADB on 03/02/2015 01:25 PM ----

From: Ashfaq Khokhar/PRM/ADB To: Liagat Ali/PRM/ADB@ADB,

Cc: Adnan Tareen/CWRD/ADB@ADB, Imran Ali Memon/PRM/ADB@ADB, Rizwan

Haider/Contractors/ADB@ADB, Nianshan Zhang/PRM/ADB@ADB

Date: 03/02/2015 01:24 PM

Subject: Re: Fw: Loan 2972-PAK: PDEIP, Tranche 3 - Submission of Bi-annual Social Monitoring

Report - IESCO

Dear Liagat,

This tranche is being looked after by Mike Beauchamp. He has returned from leave. you may send the report for his review.

Thank you Ashfaq

> Ashfaq Ahmed Khokhar Sr. Social Safeguard Officer Pakistan Resident Mission Asian Development Bank Tel (92) 051-2087300 Ext 230

Fax. +92 51 260 0365-66/208 7397-98

www.adb.org



Liaqat Ali---03/02/2015 01:18:24 PM---Dear Ashfaq: Please review and provide your comments, if any or approve for disclosure.

From: Liagat Ali/PRM/ADB

To: Ashfaq Khokhar/PRM/ADB@ADB,

Cc: Adnan Tareen/CWRD/ADB@ADB, Imran Ali Memon/PRM/ADB@ADB, Rizwan

Haider/Contractors/ADB@ADB Date: 03/02/2015 01:18 PM

Subject: Fw: Loan 2972-PAK: PDEIP, Tranche 3 - Submission of Bi-annual Social Monitoring

Report - IESCO

Dear Ashfaq:

Please review and provide your comments, if any or approve for disclosure.

Regards,

Liaqat Ali, Project Analyst, Pakistan Resident Mission

Level 8, North, Serena Office Complex, G-5, Islamabad/Pakistan

Tele: (92-51) 2600351-69/2087210 Fax: (92-51) 2600365-66/2087397-98

email: lali@adb.org.

---- Forwarded by Liagat Ali/PRM/ADB on 03/02/2015 01:16 PM ----

From: PMU IESCO Islamabad <iescopmu@hotmail.com>

To: liagat Ali Project Analyst ADB Mission Pak < lali@adb.org >,

Cc: Ashfaq Khokhar ADB <akhokhar@adb.org>

Date: 03/02/2015 12:19 PM

Subject: Loan 2972-PAK: PDEIP, Tranche 3 - Submission of Bi-annual Social Monitoring Report -

IESCO

Dear Liagat Ali Sb.

Attached herewith find the Bi-annual Social Monitoring Report of Tranche-III sub-projects (L # 2972) in respect of IESCO as desired please.

Regards.

Mohammad Yasin

Dy. Manager (E&SS)

O/O Chief Engineer (Development)
Project Management Unit

IESCO, Islamabad.

To: iescopmu@hotmail.com

Subject: RE: Loans 2727-PAK: and 2972-PAK: PDEIP, Tranche 2 and 3 - Submission of Bi-annual Social

and Environmental Monitoring Reports

From: lali@adb.org

Date: Thu, 29 Jan 2015 14:50:11 +0500

Thank you for your prompt respone. Please note that I have requested for the SMR for Loan 2972 and not for 2727 (already received and reviewed by ADB). Please submit SMR for Loan 2972 immediately.

Regards,

Liaqat Ali, Project Analyst, Pakistan Resident Mission

Level 8, North, Serena Office Complex, G-5, Islamabad/Pakistan

Tele: (92-51) 2600351-69/2087210 Fax: (92-51) 2600365-66/2087397-98

email: lali@adb.org.

From: PMU IESCO Islamabad <iescopmu@hotmail.com>
To: liaqat Ali Project Analyst ADB Mission Pak <lali@adb.org>,

Date: 29/01/2015 02:33 PM

Subject: RE: Loans 2727-PAK: and 2972-PAK: PDEIP, Tranche 2 and 3 - Submission of Bi-annual Social and Environmental

Monitoring Reports

Dear Liagat Sb

IESCO has already submitted the required documents on January 09, 2015 via e-mail. The same e-mail is once again forwarded for information and record please.

Bi-annual Social Monitoring Report - T2 (L-2727) is re-attached for ready reference, where as the Bi-annual social monitoring report for T3 (L-2972) is not due as the projects field execution is yet to start.

Regards.

Mohammad Yasin Dy. Manager (E&SS)

For

Chief Engineer (Development)
Project Management Unit
IESCO, Islamabad.

From: iescopmu@hotmail.com

To: sshafiq.consultant@adb.org; akhokhar@adb.org

CC: riazali.shah84@gmail.com; atareen@adb.org; zabbas@adb.org; rhaider.contractor@adb.org;

lali@adb.org; yasin_ktk@hotmail.com

Subject: L-2727, L-2972 PDEIP: Submission of Bi-Annual Monitoring Reports (Jul-Dec 2014)

Environment & Social

Date: Fri, 9 Jan 2015 12:29:14 +0500

Dear Ma'm Safia and Mr. Ishfaq Khokar

The following Bi-annual Monitoring reports of PDEIP T2 (L-2727) and T3 (L-2972) for the period July-December 2013 in respect of IESCO are attached herewith for information and record as per requirement please.

- i) Bi-annual Environment Monitoring Report T2 (L-2727)
- ii) Bi-annual Social Monitoring Report T2 (L-2727)
- iii) Bi-annual Environment Monitoring Report T3 (L-2972)

The Bi-annual social monitoring report for T3 (L-2972) is not due as all the projects field execution is yet to start.

Regards.

Mohammad Yasin Dy. Manager (E&SS)

For Chief Engineer (Development) Project Management Unit IESCO, Islamabad.

(See attached file: Bi Annual SMR Tr-III (L# 2972)_IESCO July - December, 2014.pdf)

[attachment "Bi Annual SMR Tr-III (L# 2972)_IESCO July - December, 2014.pdf" removed by Vergel M. Medina/CWRD/ADB]
