

Social Monitoring Report

Semi Annual Report

Project Number: 41155-013

Loan/Grant Number: L2808/G0270/G0271

Period covered: (Jan-Jun) 2019

July 2019

NEP: Electricity Transmission Expansion and Supply Improvement Project (ETESIP)

Prepared by Nepal Electricity Authority for the Asian Development Bank.

This Social Monitoring Report is documents owned by the borrower. The views expressed herein do not necessarily represent those of ADB's Board of Directors, Management, or staff and may be preliminary in nature. In preparing any country program or strategy, financing any project, or by making any designation of or reference to a particular territory or geographical area in this document, the Asian Development Bank does not intend to make any judgement as to the legal or other status of any territory or area.



Semi- Annual Social Safeguards Monitoring Report

January - June, 2019

NEP: Electricity Transmission Expansion and Supply Improvement Project

(ETESIP, ADB: Loan No. 2808/ Grant No. 0270/ 0271)

Prepared by: Nepal Electricity Authority
Project Management Directorate (PMD)

Submitted to: Asian Development Bank
Nepal Residence Mission

July- 2019

Semi -Annual Social Safeguards Monitoring Report

Acronyms and Abbreviations

ADB	Asian Development Bank
CFUGs	Community Forest User Groups
CSR	Corporate Social Responsibility
CPP	Compensatory Plantation Plan
DFCC	District Forest Coordination Committee
EM	Entitlement Matrix
ESMU	Environmental and Social Management Unit
ESSD	Environment and Social Studies Department
ETESIP	Electricity Transmission and Supply Improvement Project
GoN	Government of Nepal
GRC	Grievance Redress Committee
Ha	hectare
HH	Household
HPP	Hydro Power Project
IEE	Initial Environmental Examination
IP	Indigenous People
IR	Involuntary Resettlement
LRO	Land Revenue Office
NEA	Nepal Electricity Authority
PAF	Project Affected Family
PCC	Plain Cement Concrete
PTDEEP	Power Transmission and Distribution Efficiency Enhancement Project
RAP	Resettlement Action Plan
RCC	Reinforced Cement Concrete
RM	Rural Municipality
RP	Resettlement Plan
RoW	Right of Way
SDFO	Sub-divisional Forest Office
SPS	Safeguard Policy Statement
TKTLP	Tamakoshi-Kathmandu 220/400kV Transmission Line Project
TL	Transmission Line

Table of Contents

Acronyms and Abbreviations.....	i
Table of Contents.....	ii
1. Introduction.....	1
1.1 Background.....	1
1.2 Project Components and Physical Progress.....	1
1.3 Monitoring Requirements and Frequency of Submission.....	2
1.4 Scope of Monitoring Report.....	2
1.5 Reporting Period.....	3
2. Changes in Project Scope and Adjusted Safeguard Measures.....	3
3. Qualitative and Quantitative Data.....	3
4. Monitoring Parameters/Indicators and Methods.....	3
5. Monitoring Results.....	4
5.1 Documentation and Approval.....	4
5.2 Safeguard Objectives.....	4
5.2.1 Safeguard Implementation Progress.....	4
5.2.2 Safeguard Compliance Monitoring Review Mission.....	4
5.3 Land Acquisition and Compensation.....	5
5.3.1 Compensation for Acquired Land.....	5
5.3.2 Compensation for Structure Loss.....	6
5.3.3 Compensation for Trees/Plants.....	6
5.3.4 Major Issues in Land Acquisition and Compensation Distribution.....	6
5.3.5 Livelihood Restoration Program.....	7
5.3.6 Ensuring IPs Identity, Human Rights, Livelihood and Cultural Uniqueness.....	7
5.3.7 Grievance Redress Mechanisms.....	8
6. Public Consultation and Information Disclosure.....	10
7. Corporate Social Responsibility.....	11
8. Gaps and Corrective Action Plan for Mitigation.....	11
9. Recommendations.....	12
10. Institutional Arrangement for Monitoring.....	12
11. Proposed Major Items of Focus for Next Month.....	13

List of Tables

Table 1: Physical Progress of the Project Activities.....	1
Table 2: Sub-Project Components with Land Acquisition and Resettlement Impacts.....	3
Table 3: Details of Land Acquisition.....	5
Table 4: Compensation Distribution Status.....	6
Table 5: Compensation Distribution for Structure Loss.....	6
Table 6: Major Issues Associated with Land Acquisition.....	6
Table 7: Status of Project Affected Households.....	8
Table 8: GRC Formation Details.....	8
Table 9: Underlying Issues and Grievances.....	9
Table 10: Local Consultative Meeting Details.....	10
Table 11: List of CSR Activities and its Details.....	11
Table 12: Gaps and Corrective Plan of Action.....	11
Table 13: Proposed Major Item of Focus for Next Month.....	13

List of Annexes

Annex- 1: Entitlement Matrix.....	I
Annex- 2: Compliance Monitoring Results in terms of Involuntary Resettlement Safeguards.....	III
Annex- 3: Monitoring Results in terms of Indigenous Peoples Safeguards.....	V

Annex- 4: An Assessment Report submitted as requested by ADB ETESIP Review Mission.....	VI
Annex- 5: GRC Formation Meeting Minutes.....	IX
Annex- 6: Documentation of Recorded Grievances and its Address.....	XII
Annex- 7: Local Consultative Meeting Minutes.....	XX
Annex- 8: Notice for Implementing CSR Activities.....	XXI
Annex- 9: Photographs.....	XXIV

1. Introduction

1.1 Background

The Project is the part of Electricity Transmission Expansion & Supply Improvement Project of NEA. The Electricity Transmission Expansion and Supply Improvement Project (ETESIP) was approved on 15th November 2011 with its completion date extended to 31st March 2020. The ETESIP is a \$128 million project with financial assistance of 44% loan and 34% grant support from ADB, Government of Norway, NEA and Government of Nepal. The project also has an approved fund of \$2 million for capacity development assistance. The project comprises of following three major integrals:

- Transmission Line expansion, including new transmission lines and substations
- Distribution System expansion
- Rehabilitation of Hydropower stations

Based on these major integrals, the project has following components:

- Tamakoshi Kathmandu 220/400kV TL
- Rehabilitation of 640kV Sundarijal HPP
- Rehabilitation of 1MW Tinau HPP
- Augmentation of distribution Services (East i.e. Jare, Gaur, Nijgadh, Chandraghadhi and Belbari)
- Augmentation of Distribution Services (West i.e. Parasi, Amuwa, Taulihawa, Krishnanagar, Gorkha, Mirm and Gaddachowki)
- Expansion of Chapali SS, Kohalpur-Mahendranagar 132kV second circuit
- Upgradation of distribution lines at Kathmandu, Bhaktapur, Kavrepalanchowk, Sindhupalchowk, Dolakha, Sindhuli and Ramechhap Districts

Among the above components Tamakoshi -Kathmandu Transmission Line Project (TKTLP) is in its initial phase of construction. The Initial Environment Examination (IEE) of TKTLP has been prepared in abidance with ADB Safeguard policy Statement 2009 and has been approved by MoE. The TKTLP is divided into two sections: i) Khimti-Barhabise section and ii) Barhabise-Kathmandu section.

Some changes has been occurred in the ETESIP project mainly due to shifting of three substations under the Power Transmission and Distribution Efficiency Enhancement Project (PTDEEP) from ETESIP. The scope of acquisition, compensation and other associated activities of the mentioned three substation components have also been transferred under the PTDEEP. The shifted substations are: i) Barhabise SS, Sindhupalchowk, ii) Lapsipedi SS, Kathmandu and iii) Changunarayan SS, Bhaktapur. The contract has been awarded and the project is in its initial phase of construction.

1.2 Project Components and Physical Progress

As stated above, there are two major sections in TKTLP. The TL of Khimti-Barhabise section which starts from substation at Phulasi, Ramechhap and ends in substation at Barhabise, Sindhupalchowk whereas the next section starts from substation at Barhabise, Sindhupalchowk and ends in substation at Changunarayan, Bhaktapur with the total length of 42.638 km and 56.722 km respectively (*source: IEE report*). Besides that the report also covers the status of the above mentioned three substations under PTDEEP. The description of the project components and their overall progress status has been summarized below:

Table 1 Physical Progress of the Project Activities

SN	Name of the Project	Project Details	Progress Status
1.	TKTLP/ Tamakoshi – Kathmandu 220/400 kV Transmission Line Project (ETESIP)		
a.	Khimti Barhabise section	Construction of double circuit 220/400 kV TL from Khimti, Ramechhap to Barhabise, Sindhupalchowk	i. Initial contract awarded on September 26 th 2016 cancelled and the selection of new contractor has been done. The agreement will be effective very soon. ii. Route Alignment finalized

SN	Name of the Project	Project Details	Progress Status
			iii. Construction has not been started
b.	Barhabise – Kathmandu section	Construction of double circuit 220/400 kV TL from Barhabise, Sindhupalchowk to Changunarayan, Bhaktapur	i. Contract awarded on June 13th 2017 ii. Check survey completed iii. Enumeration of trees to be cut completed in Sindhupalchowk District and has been initiated in Kavrepalanchowk, Kathmandu and Bhaktapur District Tower Footing (Angle Points) • At Sindhupalchowk District, altogether 10 tower foundation work has been completed till this reporting period which are as follows: AP 31/0, AP 32/0, AP 33/0, AP 33/1, AP 35/0, AP 35/1, AP 35/2, AP 37/0, AP 37A/0 & AP 39/0 • Likewise, foundation work of 5 towers are in progress as follows: ➤ 50% progress in AP 25/0 ➤ 50% progress in AP 25/1 ➤ 25% progress in AP 28/0 ➤ 75% progress in AP 30/0 ➤ 75% progress in AP 31/1

(Source: Field visit, compensation disbursement data sheet, project document and consultation with project staffs)

1.3 Monitoring Requirements and Frequency of Submission

As per the ADB reporting guidelines, this Semi-Annual Social Safeguards Monitoring Report has been prepared and submitted by ESSD, NEA in compliance with ADB requirements. The report has been prepared by the review of documents, field verifications and consultations with relevant stakeholders and project staffs. It covers and evaluates the social safeguard activities conducted by Environment and Social Management Unit (ESMU) for the period of January - June, 2019.

1.4 Scope of Monitoring Report

The semi-annual report contains information on execution of the different project activities and on implementation of land acquisition, resettlement activities ensuring social safeguard provisions and compliance verification as applicable. The scope of the report is focused to the different project components with land acquisition and resettlement scope/impact as described in the table below:

Table 2 Sub-Project Components with Land Acquisition and Resettlement Impacts

SN	Sub-Project Components
1.	Power Transmission and Distribution Efficiency Enhancement Project (PTDEEP)
a.	Barhabise Substation: Construction of 160MVA, 220/132/11 kV SS
b.	Lapsipedi Substation: Construction of 220/132/11 kV GIS
c.	Changunarayan Substation: Construction of 132/11 kV GIS
2.	Electricity Transmission Expansion and Supply Improvement Project (ETESIP)
	Tamakoshi-Kathmandu 220/400 kV Transmission Line Project (TKTLP)
a.	Khimti – Barhabise TL section: Construction of 220/400 kV TL
b.	Barhabise – Kathmandu TL section
	Barhabise – Lapsipedi TL section: Construction of 220/400 kV TL
	Lapsipedi – Changunarayan TL section: Construction of 132 kV TL

(Source: Project document)

1.5 Reporting Period

The semi-annual social safeguards compliance monitoring report covers the duration from the month of January – June, 2019.

2. Changes in Project Scope and Adjusted Safeguard Measures

As explained above, some changes have occurred in the scope of ETESIP with the shifting of three substations to PTDEEP. However, the report has been prepared as per their approved project scope and includes the status of both the areas TL section and Substations. Also based on the collected and classified impact data, safeguard category has been classified in accordance to ADB SPS 2009 as follows:

a) **Category A:** If the proposed project is likely to have significant involuntary resettlement impacts to 200 or more persons will be physically displaced from home, 200 or more persons lose 10% or more of their productive or income generating assets or 200 or more persons experience a combination of both.

b) **Category B:** If the proposed subproject includes involuntary resettlement impacts that are not deemed significant.

c) **Category C:** The proposed subproject has no involuntary resettlement impact.

Based on the data of land acquisition and PAFs the construction of three substations under PTDEEP falls under **Category A** for involuntary resettlement and **Category B** for indigenous people. Similarly with regards to ETESIP social safeguard categorization, TKTLP was classified as **Category B**, during the processing phase. However, as land acquisition, compensation distribution for tower construction and restriction of land for maintaining RoW is yet to be geared up, the screening and categorization is still ongoing. Thus, the involuntary resettlement category can be changed at any time. Till this stage of reporting period the safeguard classification is likely to be eligible for **Category A** for involuntary resettlement and **Category B** for indigenous peoples.

3. Qualitative and Quantitative Data

The report contains both the qualitative and quantitative data related to social safeguard issues and implementation activities. The quantitative data are collected to measure the status and change of specific variables as affected persons, affected land, affected households & other assets, compensation distribution status, total structure loss, total crop loss and others. The qualitative data are collected to identify the issues and get a detailed information on implementation process. These data are collected from NEA/project official records and relevant stakeholders through consultations, meetings, discussion and dialogues with project staffs/officials, PAFs, local communities and others.

4. Monitoring Parameters/Indicators and Methods

The screening of resettlement category, classification, number and extent of impacts are the major parameters of monitoring. The important monitoring indicators include (i) type of acquisition impacts, (ii) extent of impacts, (iii) measures adopted to mitigate the impacts, (iv) implementation status of the mitigation measures, (v) consultation and dissemination, (vi) grievance redressal, (vii) compensation payment, (viii) deed transfer, (ix) resettlement and rehabilitation etc and comparative analysis of current situations.

Various tools are used for collecting data and information, identifying land acquisition, compensation disbursement and other social issues. The major tools include (i) observation, (ii) interviews, (iii) grievance redress mechanism, (iv) formal survey, (v) local consultative meetings and (v) participatory method used with locals, workers, official staffs and other relevant stakeholders.

5. Monitoring Results

5.1 Documentation and Approval

The RP of TKTLP, Khimti-Barhabise section and Barhabise-Kathmandu section has to be prepared and approved from NEA and ADB. The data collection, field survey for RP updating has been completed in Chautara Sangachokgadi Municipality, ward no- 8, Irkhu, ward no- 9, Kadambas, ward no- 13, Thulo Sirubari, and Indrawati ward no- 10, Bhotesipa under Barhabise-Kathmandu TL Section. The data collection and field survey was conducted from 4th of June 2019 to 9th of June 2019. The collected data are being tabulated, reviewed and analyzed and will be

finally presented in the RP document. The updated RP document of Barhabise-Kathmandu section will be submitted to ADB for approval July 30, 2019.

5.2 Safeguard Objectives

The safeguard objectives is to compensate all the PAFs having impact on their land and assets at the replacement cost, ensuring shifting, relocation assistances as well as rental cost required for rental accommodation due to impact on their structures. Along with that, the project also provides vulnerability assistance to vulnerable households (e.g. dalit HHs, indigenous people HHs, single women headed HHs, HHs having persons with disabilities, HHs having senior citizens etc). The RP has the provision of livelihood improvement, entrepreneurship development and skill development trainings to the vulnerable and significantly affected households.

5.2.1 Safeguard Implementation Progress

The Entitlement Matrix (EM) prepared during the feasibility phase has the provisions that need to be strictly followed during the project implementation process. The details are presented in the **Annex- 1**. Similarly, the status of compliance monitoring results in terms of involuntary resettlement and indigenous peoples safeguard measures are presented in **Annex- 2** and **Annex- 3** respectively.

5.2.2 Safeguard Compliance Monitoring Review Mission

The ETESIP review mission field monitoring visit was conducted on 12th & 13th June 2019. The visit was mainly focused on the monitoring of the ongoing construction activities and the **Major Issues Associated with Land Acquisition and Compensation Distribution**. The team involved in the visit was the ADB officials, Project officials, ESSD focal person, ESMU field staffs, Contractors along with their desk & field staffs and some PAFs who joined in the site. The team visited Barhabise SS, Tower foundation construction site in Irkhu (AP 25/0) and the Lapsipedi SS area. The team looked after the non-compliance status (tower foundation construction without distribution of compensation) of the project and request the project officials to follow the ADB SPS guidelines and project agreement documents. Also, they asked social safeguard expert to submit an assessment report on the major issues of Barhabise SS and TL section. The submitted assessment report is attached herein **Annex- 4**.

Similarly, environmental compliance field monitoring visit was conducted on 17th June 2019. The visit mainly focused on the monitoring of the environmental safeguard compliances and the team involved were the ADB officials, ESMU field staffs along with the Contractors desk & field staffs. The team visited tower foundation construction site in Thulo Sirubari (AP 33/0, AP 32/0, AP 32/1) and Barhabise SS. The team suggested the contractors to follow their EHS plan, provide PPEs to all the labors and maintain the first aid box well equipped. Also they suggested them to manage the spoils excavated so that the rain will not wash away.

5.3 Land Acquisition and Compensation

The land acquisition and compensation distribution is progressively going on. The compensation for the land has already been fixed for Barhabise SS, Lapsipedi SS and Changunarayan SS. The fund has also been allocated and more than 95% of disbursement has been completed till date.

Similarly, the detail survey for TKTLP, Barhabise-Kathmandu section has been completed. The route alignment for 400 kV TL has also been completed. There are 80 towers to be constructed in Barhabise Municipality (Former Barhabise VDC, ward no-1, 2, 3 & Ramche VDC, ward no- 3, 5, 6, 8), Balephi RM (former Mankha VDC, ward no- 1, 2, 6, 9 & Phulping Dada VDC, ward no- 4, 5, 6, 7, 8), Chautara Sangachokgadi Municipality (former Irkhu VDC, ward no- 2, 3, 5, 7; Kadambas VDC, ward no- 9 & Thulo Sirubari VDC, ward no- 3, 4, 5, 6) and Indrawati RM (former Bhotesipa VDC, ward no- 8, 9), out of which the land required for 76 towers has to be permanently acquired at this stage. Thus, the public notice for land acquisition of these areas has been published in Rajdhani Daily Newspaper on 6th November, 2018 (Kartik 20, 2075). Among these

76 towers 30 towers (24 towers in private land & 6 towers in GoN land) falls in Chautara Sangachokgadi Municipality and 6 towers falls in Indrawati RM. The compensation Determination Committee has been formed in Sindhupalchowk District and it has already finalized the compensation rate for land of Chautara Sangachokgadi Municipality and Indrawati RM. The land parceling, plotting, ownership transfer and compensation disbursement is currently undergoing. The details of the proposed land, actual acquired land till this period and ownership transfer are presented in the table below.

Table 3 Details of Land Acquisition

SN	Project Component	Land Required (ha)	Land Acquired (ha)	Ownership transfer
1.	TKTLP/ Tamakoshi-Kathmandu 220/400 kV Transmission Line Project (ETESIP)			
a.	Khimti- Barhabise section			
b.	Barhabise- Kathmandu section for Tower foundation			
	Indrawati RM, ward no- 10	0.96 [18-13-3-2 (6 towers)]	0.25 [4-14-3-1]	GoN approval, Land parceling, ownership transfer- process ongoing
	Chautara Sangachokgadi Municipality, ward no- 8, 9, 13	30 towers (24 in private land & 6 in GoN land)	3.09 [60-10-2-2 (24 towers)]	GoN approval, Land parceling, ownership transfer- process ongoing
	Sub-total	-	3.34	
	Total	-	20.84	

*At Lapsipedi substation there are few households yet to have ownership transferred from Birta land to private land

(Source: RP, Land acquisition public notice, compensation distribution project data sheet)

5.3.1 Compensation for Acquired Land

A total number of 248 PAFs have been affected due to land acquisition for the construction of SS in Barhabise, Lapsipedi, Changunarayan and the tower foundation in Sindhupalchowk district. The compensation has been fixed and almost 95 % has been distributed for the substations. Likewise, the compensation rate has been fixed for tower foundation however land parceling, area determination and ownership transferring is on process for compensation disbursement in Indrawati- 10, Chautara Sangachokgadi Municipality- 8, 9 & 13.

Table 4 Compensation Distribution Status

SN	Project Component	PAFs	Acquired Land (ha)	Compensation Received PAFs	Compensation Target (NRs)	Compensation Paid (NRs)	Compensation Remained (NRs)
1.	TKTLP (ETESIP)						
a.	Khimti- Barhabise section						
	Barhabise- Kathmandu section						
	Indrawati RM- 10	12	0.25				
b.	Chautara Sangachokgadi Municipality- 8, 9 & 13	102	3.09				
				GoN approval, Land parceling, ownership transfer and compensation disbursement- process ongoing			

(Source: Field verification, Land acquisition and compensation distribution project data sheet)

5.3.2 Compensation for Structure Loss

The project has also compensated 13 affected structures in total till this reporting period. The compensation was distributed along with the compensation distribution of the acquired land.

Table 5 Compensation Distribution for Structure Loss

SN	Type of structures	No.	Estimated compensation (NRs)	Compensation paid (NRs)
Barhabise Sub-station				
1.	Kachhi ghar	5	3,000,008.00	Paid. [The compensation was included in the same package (i.e. compensation for acquired land)]
2.	Semi pakki ghar	2		
3.	Pakki ghar	1		
4.	Cowshed	4		
	Total	12	3,000,008.00	
Changunarayan Sub-station				
1.	Temporary ghar/shed	1	120,000.00	95,590.24
	Grand Total	13	3,12,008.00	95,590.24

(Source: Land acquisition and compensation distribution project data sheet)

5.3.3 Compensation for Trees/Plants

No progress has been documented in till this reporting period.

5.3.4 Major Issues in Land Acquisition and Compensation Distribution

Although NEA has tried to utilize government land and land owned by NEA to minimize the acquisition of private land, as per the objective of ADB SPS, it is not feasible across the whole TL alignment. Thus, private land has to be acquired, when and wherever is needed. During this process of acquisition of land for TL, there arises many problems. Most of the time people are not willing to give their land and in some areas people are not satisfied with the compensation rate being provided. The major issues associated are as follows:

Table 6 Major Issues Associated with Land Acquisition

SN	Issues	Action taken and Status	Remarks
1.	Unwillingness to provide land in Barhabise Substation- SS need to acquire 2-0-0-0 Ropani (0.10 ha) of Mr. Nain Bd Poudel but he is requesting project either to acquire the whole plot (7-0-0-0 Ropani i.e. 0.35 ha) or remove the substation from his land and transfer the ownership back to him.	The project is coordinating with the person to address the issue.	
2.	Ms. Goma Poudel- Single woman, is requesting to provide the access road through SS area to her land/house.	The project is coordinating with the relevant person to address the issue.	
3.	Unwillingness to provide land for tower foundation- Few HHs in Balephi RM ward no- 7 are not willing to provide land for tower foundation and are also requesting to change the TL route alignment. It's because of lack of awareness they are afraid of high voltage transmission line.	The project has coordinated with the relevant stakeholders, explained the risk, hazard and benefits of the project and the PAFs are willing to provide the land but are demanding for compensation first and the employment during the construction.	However, project has agreed to provide them the employment as per their skill set but the PAFs are bargaining for the overall sub-contract to the construction activities to be held within their area.
4.	Unwillingness to provide land- HHs from Kuntabesi are not willing to allow TL to pass through their village and are requesting to change the alignment and TL route	The project is coordinating with the relevant group to address the issue.	
5.	PAFs are demanding to disclose/put public notice regarding the compensation rate and their actual compensation fund based on the exact area of their acquired land, before starting any physical work.	PMO is in the process to address the issue and is in the process of publishing the compensation disbursement rate and notice.	
6.	Almost 32-37 Ropani (around 2 ha) of land yet to have ownership transferred from Birta to private land in Lapsipedi.	In support of locally elected leaders, locals/PAFs are coordinating with the related departments and ministries for the ownership transfer. Once the ownership transfer completes the PAFs will transfer it to the Project.	As per the request from PAFs, the project is also writing a letter to the respective department to support the PAFs in ownership transfer process, as provided by the rules & regulations.
7.	Major issues seems to be the access road for tower foundation construction	Negotiation is going on.	Although the contractor is signing to restore the land used and providing compensation, PAFs are not satisfied with what they are receiving as crop loss/tree loss/land use compensation and are demanding at the extremely high amount, irrespective of

SN	Issues	Action taken and Status	Remarks
			whatever the basic calculation guides are.

(Source: Field verification, Project staffs)

5.3.5 Livelihood Restoration Program

ADB SPS, 2009 aims to enhance or at least restore the livelihoods of all the displaced persons in real terms, relative to pre-project levels and to improve the living standard of the displaced poor and vulnerable groups. The RP has been prepared for substations and is in the process of updating for TL section. The updated RP for TL section approved by NEA and ADB, will provide the exact details of affected HHs, family size, IPs and vulnerable people. Once the data is obtained ESSD will initiate the livelihood enhancement, skill development trainings for the needed/affected persons.

5.3.6 Ensuring IPs Identity, Human Rights, Livelihood and Cultural Uniqueness

The acquisition of land for substations and TL sections will have impact to vulnerable households (dalit HHs, single women headed HHs, HHs having persons with disabilities, HHs having senior citizens) including indigenous people. The actual number will be identified only after the completion of processing of land acquisition and maintaining RoW for the TL. Till this reporting period there are 150 indigenous peoples household affected by the project activities. The details are presented in the table below:

Table 7 Status of Project Affected Households

SN	Project Component	Land Acquired (ha)	IP HHs	Total Affected HHs	Total Affected Persons	Remarks
1.	TKTLP/ Tamakoshi-Kathmandu 220/400 kV Transmission Line Project (ETESIP)					
a.	Khimti – Barhabise TL section					(*Note: Since the data is based on Land acquisition public notice published by NEA, the actual number might change after the detail field survey conducted for updating RP)
	The work has not begun		0	0	0	
Sub-total (a)			0	0	0	
b.	Barhabise – Kathmandu TL section					
	Indrawati RM, ward no- 10	0.25	10	12	** number of total affected person will be calculated only after the detailed survey/RP update	
	Chautara Sangachokgadi M, ward no- 8, Irkhu	3.09	46	51		
	Chautara Sangachokgadi M, ward no- 9, Kadambas		1	1		
	Chautara Sangachokgadi M, ward no- 13, Thulo Sirubari		31	50		
Sub-total (b)		3.34	88	114		
Total (a+ b)		3.34	88	114		
Grand Total (1+ 2)		20.84	150	248		

(Source: RP, Land acquisition public notice)

5.3.7 Grievance Redressal Mechanisms

The provision for Grievance Redress Committee in Land Acquisition Act 1977 and the approved Resettlement Plan of the project has facilitate to coordinate with district level stakeholders in formation of the committee. However the establishment of GRC for all the affected RMs and Municipalities are in the process of formation. In TKTLP 10 GRC formation letters have been dispatched and 3 GRCs have been formed till this reporting period. The details are presented in the table below and the minutes are presented in the **Annex- 5**.

Table 8 GRC Formation Details

SN	Location & Date	Total Participant no.			Committee member no.			Remarks
		Male	Female	Total	Male	Female	Total	
1.	Chautara Sangachokgadi Municipality- 13, Thulo Sirubari (2019/5/14)	19	3	22	8	1	9	

2.	Chautara Sangachokgadi Municipality- 8, Irkhu (2019/5/17)	15	1	16	9	0	9	
3.	Indrawati RM- 10, Bhotesipa (2019/5/29)	13	4	17	8	1	9	
4.	Barhabise Municipality							Letter submitted, waiting for time schedule
5.	Balephi RM- 7							
6.	Balephi RM- 8							
7.	Chautara Sangachokgadi Municipality- 9, Kadambas							
8.	Shankarapur municipality- 5, Palubari							
9.	Changunarayan Municipality- 4, Changu							
10.	Changunarayan Municipality- 6, Telkot							

Despite this delayed information, the PAFs and relevant stakeholders are contacting the project officials, ESMU field staffs, project office and the district level line agencies and their written as well as verbal grievances are being heard and recorded by project staffs and line agencies officials. Some of the major grievances recorded are as follows and the letters are presented in **Annex- 6**.

Table 9 Underlying Issues and Grievances

SN	Location	Recorded by / Issue Type	Issue Description	Status
1.	AP 37, AP 38, AP 39	PAFs / Written (2019/03/02) / Support for irrigation pipes	Request for Irrigation water pump and PPR pipe at Indrawati RM- 10	The requested materials has been provided to ward office (2019/04/02) and the construction is currently undergoing.
2.	AP 28	PAFs / Written (2019/03/14) / Support for irrigation pipes	Request for Irrigation pipe at Irkhu	SOLVED [Pipe has been provided to PAFs in presence of representatives from ward office]
3.	AP 28	PAFs / Written (2019/04/23) / Support for irrigation pipes	Request for 16 socket and 4 elbow to join available/supported pipe, Irkhu	SOLVED
4.	TL –Irkhu section	PAFs / Written (2019/04/04)	Request for gabion wall construction in school and road maintenance	Design, cost estimate survey completed & ESSD has open the bidding process where the enough number of bidders were not present. Hence, ESSD going through re-bidding process.
5.	TL –Irkhu section	PAFs / Written (2019/04/04)	Request for construction of temple and construction of stairs to temple	Design, cost estimate survey completed & ESSD has open the bidding process where the enough number of bidders were not present. Hence, ESSD going through re-bidding process
6.	TL –Thulo Sirubari section	PAFs / Written (2019/05/14)	Request for additional support projects	Information has been shared with the Project Office

(Source: Field verification, project officials, project office)

6. Public Consultation and Information Disclosure

The NEA through its relevant project office maintains records on disclosures regarding the environmental and social activities. Each subproject submits the report to PMD and relevant divisions in NEA. The PMD then prepares and updates the semiannual report based on monthly reports, field observations and consultations which is submitted to ADB and the finalized report is uploaded in ADB website for public view.

The regular consultation with the local peoples and relevant stakeholders is conducted whenever needed. Information regarding project activities is shared with them and any questions/queries is answered. While implementing the RP, IR activities a meaningful consultation, group discussions programs is carried out with the PAFs. The details of the consultative meetings held till this reporting period are presented below and the minutes are presented in the **Annex- 7**.

Table 10 Local Consultative Meeting Details

SN	Location and Date	Major Issues in Discussion	Participant			Remarks
			Male	Female	Total	
1.	Balephi RM ward no.- 7 (2019/04/02)	<ul style="list-style-type: none"> Dissemination of project information Public support for smooth running of the project Request for support in land acquisition 	10	0	10	PAFs assured to help for the successful completion of the project that falls under National Prioritization Project.
2.	Balephi RM ward no.- 8 (2019/04/03)	<ul style="list-style-type: none"> Dissemination of project information Public support for smooth running of the project Request for support in land acquisition Safety, hazard, risk and benefits of the project 	15	3	18	PAFs demanded that the compensation with good rates should be distributed before starting physical work of the project.
3.	AP 15 & AP 17, Balephi RM-7 (2019/05/17)	<ul style="list-style-type: none"> Request for support to start the construction of tower foundation 	6	0	6	PAFs asked to publish the notice along with the compensation details before starting the work.
4.	AP 3, AP 3A, AP 4, AP 5 & AP 5A, Barhabise (2019/05/21)	<ul style="list-style-type: none"> Rerouting of the towers/AP Sharing of those information with the public 	7	4	11	Public shows lack of interest in rerouting of towers and were not happy about constructing towers in their land
5.	Office of Shankarapur Municipality (2019/06/16)	<ul style="list-style-type: none"> Financial support from the project for their requested sub-projects 	11	1	12	

(Source: Field verification)

7. Implementation Status of Corporate Social Responsibility (CSR)

As a corporate responsibility NEA has allocated some funds for the betterment of the local people in the Project affected areas. These funds are distributed focused on educational support program, drinking water supply, infrastructure and service facilities and other additional support allowances for vulnerable communities. The details of CSR activities conducted till this reporting period are presented in the table below and other supporting documents are presented in the **Annex- 8**.

Table 11 List of CSR Activities and its Details

SN	CSR activities	Location	Current status	Remarks
1.	Supply, Delivery, Installation, Testing and Commissioning of Irrigation Water Pump and PPR Pipe	Indrawati RM- 10, Sindhupalchowk	Construction under process	
2.	Supply of Irrigation water PPR pipe	AP 28/0, Irkhu	Provided	
3.	Supply of sockets and elbow	AP 28/0, Irkhu	Provided	
4.	Gabion wall construction for the support of school playground and road maintenance	Setidevi Aadharbhut School, Irkhu	Design, cost estimate survey completed & ESSD has open the bidding process	
5.	Construction of stairs and temple	Setidevi Mandir, Dandagaun, Irkhu	Design, cost estimate survey completed & ESSD has open the bidding process	
6.	Supply of educational/reference materials	Namuna Sunkhani AAdharbhut School, Barhabise	Process for purchasing is undergoing	

SN	CSR activities	Location	Current status	Remarks
7.	Construction of Pratikshyala, Kriyaputri Bhawan Restoration and Reconstruction of Bhimsen Temple	Barhabise	Design, cost estimate survey completed & ESSD has open the bidding process	

(Source: Project Office, ESSD, Field visit)

8. Gaps and Corrective Action Plan for Mitigation

The Environmental and Social Monitoring Unit (ESMU) under ESSD, NEA has been set up in the field for regular monitoring and proper implementation of safeguard activities and mitigation measures. The team also identifies gaps and recommend the corrective action plan of mitigation in its section. The following corrective actions are required in order to improve the monitoring activities.

Table 12 Gaps and Corrective Plan of Action

SN	Issues	Corrective actions	Responsibility	Remarks
1.	Orientation and Training	Provide orientation and practical training, information sharing about project, reporting format and guidelines to the field based staffs/consultants before mobilizing them in the field	NEA/ESSD	
2.	Information sharing	Conduct information sharing sessions regularly/once every month	Project Office/ESSD	Helps to share experiences/obstacles/ gathered information and other short comings within the team
3.	Skill development training	Provide necessary skill development training	NEA/ESSD	
4.	Safeguard desk & strengthening empowerment	Regular coordination with contractors, project office, ESMU, ESSD in project activities, cadastral survey, & other issues in construction activities	ESMU/ Contractor/ Project Office/ESSD	
5.	Obstruction in tower foundation work	Provide compensation rate/ actual compensation amount for the respective PAFs in the respective section before commencement of tower foundation construction	Project office/ESMU	
6.	Non-compliance status in Land acquisition and Compensation disbursement	Provide compensation to the PAFs before the commencement of construction works	Project office	Suggested by ADB mission, however NEA is in process towards it and the land parceling and ownership transfer is taking more time
7.	Newly constructed houses an obstruction in TL route alignment	Provide information about the TL route alignment to the public and explain them that the project will not be liable to provide them the compensation of the houses build in the TL alignment, after the cadastral survey & information flow of the TL route alignment has been shared/publicly announced	Project Office	
8.	Quantification of spoils generated	Quantify the construction activities in support of contractors & their field staffs	ESMU	Helps to provide actual data on spoils excavated, refilled, & management

9. Recommendations

The monitoring of social safeguard activities and implementation will be continued throughout the project implementation period. The following recommendations are suggested for the monitoring adjustments, activities implementation and timely project completion.

- Provide information regarding compensation rate/actual compensation amount for the acquired land to PAFs before mobilizing contractor for tower foundation construction

- Prepare valuation amount/rate for private tree loss based upon their species, height and basal diameter, so that when contractor move to the field he/she can answer PAFs with factual information

10. Institutional Arrangement for Monitoring

The Project Management Directorate (PMD) office is responsible for the overall conduction and implementation of all the ADB funded projects. Inside PMD there will be separate unit for each projects which are headed by the respective Project Manager (PM) and the project is coordinated, conducted and implemented by his team under his supervision.

Furthermore, in close coordination and cooperation with PMD, Environment and Social Service Department (ESSD) will handled the environmental and social safeguard mitigation and compliance monitoring from its Environmental and Social Monitoring Unit (ESMU) established in each section of the TL. The ESMU comprises of one environment specialist and one socio-development specialist, whose main responsibility is to monitor the environment and social safeguard activities being implemented in the field during project implementation phase.

Likewise there will be a separate Compensation Determination Committee (CDC) formed in initiation of PMD/PM in each district. The CDC is chaired by the respective Chief District Officer (CDO) and members from District Level relevant Government Line agencies in each district. The main responsibility of the CDC is to determine the compensation rate for the land to be acquired for the project activities. It is also responsible for solving the issues/grievances related to land acquisition and compensation.

11. Proposed Major Item of Focus for Next Month

The next month report will be focused in completing the following activities:

Table 13 Proposed Major Item of Focus for Next Month

SN	Location	Activities
1.	Barhabise – Kathmandu TL section	<ul style="list-style-type: none"> • Field visit to different sites where construction is currently undergoing • Social safeguard compliance monitoring & Local consultation/ meetings • Follow-up & monitoring of CSR activities • Follow-up & Formation of GRC in the areas where the letter has already been dispatched (Shankarapur Municipality, ward no-5, Changunarayan Municipality, ward no-4 & 6, Balephi RM, ward no- 7 & 8, Chautara Sangachokgadi Municipality, ward no- 9, Kadambas)

Annexes

Annex- 1 Entitlement Matrix

SN	Nature of Loss	Entitlements	Current Status	Action Taken By	Remarks
1.	Permanent acquisition of agricultural/ residential/ commercial and other private lands by landowners	<ul style="list-style-type: none"> • Cash compensation at replacement cost based on current market price • Provision of land for land compensation will be made for those PAFs having complete loss of land in accordance to the prevailing act if land is available 	Partially Complied with:	NEA / CDC	Compensation disbursement is progressively going on for acquired land and for other land to be acquired land parceling, ownership transfer, compensation fixation is under process.
2.	Land restricted to use except for cultivation along the RoW of TL	<ul style="list-style-type: none"> • One time cash compensation for the land restricted to maintain RoW of the TL, except to use for agricultural purpose 	-	NEA / CDC	The work has not begun
3.	Land temporarily acquired by the contractor during the implementation/construction phase	<ul style="list-style-type: none"> • Contract will be signed between PAFs and contractor for temporary use/acquisition • Rental rate/compensation for crop/agricultural loss will be provided as per the valuation on national criteria • Land will be restored to its original state or to be compensated at replacement cost 	Complied with:	Contractor	NEA to facilitate during the process
4.	Loss of residential/ commercial and other structures by titleholders	<ul style="list-style-type: none"> • Cash compensation for the loss of the built-up structures at full replacement cost based on the current market price • PAFs allowed to take/reuse their salvageable materials • Provided one time shifting allowance 	Complied with:	NEA / CDC	
5.	Loss of residential/ commercial structures by squatters	<ul style="list-style-type: none"> • Cash compensation for the loss of built-up structures at full replacement cost • PAFs allowed to take/reuse their salvageable materials • Provided one time shifting allowance 	Complied with:	NEA / CDC	
6.	Loss of residential/ commercial structures by encroachers	<ul style="list-style-type: none"> • Cash compensation for non-land assets at replacement cost • Owner will be notified and allowed to take/reuse their salvageable materials 	Complied with:	NEA-PMD / CDC	
7.	Loss of fruit and trees on permanently acquired land	<ul style="list-style-type: none"> • One time cash compensation for the loss of fruit trees for average fruit production for next productive years computed at current market value • One time cash compensation for loss of wood trees at current market value (timber of firewood, as the case may be) 	Complied with:	CDC / NEA / Contractor	In coordination and consultation with District Forest Office and District Agricultural Office

SN	Nature of Loss	Entitlements	Current Status	Action Taken By	Remarks
8.	Loss of agricultural crops, fruits and wood trees	<ul style="list-style-type: none"> • One time cash compensation for the temporary loss of agricultural crops along the corridor of RoW due to stringing of TL at current market price based on average production of the affected area • One month advance notice to harvest crops, if required 	-	CDC / NEA / Contractor	In coordination and consultation with District Forest Office and District Agricultural Office (However the work has not begun)
9.	Loss of cultural & community structures/ facilities/ resources	<ul style="list-style-type: none"> • Complete rehabilitation/ restoration by the project or cash compensation for restoration/ reestablishment of the affected cultural/ community structures and installations, to the recognized patron/ custodian 	Complied with:	NEA / CDC / Local community	
10.	Loss of income and livelihood	<ul style="list-style-type: none"> • Assistance for lost income based on three months minimum wage rates • Additional compensation for the vulnerable HHs • Consideration for project employment 	Complied with:	NEA-PMD / CDC	
11.	Loss of Government Property/Land	<ul style="list-style-type: none"> • Lump sum compensation as per government rules 	Complied with:	NEA / Relevant Department	
12.	Impact on vulnerable PAFs	<ul style="list-style-type: none"> • Additional assistance based on three months of minimum wage • Will be given priority in project construction employment 	Complied with:	NEA / Contractor	
13.	Other impacts not identified	<ul style="list-style-type: none"> • Compensation and assistance 	Complied with:	NEA-PMD / CDC / Contractor	Unforeseen impacts will be documented and mitigated based on the principles agreed upon in the resettlement framework

Annex- 2 Compliance Monitoring Results in terms of Involuntary Resettlement Safeguards

Resettlement: The Borrower/Client, shall ensure that:				
SN	Monitoring Aspects	Indicators	Current Status	Remarks
1.	Delivery of Entitlements	<ul style="list-style-type: none"> Entitlements disbursed, compared with no. and category of losses set out in the Entitlement matrix. Identification of the displaced persons losing land temporarily, e.g. through soil disposal, borrow pits, contractors' camps, been included Restoration of social infrastructure and services. Progress on income and livelihood restoration activities being implemented as set out in the income restoration plan, for example, utilizing replacement land, commencement of production, the no. of the displaced persons trained in employment with jobs, Micro-credit disbursed, no. of income-generating activities assisted. 	Partially Complied with:	Compensation disbursement has been processed whereas other activities will be process after the approval/updating of RP and actual data collected
2.	Consultation and Grievances	<ul style="list-style-type: none"> Consultations organized as scheduled including meetings, groups, and community activities. Knowledge of entitlements by the displaced persons. Use of the grievance redresses mechanism by the displaced persons. Information on the resolution of the grievances. Information on the implementation of the social preparation phase Implementation of special measures for Indigenous Peoples 	Partially Complied with:	Since the project is in initial phase of implementation, no progress has been recorded so far
3.	Communication and Participation	<ul style="list-style-type: none"> Percentage of women out of total participants. No. of meetings exclusively with women. No. of meetings exclusively with vulnerable groups. No. of meetings at new sites. No. of meetings between hosts and the displaced persons. Level of participation in meetings (of women, men, and vulnerable groups). Level of information communicated—adequate or inadequate. Information disclosure. Translation of information disclosure in the local languages 	Partially Complied with:	Since the project is in initial phase of implementation, indicators are compiled as per the available data and resources
4.	Budget and Time Frame	<ul style="list-style-type: none"> Land acquisition and resettlement staff appointed and mobilized on schedule for the field and office work. Capacity building and training activities completed on schedule. Achieving resettlement implementation activities against the agreed implementation plan. Funds allocation for resettlement to resettlement agencies on time. Receipt of scheduled funds by resettlement offices. Funds disbursement according to the resettlement plan. Social preparation phase as per schedule. Land acquisition and occupation in time for implementation. 	-	Since the project is in initial phase of implementation, no progress has been recorded so far
5.	Livelihood and Income	<ul style="list-style-type: none"> No. of displaced persons under the rehabilitation programs (women, men, and vulnerable groups). No. of displaced persons who received vocational training (women, men, and vulnerable groups). 	-	Since the project is in initial phase of implementation, no

		<ul style="list-style-type: none"> • Types of training and no. of participants in each. • No. and percentage of displaced persons covered under livelihood programs (women, men, and vulnerable groups). • No. of displaced persons who have restored their income and livelihood patterns (women, men, and vulnerable groups). • No. of new employment activities. • Extent of participation in rehabilitation programs. • Extent of participation in vocational training programs. • Degree of satisfaction with support received for livelihood programs. • Percentage of successful enterprises breaking even (women, men, and vulnerable groups). • Percentage of displaced persons who improved their income (women, men, and vulnerable groups) • Percentage of displaced persons who improved their standard of living (women, men, and vulnerable groups) • No. of displaced persons with replacement agriculture land (women, men, and vulnerable groups) • Quantity of land owned/contracted by displaced persons (women, men and vulnerable groups) No. of households with agricultural equipment 		progress has been recorded so far
6.	Benefit Monitoring	<ul style="list-style-type: none"> • Noticeable changes in patterns of occupation, production, and resource use compared to the pre-project situation. • Noticeable changes in income and expenditure patterns compared to the pre-project situation. • Changes in cost of living compared to the pre-project situation. • Changes in key social and cultural parameters relating to living standards. • Changes occurred for vulnerable groups. • Benefiting from the project by the displaced persons. 	-	Since the project is in initial phase of implementation, no progress has been recorded so far

Annex- 3 Monitoring Results in terms of Indigenous Peoples Safeguards

The Borrower/Client, shall ensure that:				
SN	Monitoring Aspects	Indicators	Current Status	Remarks
1.	Demographic Baseline	<ul style="list-style-type: none"> • The no. of affected Indigenous Peoples (IP) by category of impact, gender, age, habitat (village etc.), income, status and position • No. of households with handicapped, elderly or invalid members • No. of female headed households • No. of vulnerable households (poor, elderly) • No. of households by ethnic group • No. of births and deaths 	In process of compliance	Survey & Data collection has recently done for RP update.
2.	Consultation and participation	<ul style="list-style-type: none"> • No. of consultation and participation activities that occur- meetings, information dissemination, brochures; flyers, training • Percentage of IP women as participants; no. of meetings exclusively with IP women • Percentage of vulnerable IP groups represented / attending meetings; no. of meetings exclusively with vulnerable IP groups. • Languages used at meetings • Good faith negotiations- recording of process, participants, locations, correspondence • Broad community support- record of processes, participants, locations and agreement obtained • Consultation and participation progress against plan and budget 	-	Since the project is in initial phase of implementation, no progress has been recorded so far
3.	Mitigation Measures	<ul style="list-style-type: none"> • Progress of implementation of mitigation / beneficial measures against plan • No. of activities that occur/completed- such as construction, livelihood restoration, disbursements, training • Percentage progress against timelines and budget 	-	Since the project is in initial phase of implementation, no progress has been recorded so far
4.	Grievance Redress	<ul style="list-style-type: none"> • Total no. of people/groups using the grievance redress procedure. • No. of distinct people/groups. Any IP group with significantly more grievances? • How many times has a household submitted the same grievance? • No. of grievances resolved? • Length of time taken to be resolved? • Types of grievance categories and prevalence 	In the process of compliance	Since the project is in initial phase of implementation, indicators are compiled as per the available data and resources
5.	Implementation Problems	<ul style="list-style-type: none"> • Identified delays— (days, cost) due to personnel, capacity, insufficient funds, etc. • No. of times implementation schedule revised 	-	No issues/problems has been seen till this reporting period

Annex- 4 An Assessment Report submitted as requested by ADB ETESIP Review Mission

An Assessment Report prepared by Social Safeguard Officer on the Major Issues related to
TILIP during ADB ETESIP Review Mission

Under Tarakeshi-Kathmandu 220/40 KV Transmission Line Project being executed by NEA, some issues were observed by the joint ADB Mission and Environmental and Social Safeguard Field Officer of TILIP. Observations of field-level staff were requested to expedite the ADB field assignments for issues observed below.

These issues were observed during jointly and were importance of the field officers possible numbers of affected the communities.

Issue 1

Mr. Bishu B. Poudel was a report of land under the community. One of the most of report land has been acquired by the project for the transmission construction. Mr. Poudel states the project requires the whole land area (7 report), as means both the 2 report and also provide for the water side because want to his land area.

Recommendation/Action plan

- * As per the Land Acquisition Act/Regulation, to acquire lands for public purposes Nepal government has the legal right to acquire the required land, paying compensation to the landowner.
- * In addition, Safeguard Policy Statement (SPS) also has been described that if there are no adverse effects of the project throughout the project cycle, it would not be necessary to acquire land from the public if the project owner could avoid from the necessary area. Thus, the project doesn't need to acquire more than the requirement or requested by the owner unless decided under mutual understanding. From a legal point of view, if the project owner can get the only 2 reports to get the need, it should be fine.
- * Also, the report on water and public land areas noted, as the community was threatened by the project. But he showed the project by means of the need by the project owner required. As the legal government has the right to provide the community with the need to the project owner. However, the project was negotiating to provide the 2 report and was requesting to maintain the rest from the public which has to maintain regarding. Again later that only the transmission from the project was to be installed will not complete all the need will not achieve other benefits of the project of the need are willing to do which will the situation become considerable. Then in this situation, it would be better to provide the with an alternative source need that the project has proposed the below.

Issue 2

Mrs. Durga Poudel was a report of land near the line work to water point of the community. Before the construction of the installation, she had maintained from the way of installation in her land. Once the construction of installation was started water in her land has been blocked. Mr. says to the

project is, either the project provides access to a tractor able road to her land or the project acquire her total land. The ground reality justifies her urge.

Recommendation:

- As per the safeguard policy statement 2008, in case adverse effects to the landowner, the project needs to mitigate those types of issues through the project. Since she was having access to her land before the project, she should have ensured her with the access primarily. Otherwise, her urge to acquire the whole land remains valid.
- Alternatively, the project can acquire her whole land and can provide her with the compensatory/replacement land with the resettlement compensation.

Tower status:

The total tower pade from Barabhis to Lapalphedi TL section and Lapalphedi to Kathamandi TL section is 122 and 56 respectively, updated till this date. At present construction work is being carried out in 15 different locations.

However, the compensation for the tower pade has not been distributed in all the sections where the construction is under process at present. The public notice of the land acquisition for the land required for constructing tower pade in Indrawati RM ward no. -10, Bhotesiga (former Bhotesiga VDC -8 & 9), Chaurara Sengachokgadhi Municipality ward no. -04, Idhu (former Idhu VDC -2, 3, 4 & 7), ward no. -9, Kadambas, ward no. -13, Thulo Simbari (former Thulo Simbari VDC- 1, 4, 5 & 6), Balophi RM ward no. -4 (former Palsingdada VDC-3), ward no. -5 (former Palsingdada VDC- 6), ward no.-6 (former Manika VDC-5), ward no.-7 (former Manika VDC-6), ward no.-8 (former Manika VDC-1), and Barabhis municipality ward no.-9 (former Barabhis VDC-3, 5, 6 & 8), ward no.-9 (former Barabhis VDC-1) was published on 6th November, 2018 in Rajdhan Daily newspaper. Accordingly, the land acquisition process has proceeded. The Compensation Distribution Committee (CDC) chaired by the Chief District Officer (CDO) has finalized the compensation rate for Indrawati RM ward no. 10, Chaurara Sengachokgadhi Municipality ward no- 4, 9 & 13 and Balophi RM ward no- 7, which has permitted NEA to proceed further for the compensation distribution procedures in those areas. The land proceeding, ownership transfer has been almost completed in Indrawati RM ward no- 10 whereas it is under process in other areas where CDC has finalized the compensation rate (i.e. Chaurara Sengachokgadhi Municipality ward no.-4, Idhu, ward no.-9, Kadambas and ward no.-13, Thulo Simbari, and Balophi RM ward no.- 7). Despite the fact that NEA has transferred the compensation fund to District Administration Office for Indrawati RM ward no.- 10, none of the PAFs has been to or has provided their bank account details to DAO to receive the compensation. Also because of the transfer of previous account officer there created a shortage of human resources in DAO which is further extending time in the disbursement of those funds. This made Project Office, NEA to think an alternative option in the distribution of compensation fund and hence it is planning to distribute by their own human resources. Although the distribution might be done by NEA, itself, the allocated fund cannot be deposited in the respective PAFs bank account until the land proceeding and ownership transfer has been completed and the PAFs will provide all their details regarding the acquired land (ownership details, efficiency, and revenue/tax paid receipt), which is taking more time than

expected to distribution of land. Nevertheless, the construction is being carried out in these areas in mutual understanding with the P.A. & tower pad landowner.

Besides these, the major issue being observed in tower location is the construction of a temporary access road to the tower foundation/tower pad from the nearby access road. However, the contractor is providing the compensation for crop loss of 3 growing seasons and is agreeing to restore the used land as before by the end of the construction activities, the landowners are not happy with the compensation and are asking a huge amount. Negotiation is continuously going on with the owners and the work is done only in the area where the owner P.A. is giving the compensation of crop loss and are okay with the restoration of the land given by the contractor in the future. The details are present below:

Table 1 Status of the construction activities in Tower foundation

S.N.	Location	AP	Progress Status	Remarks
1.	Chandrapur-14, Chaudhara	370	4 g% completed	Foundation 100% completed
2.	Chandrapur-14, Chaudhara	370	4 g% completed	Foundation 100% completed
3.	Chandrapur-14, Chaudhara	370	4 g% completed	Foundation 100% completed
4.	Chandrapur-14, Chaudhara	370	4 g% completed	Foundation 100% completed
5.	Chandrapur-14, Chaudhara	370	4 g% completed	Foundation 100% completed
6.	Chandrapur-14, Chaudhara	370	4 g% completed	Foundation 100% completed
7.	Chandrapur-14, Chaudhara	370	4 g% completed	Foundation 100% completed
8.	Chandrapur-14, Chaudhara	370	4 g% completed	Foundation 100% completed
9.	Chandrapur-14, Chaudhara	370	4 g% completed	Foundation 100% completed
10.	Chandrapur-14, Chaudhara	370	4 g% completed	Foundation 100% completed
11.	Chandrapur-14, Chaudhara	370	4 g% completed	Foundation 100% completed
12.	Chandrapur-14, Chaudhara	370	4 g% completed	Foundation 100% completed
13.	Chandrapur-14, Chaudhara	370	4 g% completed	Foundation 100% completed
14.	Chandrapur-14, Chaudhara	370	4 g% completed	Foundation 100% completed
15.	Chandrapur-14, Chaudhara	370	4 g% completed	Foundation 100% completed

1. GRC formation, Chautara Sangachokgadi Municipality, ward no- 13, Thulo Sirubari (2019/05/14)

क्र.सं.	नाम व पद	प्रा.	नो.सं.	दस्तावेज
१	रत प्रसाद शर्मा	प्रधान	१४०१७७१५	१४०१७७१५
२	सोनीप्रास वैद	उप.प्र.	१४०४५५४०	१४०४५५४०
३	विष्णु प्रसाद	उप.प्र.	१४०५५५५५	१४०५५५५५
४	विष्णु प्रसाद	उप.प्र.	१४०५५५५५	१४०५५५५५
५	विष्णु प्रसाद	उप.प्र.	१४०५५५५५	१४०५५५५५
६	विष्णु प्रसाद	उप.प्र.	१४०५५५५५	१४०५५५५५
७	विष्णु प्रसाद	उप.प्र.	१४०५५५५५	१४०५५५५५
८	विष्णु प्रसाद	उप.प्र.	१४०५५५५५	१४०५५५५५
९	विष्णु प्रसाद	उप.प्र.	१४०५५५५५	१४०५५५५५
१०	विष्णु प्रसाद	उप.प्र.	१४०५५५५५	१४०५५५५५
११	विष्णु प्रसाद	उप.प्र.	१४०५५५५५	१४०५५५५५
१२	विष्णु प्रसाद	उप.प्र.	१४०५५५५५	१४०५५५५५
१३	विष्णु प्रसाद	उप.प्र.	१४०५५५५५	१४०५५५५५
१४	विष्णु प्रसाद	उप.प्र.	१४०५५५५५	१४०५५५५५
१५	विष्णु प्रसाद	उप.प्र.	१४०५५५५५	१४०५५५५५
१६	विष्णु प्रसाद	उप.प्र.	१४०५५५५५	१४०५५५५५
१७	विष्णु प्रसाद	उप.प्र.	१४०५५५५५	१४०५५५५५
१८	विष्णु प्रसाद	उप.प्र.	१४०५५५५५	१४०५५५५५
१९	विष्णु प्रसाद	उप.प्र.	१४०५५५५५	१४०५५५५५
२०	विष्णु प्रसाद	उप.प्र.	१४०५५५५५	१४०५५५५५

26) 2008 10/05/2008 78100 582146 100000
27) 2008 10/05/2008 78100 582146 100000
28) 2008 10/05/2008 78100 582146 100000
29) 2008 10/05/2008 78100 582146 100000
30) 2008 10/05/2008 78100 582146 100000

[illegible]

आम मीते २००६ साल जेष्ठ ६ जेबका तित गैयल अस्कार, तेषाल सिधुत प्राधिकरणको स्थापना ज्ञानिमा र समिसुली विकास बिकसो कमीसन्कोसामा स्थापनित नामाकोसी-काठमाडौँ ६४०/६०२ दि.बी. प्रसारण लाईन अगोवना विचारका क्रममा यस चौतारा समालोचनाडी कार्यालिका ईस्ट वार्ड नं. ८ मा प्रसारणलाई विस्तार जेतिसमा अग्रगत हो आधुनिक तथा पातायणीय अस् वस्तुगत स्मृतिगत तथा व्यवस्थापन र स्थापित प्रभावितहरूको धारो तथा गुणकोलाई निता तथा व्यवस्थापन उनी कार्यक्षम गुणकोलाईसत अस्कार समिति गठन गनिये। लखि खले गएको पदार्थका की निर्वाह र जेष्ठ अु की कार्यक्षमता नितावुसार अस् वस्तुगत उपायनिता लुप्त होल बसो निम्नका प्रसारण र मा हलफल तथा विनीय जडियो।

क्र.सं.	नामधारी	पद	मो. नं.	संसाधन
१.	विमल क. शर्मा	प्रशासक	९८४४४९३०९	मिशन
२.	काशीद. लामा	प्रशासक		
३.	प्रकाश. देवा	प्रशासक	८०७१००६६२	
४.	विमल क. शर्मा	प्रशासक	९८४४४९३०९	
५.	प्रकाश. देवा	प्रशासक	८०७१००६६२	
६.	विमल क. शर्मा	प्रशासक	९८४४४९३०९	
७.	प्रकाश. देवा	प्रशासक	८०७१००६६२	
८.	विमल क. शर्मा	प्रशासक	९८४४४९३०९	
९.	प्रकाश. देवा	प्रशासक	८०७१००६६२	
१०.	विमल क. शर्मा	प्रशासक	९८४४४९३०९	
११.	प्रकाश. देवा	प्रशासक	८०७१००६६२	
१२.	विमल क. शर्मा	प्रशासक	९८४४४९३०९	
१३.	प्रकाश. देवा	प्रशासक	८०७१००६६२	
१४.	विमल क. शर्मा	प्रशासक	९८४४४९३०९	
१५.	प्रकाश. देवा	प्रशासक	८०७१००६६२	

[illegible][illegible]

[illegible][illegible]

Annex- 6 Documentation of Recorded Grievances and its Addressal

चौतारा सांगाचोकगढी नगरपालिका
Chautara Sangachokgadhi Municipality
८ नं. वडा कार्यालय Office of Ward No.8
इरु खु सिन्धुपाल्चोक Irkhu Sindhupalchok
स्थापित ई.स. २०७३ ESTD:2073

सं.सं. ००८/०९
पत्रांक नं. ८८८/९
दिनांक २०७३/१३/११

विषय : सिफारिस गरिएको सम्बन्धमा

श्री नेपाल विद्युत प्राधिकरण
२२०/४०० के.भी. प्रसारण लाइन अर्बोजमा
झरिपारी, भक्तपुर

उपरोक्त सम्बन्धमा चौतारा सांगाचोकगढी न.पा. वडा नं. ८ ई.सं. मा २२०/४०० के.भी. प्रसारण लाइन अर्बोजमा विद्युत टावर निर्माण गरिएका हुन्। प्रभावित क्षेत्रमा रहेको श्री सुशीलेनी गाविस होडापाँउ सार्वजनिक ई.सं. ५ मा कान्तिपुर सार्ने सुसम्बन्धमा ध्यानि नगरी बाटो भर्षन तथा खान्ति गरी सार्वजनिक सार्वजनिक सिफारिसका साथ अनुरोध गरिन्छ।

सि.सं. ००८/०९
सि.सं. ००८/०९
सि.सं. ००८/०९

Request for support from PAFs, Irkhu

चौतारा सांगाचोकगढी नगरपालिका
Chautara Sangachokgadhi Municipality
८ नं. वडा कार्यालय Office of Ward No.8
इरु खु सिन्धुपाल्चोक Irkhu Sindhupalchok
स्थापित ई.स. २०७३ ESTD:2073

सं.सं. ००८/०९
पत्रांक नं. ८८८/९
दिनांक २०७३/१३/११


विषय : सिफारिस गरिएको सम्बन्धमा

श्री नेपाल विद्युत प्राधिकरण
२२०/४०० के.भी. प्रसारण लाइन अर्बोजमा
झरिपारी, भक्तपुर

उपरोक्त सम्बन्धमा चौतारा सांगाचोकगढी न.पा. वडा नं. ८ ई.सं. मा २२०/४०० के.भी. प्रसारण लाइन अर्बोजमा विद्युत टावर निर्माण गरिएका हुन्। प्रभावित क्षेत्रमा रहेको श्री सुशीलेनी गाविस होडापाँउ सार्वजनिक ई.सं. ५ मा कान्तिपुर सार्ने सुसम्बन्धमा ध्यानि नगरी बाटो भर्षन तथा खान्ति गरी सार्वजनिक सार्वजनिक सिफारिसका साथ अनुरोध गरिन्छ।

सि.सं. ००८/०९
सि.सं. ००८/०९
सि.सं. ००८/०९

Request for support from PAFs, Irkhu



Request for support from PAFs, Irkhu

चौतारा सांगाचोकगढी नगरपालिका
Chautara Sangachokgadhi Municipality
८ नं. वडा कार्यालय Office of Ward No.8
इरु खु सिन्धुपाल्चोक Irkhu Sindhupalchok
स्थापित ई.स. २०७३ ESTD:2073

सं.सं. ००८/०९
पत्रांक नं. ८८८/९
दिनांक २०७३/१३/११

विषय : सिफारिस गरिएको सम्बन्धमा

श्री नेपाल विद्युत प्राधिकरण
२२०/४०० के.भी. प्रसारण लाइन अर्बोजमा
झरिपारी, भक्तपुर



उपरोक्त सम्बन्धमा चौतारा सांगाचोकगढी न.पा. वडा नं. ८ ई.सं. मा २२०/४०० के.भी. प्रसारण लाइन अर्बोजमा विद्युत टावर निर्माण गरिएका हुन्। प्रभावित क्षेत्रमा रहेको श्री सुशीलेनी गाविस होडापाँउ सार्वजनिक ई.सं. ५ मा कान्तिपुर सार्ने सुसम्बन्धमा ध्यानि नगरी बाटो भर्षन तथा खान्ति गरी सार्वजनिक सार्वजनिक सिफारिसका साथ अनुरोध गरिन्छ।

सि.सं. ००८/०९
सि.सं. ००८/०९
सि.सं. ००८/०९


Request for support from PAFs, Irkhu

Addressing grievance, Irkhu

Addressing grievance, Irkhu

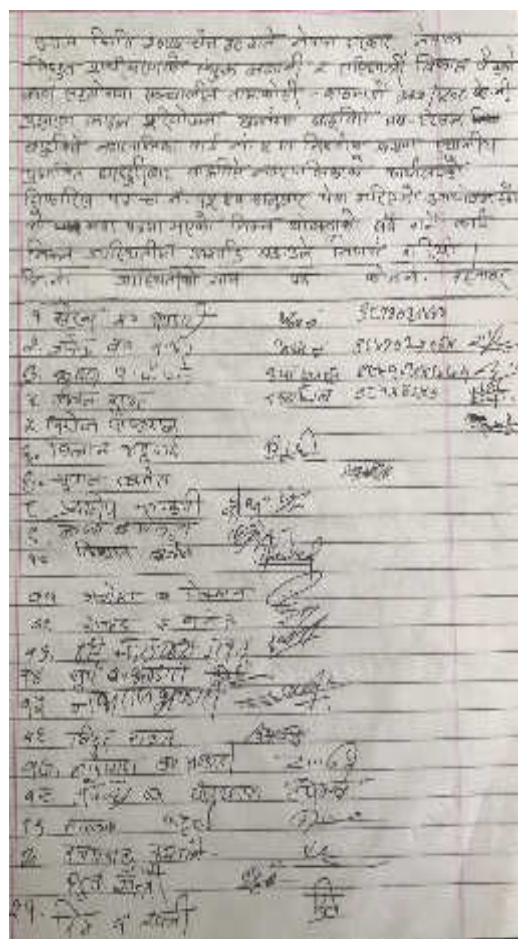

Grievance letter and its addressal document, Barhabise SS

 **चौतारा साँगाचोकगढी नगरपालिका**
CHAUTARA SANGACHOKGADHI MUNICIPALITY
 १३ नं. वडा कार्यालय Office of Ward No. 13
 ठूलोसिरुवारी, सिन्धुपाल्चोक Thulosirubari, Sindhupalchok
 स्थापना १०७३ ESTD: 2073 B.S.

पत्र संख्या (Letter No.): ०७५/०७५
 चलानी नं. (Ref No.): २६६

३ नं. प्रदेश नेपाल
 3 No. Province, Nepal
 मिति २०७६/०९/०२


विषय (Subject) : सिफारिस गरिएको सम्बन्धमा ।

श्री (To) नेपाल विद्युत प्राधिकरण
 तामाकोशी काठमाण्डौ, २२०-४०० के.भी./प्रसारण लाइन आयोजना
 खरिपाटी, भक्तपुर ।

उपरोक्त सम्बन्धमा यस नगरपालिका वडा नं. १३ अन्तर्गत संचालनमा रहेको यस नेपाल विद्युत प्राधिकरण, तामाकोशी-काठमाण्डौ, २२०-४०० के.भी./प्रसारण लाइन आयोजनाका प्रभावित क्षेत्रका स्थानियहरुको आवश्यकता मध्यनजर गरी यस आयोजनाको सामाजिक कार्य शिर्षक अन्तर्गत यस वडा भित्रका तपसिलका कार्यहरुमा निम्नानुसारका कार्य गरिदिनहुन अनुरोध छ ।

तपसिल

१. कार्कीछाप ठूलोपधेरा ट्याङ्गी निर्माण ।
२. नर्सिङडाँडा भुलभुले सडक स्तरोन्नती ।
३. सिंहदेवि मन्दिर निर्माण, हरै ।
४. नर्सिङडाँडा खानेपानी मुहानमा ट्याङ्गी निर्माण ।
५. बोजिनी खानेपानी Water pump खरिद ।


 २०७६/०९/०२
 रामप्रसाद गौतम
 वडा अध्यक्ष

Request for support from PAFs, Thulo Sirubari

शंखरापुर नगरपालिका

वडा कार्यालय
जहसुत शीवा, काठमाडौं
सुदूरपश्चिम, नेपाल

पत्र संख्या: ०७९/०७६
चलानी नं.: ९८६

फोन नं.:
मिति: २०७६/२/२३

विषय: सिफारिस सम्बन्धमा ।

श्री: लप्सेफेदी चौगुनारायण सव स्टेसन आयोजना ।

उपरोक्त सम्बन्धमा यस लप्सेफेदी चौगुनारायण सव स्टेसन आयोजनाको निर्माणाधीनको अवस्थाको बारेमा यस शंखरापुर नगरपालिका वडा नं. ३ तथा आयोजनासँग भएको पटक-पटकको छलफल र सहमतीको आधारमा तयार भएको दस्तावेज अनुसारका सम्झौताहरूको कुनै पनि शर्तहरू लागु नभएको अवस्था र हाल आएर यस वडा तारिदारको जम्जिर मुनि युगौं युगौंसम्म रहने र विधुतिय विकरणको सिकार हुने कुरा घाम जतिकै छल्लेङ्ग छ । तसर्थ: यस वडा कार्यालय सम्बन्धीत निकायसँग यो वडाको सर्वोद्देशि विकासको लागि निरन्तर रूपमा दिपेकलिन समयसम्म के कतिको हिसाबले वार्षिक रकम प्राप्त हुने हो यसको स्पष्ट जानकारीको पनि निश्चित खाका माग गर्न चाहन्छ ।

यस आयोजनासँग यस वडा भित्र नुनन्त संचालन गर्नुपर्ने कार्यक्रमको लागि अनुमानित बजेटको खाका यसै साथ पेश गरिएकोछ । आशा छ कि कार्यालयले तदारकताका साथ कार्य अगाडी बढाउनेछ ।

१. शंखरापुर न.पा. ३ मा खानेपानीको योजनाको लागि लागत र्टीमेट अनुरूपको रकम उपलब्ध हुनुपर्ने ।
२. कृष्णभवत मार्ग १० कि.मि. र लम्बाई १० मि. चौडाईको पक्की काकोपने राख्न लागत र्टीमेट बमोजिमको बजेट उपलब्ध हुनुपर्ने ।
३. गुम्जा निर्माणको लागि पछिल्लो चरणको लागि रु. १,७०,००,०००/- (एक करोड पचास लाख रुपैया) मात्र उपलब्ध हुनुपर्ने ।
४. कालिदह सिँचाईको लागि कालिदह ड्याम (Dam) र सिँचाई कुलाको लागि लागत र्टीमेट तयार गरी आवश्यक रकम उपलब्ध हुनुपर्ने ।
५. नारायणधाम मन्दिर निर्माणको लागि रु. २५,००,०००/- (पच्चिस लाख रुपैया मात्र) बजेट उपलब्ध हुनुपर्ने ।
६. स्वास्थ्य चौकी निर्माणको लागि रु. १,००,००,०००/- (एक करोड रुपैया मात्र) बजेट उपलब्ध हुनुपर्ने ।
७. वडा कार्यालय निर्माणको लागि रु. १,००,००,०००/- (एक करोड रुपैया मात्र) बजेट उपलब्ध हुनुपर्ने ।
८. कालिका शरण मा.वि. सर्वोद्देशि विकासको लागि रु. ३,००,००,०००/- (तीन करोड रुपैया मात्र) बजेट उपलब्ध हुनुपर्ने ।
९. शंखरापुर न.पा. ३ को पर्यटन प्रवर्द्धनको लागि रु. १,००,००,०००/- (एक करोड रुपैया मात्र) बजेट उपलब्ध हुनुपर्ने ।
१०. कृषि उत्पादन राम्रानको बजार प्रवर्द्धन एवं व्यवस्थापनको लागि रु. १,००,००,०००/- (एक करोड रुपैया मात्र) बजेट उपलब्ध हुनुपर्ने ।
११. शंखरापुर न.पा. ३ मा निर्माण हुन गइरहेको हिलेचौर ड्याम निर्माणको लागि डि.पि.आर. बमोजिमको रकम उपलब्ध हुनुपर्ने ।
१२. ट्रिपर मार्गको लागि डि.पि.आर. बमोजिमको केही भाग पक्की सडक निर्माणको बजेट उपलब्ध हुनुपर्ने ।

सन्त बहादुर वाइवा
सन्त बहादुर वाइवा
वडा अध्यक्ष

नेपाल विद्युत प्राधिकरण, लक्ष्मीफेदी तथा चाँगुनारायण सबस्टेशन निर्माण आयोजना बाट काठमाडौं जिल्लाको शंखरापुर नगरपालिका क्षेत्रमा निर्माण गरिने २२०/४००० के.भि. सबस्टेशन निर्माणका लागि आवश्यक पर्ने जग्गा प्राप्तिका लागि जग्गा प्राप्ती ऐन २०३४ बमोजिम प्रस्ताव अगाडी बढाउने समता रक्षणीय प्रभावित व्यक्तिहरूको उपस्थितीमा वडा अध्यक्ष श्री सन्त बहादुर बाहुवाको अध्यक्षता मिति २०७३/०१/१९ को बैठकको निर्णय सहित शंखरापुर नगरपालिका ३ नं. वडा कार्यालयको मिति २०७३/०१/१० को सिफारिस साथ प्राप्त भाग सम्बन्धमा निम्न बमोजिमको उपस्थितीमा तपसिल बमोजिमको निर्णय गरियो ।

मिति : २०७३/०१/२६

बैठक स्थान :

उपस्थिती

निर्वाहकार्यकारी निर्देशक श्री मंगोज शिलवाल, आयोजना व्यवस्थापन निर्देशनालय

मेयर श्री सुवर्ण श्रेष्ठ, शंखरापुर न.पा.

आयोजना प्रमुख श्री जुजुरत्न शान्ध, लक्ष्मीफेदी तथा चाँगुनारायण सबस्टेशन निर्माण आयोजना,

वडा अध्यक्ष श्री सन्त बहादुर बाहुवा, ३ नं. वडा, शंखरापुर न.पा.


समयमान नामा, संयोजक शान्तिशेखर प्रभावित समन्वय समिति,


सहायक प्रबन्धक श्री योगनाथ न्यौपाने, लक्ष्मीफेदी तथा चाँगुनारायण सबस्टेशन निर्माण आयोजना,

निर्णय

प्रभावित समन्वय समिति मार्फत प्राप्त निम्न भाग सम्बन्धमा

१) माग - अधिकरण गरिएका सबै जग्गाहरूको प्रति आना रु.३,००,००० को दरले मुआब्जा उपलब्ध गराउनु पर्ने । यस सम्बन्धमा निर्णय गर्ने अधिकार मुआब्जा निर्धारण समितिलाई मात्र भएकोले छलफल नभएको ।



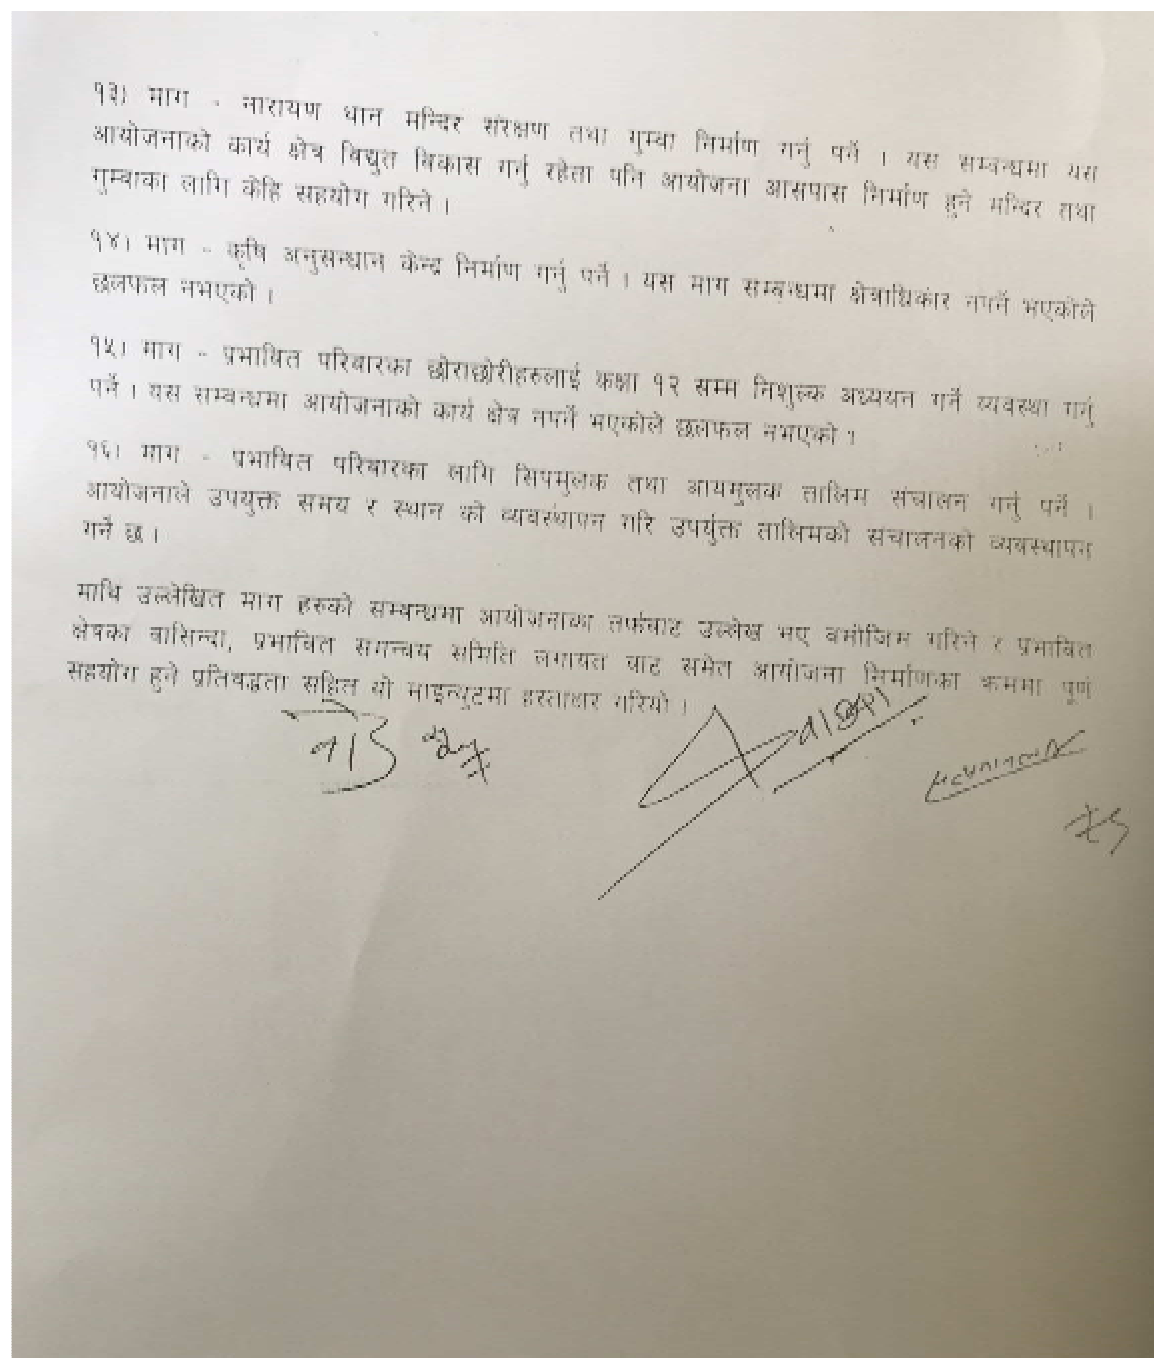

Request letter from PAFs of Lapsiphedhi SS

Annex- 7 Local Consultative Meeting Minutes

[illegible]

उत्पादन तथा निर्यात

१. प्रसारण लाईन आयोजनाको बारेमा उत्पादन विभाग सन्धीयको लागि सन्धीय गरियो।

२. प्रसारण लाईन विस्तार तथा निर्यात गर्ने काम सन्धीयको लागि सन्धीय गरियो, समावेसी, प्रसारित बार धुलिखेल सन्धीयको लागि उत्पादन गर्ने उत्पादन तथा निर्यात गरियो।

Local consultative meeting, Balephi RM, ward no- 08 (2019/04/03)


[illegible]

Local consultative meeting, Balephi RM ward no- 07
(2019/04/02)

[illegible]

Local consultative meeting, Lapsiphedhi /Shankarapur
Municipality (2019/06/16)

Annex- 8 Notice for Implementing CSR Activities



नेपाल विद्युत प्राधिकरण
(नेपाल सरकारको स्वायत्त)
इन्जिनियरिङ सेवा निर्देशनालय
वातावरण तथा सामाजिक अध्ययन विभाग

प.सं.: ०७५/१०७६
च.नं.: ८८०

मिति: २०७५/१२/१९


नेपाल
प्रकार:
संख्या: ४८६
वार्ड नं.: १०
मिति: २०७५/१२/१९


✓ श्री Creative Business Enterprises, Tripureswor, Kathmandu

विषय: विषय: कार्यदिश दिएको बारे ।

प्रस्तुत विषयमा नेपाल विद्युत प्राधिकरणद्वारा निर्माणाधीन तामाकोशी-काठमाण्डौ २२०/४०० के.भी. प्रसारण लाईन आयोजनाको CSR Activities अन्तर्गत Supply, Delivery, Installation, Testing and Commissioning of Irrigation Water Pump and PPR Pipe (Indrawati Rural Municipality Ward No 10, Sindhupalchowk) सम्बन्धी कार्यको लागि सम्बन्धी कार्यको लागि मिति २०७५/१२/१९ मा भएको सम्मौता बमोजिम उक्त कार्य ३ महिना भित्र सम्पन्न गर्न कार्यदिश दिएको व्यहोरा जानकारी गराइन्छ । सम्मौता बमोजिम आयोजना, वातावरण तथा सामाजिक व्यावस्थापन ईकाइ कार्यालय तथा स्थानिय सरोकारवालाहरूसँग समन्वय गरि कार्य गर्नु हुन समेत जानकारी गराइन्छ ।


बोधार्थ:
श्री तामाकोशी-काठमाण्डौ २२०/४०० के.भी. प्रसारण लाईन आयोजना, खरिपाटी, भक्तपुर ।
श्री वातावरण तथा सामाजिक व्यावस्थापन ईकाइ कार्यालय, खोडीचौर, सिन्धुपाल्चोक ।
श्री १० नं वडा कार्यालय, इन्द्रावती गाउँपालिका, मोटसिपा, सिन्धुपाल्चोक ।


रविन्द्र प्रसाद चौधरी
(निर्देशक)


मा.का.
२०७५-१२-२०

०/८

Notice for implementing CSR activity in Indrawati RM- 10, Bhotesipa


चौतारा साँगाचोकगढी नगरपालिका
Chautara Sangachokgadhi Municipality
 न न. वडा कार्यालय Office of Ward No.8
 ईर्खु, सिन्धुपाल्चोक Irkhu Sindhupalchok
 स्थापित २०७३ ESTD:2073

प्रत्र संख्या: ०७५/७६
 चलानी नं: ४९८

प्रदेश नं.३ नेपाल
 मिति २०७६/०१/०९

श्री वातावरण तथा सामाजिक अध्ययन विभाग
 ने.वि. प्रा. खरिपाटि, भक्तपुर

विषय : जिन्स सामान बुझिलिएको लिइएको भर्पाइ सम्बन्धमा

भर्पाइ दादै ने.वि.प्रा. तामाकोशी काठमाण्डौ २२०१४०० के.वि. प्रसारण लाइन आयोजनाको प्रभावित क्षेत्र डाँड गाँउमा सिंचाइको लागि त्यस विभाग बाट HD पाइप न इन्चि ६ एम.एम. को १६० मि. सहयोग स्वरुप यस वडा कार्यालयमा प्राप्त हुन आएको हुदाँ उक्त जिन्स सामान बुझिलिइ यो भर्पाइ गरिदियौ ।

रोहवर
 १.विर बं. श्रेष्ठ
 २.स.निर्देशक-भक्ति प्रसाद तिमिसिना
 ३.माधप भट्टराई -

कर्साङ तामाङ
 (वडा सदस्य)

Handing over Irrigation PPR Pipes in Irkhu

गोश्वामा

०८८८८८ २८ प्रकाशित

०८८८८८ २८ प्रकाशित

Invitation for Sealed Quotations

Publication Date: 2076/02/28

1. Nepal Electricity Authority, Environment and Social Studies Department (NEA-ESSD) invites sealed quotations for the following construction Works under CSR Activities of Tamakoshi-Kathmandu 220/400 kV Transmission Line Project in Sindhupalchowk district.

S.N	SQ. No.	Summary of Works	Estimated Amount With VAT (NRs)	Bid Security (NRs)
1	ESSD/SQ/ 24-2075-076	Construction of Pratikshyalaya (Resting Place), Kriyaputri Bhawan Restoration and Reconstruction of Bhimsen Temple	12,84,536.31	39,000
2	ESSD/SQ/ 25-2075-076	Compound Wall Construction of Buddha Stupa	11,27,019.50	34,000

2. Eligible Contractors may obtain further information and inspect the Bidding Documents at the office of Environment and Social Studies Department, Nepal Electricity Authority, Kharipati, Bhaktapur, address as mentioned below.

3. A complete set of Bidding Documents may be purchased from the office address mentioned below by eligible Contractors on the submission of a written application, along with the copy of company/firm registration certificate, Construction License certificate, Tax clearance certificate (F/Y: 2074/075), VAT registration certificate and upon payment of a non-refundable fee of NRs. 1000.00 deposited in account number 37-01-524-250978-01-7 of Nepal Electricity Authority, Environment and Social Studies Department at the Machhapuchhre Bank Limited, Kamal Binayak Branch, Bhaktapur during office hours on all working days within the 15th day of the publication of this notice.

4. Sealed bids must be submitted to the office address mentioned below on or before 12.00 noon within 16th day of publication of this notice. Bids received after this deadline will be rejected.

5. The bids will be opened in the presence of Bidders' representatives who choose to attend at 2.00 PM on the 16th day after publication of this notice at the office of NEA-ESSD, Kharipati Bhaktapur. Bids must be valid for a period of 45 days after bid opening and must be accompanied by a bid security/Cash security or Bank Guarantee amounting to a minimum amount mentioned above shall be valid for 75 days after opening the Bids.

6. If bidder wishes to submit the Cash Security, the cash should be deposited in account number 37-01-524-250978-01-7 at the Machhapuchhre Bank Limited, Kamal Binayak Branch, Nepal and submit the receipt of the deposited amount of cash along with the Bid Document.

7. If the last date of purchasing and/or submission falls on a government holiday, then the next working day shall be considered as the last date. In such case the validity period of the bid security shall remain the same as specified for the original last date of bid submission.

8. ESSD reserves the right to accept or reject, wholly or partly, any or all the Sealed Quotations without assigning any reason, whatsoever.

Environment and Social Studies Department

Nepal Electricity Authority

Kharipati, Bhaktapur, Nepal

Tel: 01-6611580, Fax: 01-6611590

Email: env.social@nea.org.np

Notice for sealed quotations for the selection of contractors for the construction of sub-projects in Barhabise

Annex- 9 Photographs



1: Labor camp at TL section AP 35/1



2: Men at work



3: Local consultative meeting, Balephi, AP 15 & AP 17



4: Local consultative meeting, Balephi RM- 7



5: Local consultative meeting, Balephi RM- 8



6: Local consultative meeting, Shankarapur Municipality



7: GRC formation meeting, Irkhu



8: GRC formation meeting, Thulo Sirubari



9: Orientation for enumerators for RP updating



10: ADB ETESIP review mission field visit





11: Gabion wall survey, Irkhu



12: Survey for road maintenance in Irkhu



13: Community building survey, Barhabise



14: Handing over irrigation pipes, Irkhu
