

Semiannual Environmental Monitoring Report

Project No. 42378-017

Loan No.- BAN-3350

December 2018

**Power System Expansion and Efficiency Improvement Investment Program - Tranche 3
Output-2: Transmission System expanded and upgraded**

Prepared by Power Grid Company of Bangladesh Ltd (PGCB) for People's Republic of Bangladesh.

This Semiannual Environmental Monitoring Report is a document of the borrower. The views expressed herein do not necessarily represent those of ADB's Board of Directors, Management, or staff, and may be preliminary in nature.

In preparing any country program or strategy, financing any project, or by making any designation of or reference to a particular territory or geographic area in this document, the Asian Development Bank does not intend to make any judgments as to the legal or other status of any territory or area.

Semi-annual Environmental Monitoring Report

Reporting Period : July, 2018 to December, 2018
Date : February, 2019

Power System Expansion and Efficiency Improvement Investment Program-Tranche 3

Loan No: 3350-BAN

(400/230/132 kV Grid Network Development Project)

TABLE OF CONTENTS

	Site Location of the Project	3-6
1.0	Introduction	7
2.0	Project Description	8-9
	2.1 Objectives of the Project	
	2.2 Scope of the Project	
	2.3 Project Progress Status and Implementation Schedule	
3.0	Compliance to National Regulations	10
	3.1 Brief summary of status of compliance with Environmental Conservation Rules 1997	
	3.2 Compliance to Environmental Covenants from the ADB Loan Agreement	
4.0	Progress of Implementation of EMP	11-12
	4.1 Compliance to Environmental Management Plan	
	4.2 Implementation of Environmental Safeguards Policies	
5.0	Safeguards Monitoring Results and Unanticipated Impacts	12-13
6.0	Conclusion and Recommendations	13
	Tables	
	Table-2.1 Project at a Glance	
	Table-4.1 Compliance with EMP	
	Table-5.1 Findings, Recommendations & Assistance to EA & its Contractors in Monitoring EMMP	



SITE LOCATION OF THE PROJECT:

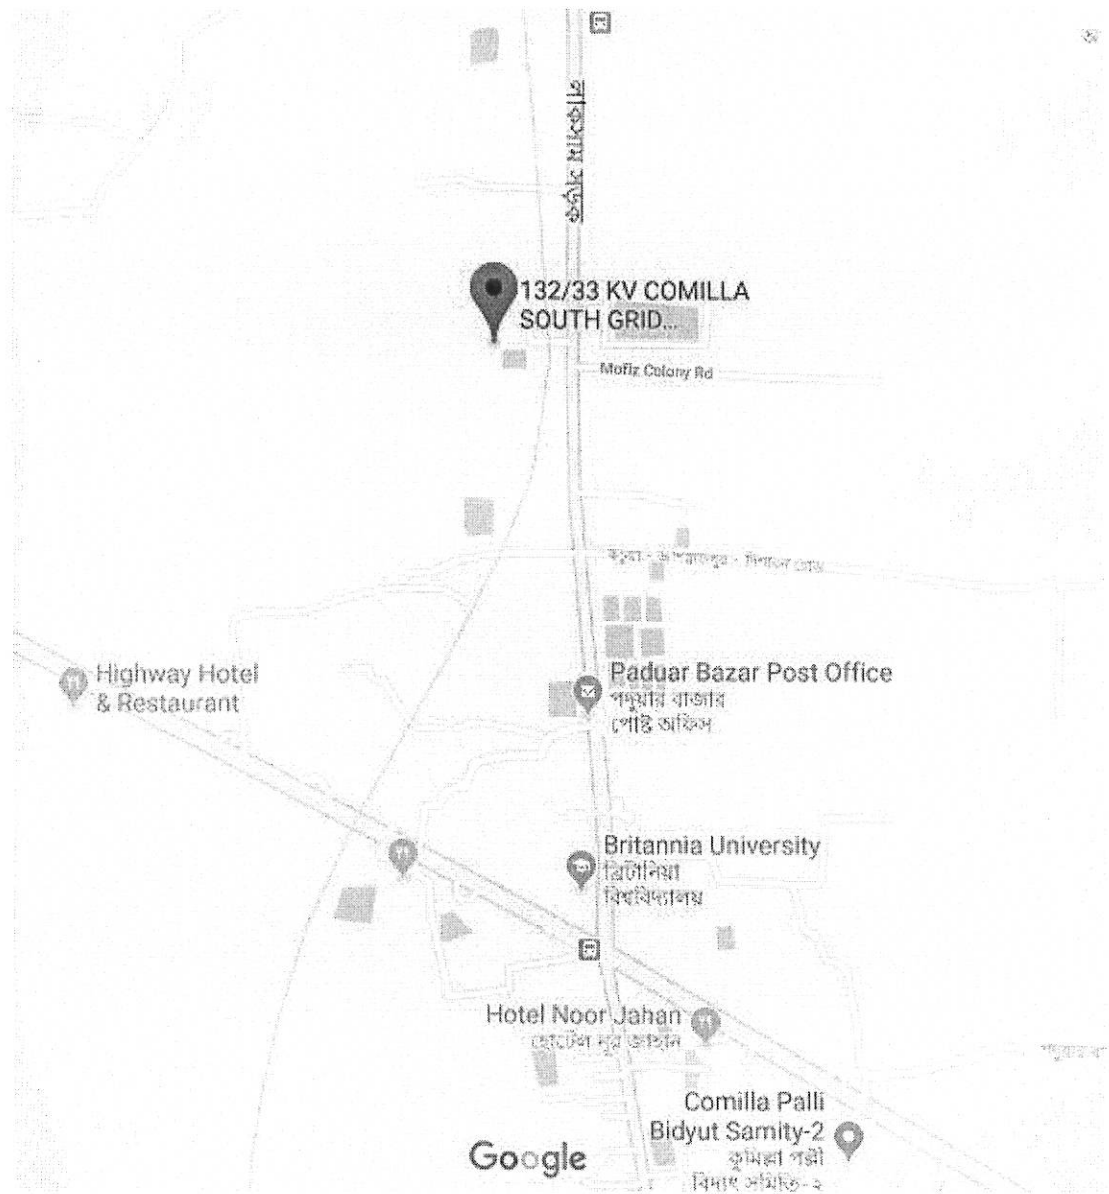


Fig-1: Site Location of 132/33 kV GIS Grid Substation at Comilla (South).





Fig-1: Site Location of 132/33 kV AIS Grid Substation at Kachua, Chandpur.

✓

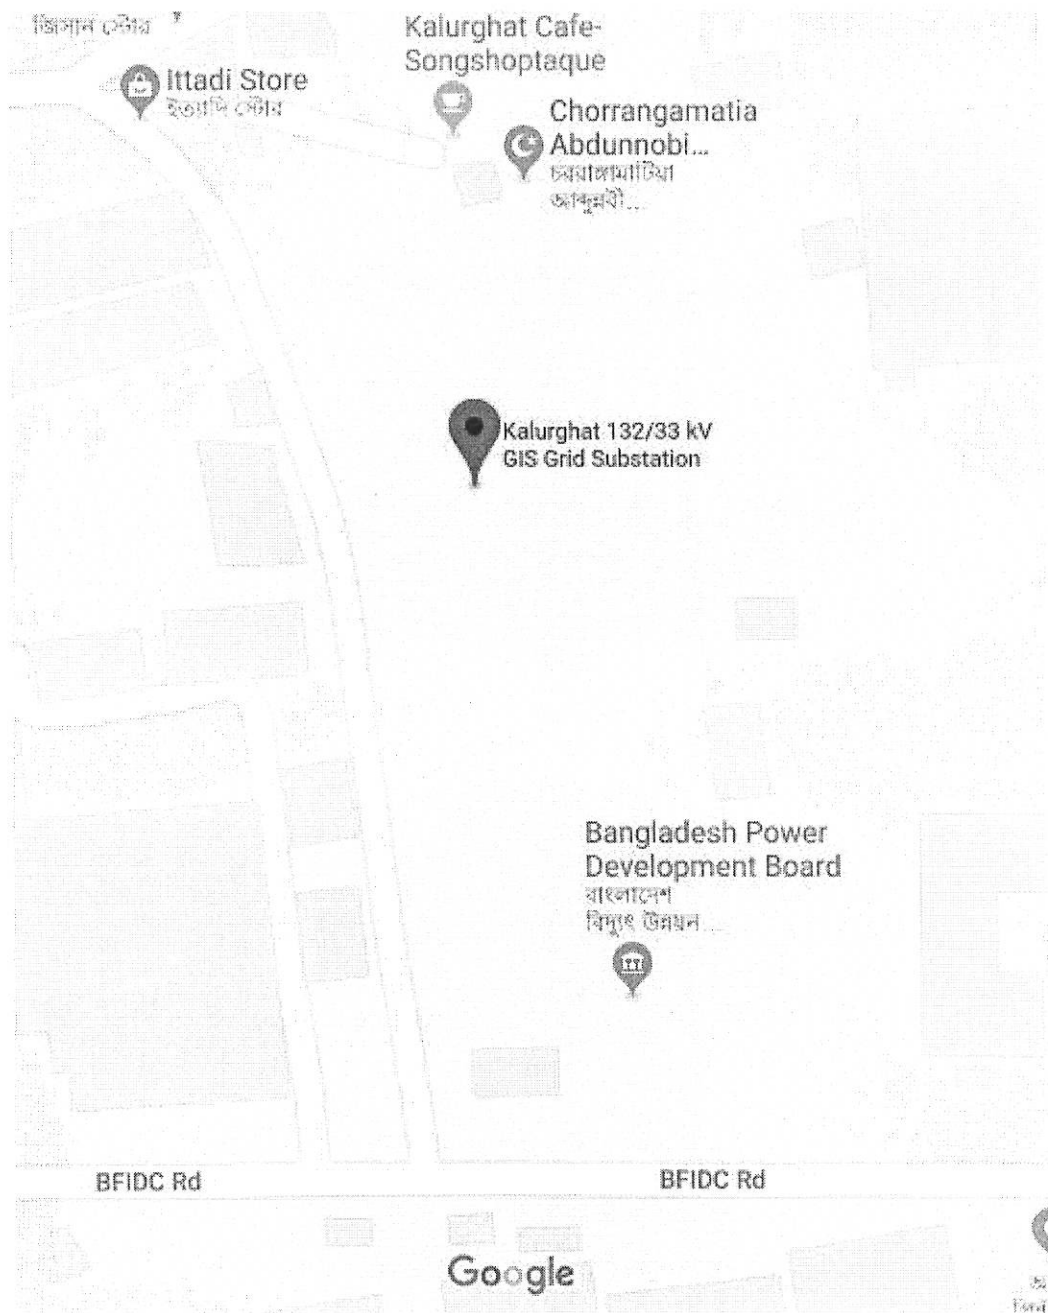


Fig-1: Site Location of 132/33 kV GIS Grid Substation at Kalurghat, Chittagong.

16

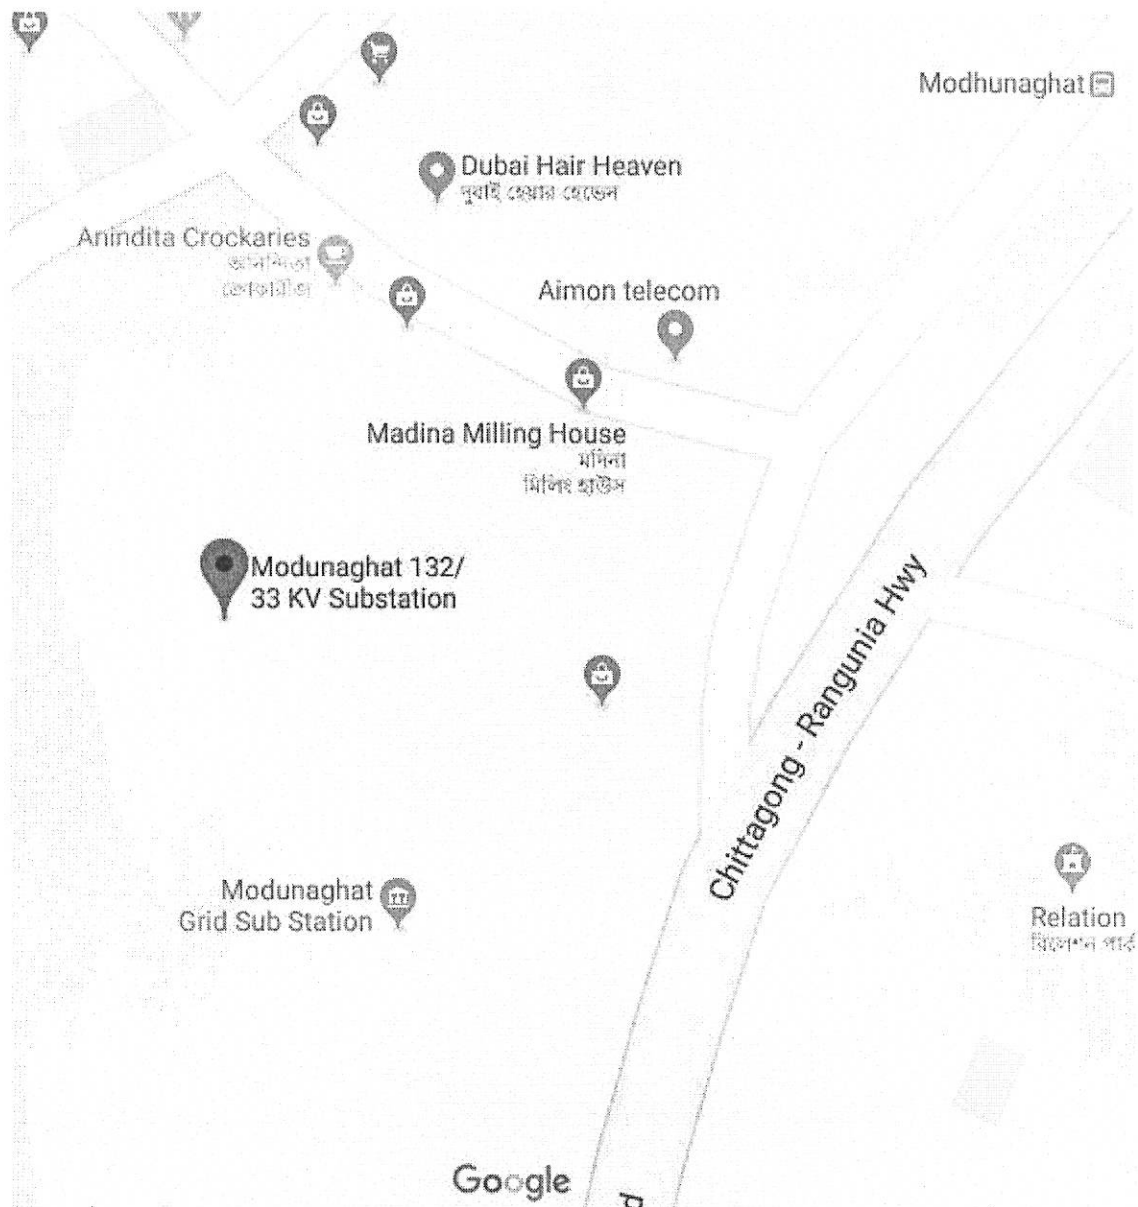


Fig-1: Site Location of 132/33 kV GIS Grid Substation at Madunaghat, Chittagong.



1.0 Introduction

Under Power System Expansion and Efficiency Improvement Investment Program -Tranche 3 (PSEEIP-III) of ADB 400/230/132 kV GND Project of Power Grid Company of Bangladesh (PGCB) is executing this project. A loan agreement was signed between ADB and GOB in this regard on December 22, 2015.

The project includes construction of 04 nos. (new 02 nos. & up-gradation 02 nos.) Grid substations and construction of around 72 km Transmission lines to up gradation transmission network of Dhaka & Chittagong and improve the power supply reliability.

This is a Semi-annual Environmental Monitoring Report for July, 2018 to December, 2018 time period. The objective of this report is to provide a status update on the implementation of Environmental Management Plans and other environmental compliance issues. This monitoring report is being submitted by 400/230/132 kV GND Project, PGCB to ADB.



2.0 Project Description

PGCB is the implementing agency of 400/230/132 kV Grid Network Development Project under the Ministry of Power, Energy and Mineral Resources.

2.1 Objectives of the Project

- To increase the power supply reliability of Comilla, Chandpur (Kachua) and Chittagong (Kalurghat & Madunaghat) area.
- To meet the growing demand of Comilla, Chandpur (Kachua) and Chittagong (Kalurghat & Madunaghat) area.
- To strengthen the power evacuation arrangement & increase power supply stability, reliability & Transmission capability in Comilla, Chandpur (Kachua) and Chittagong (Kalurghat & Madunaghat) area.

2.2 Scope of Work of the Project:

- **Lot-1 (Sub-station):**
 - a) New 132/33 kV, 2x50/75 MVA AIS Grid Sub-station at Kachua.
 - b) New 132/33 kV, 2x50/75 MVA GIS Grid Sub-station at Kalurghat.
 - c) Up gradation of 132/33 kV AIS substation to GIS substation at Madunaghat.
 - d) Up gradation of 132/33 kV AIS substation to GIS substation at Comilla(S).
- **Lot-2 (Transmission Lines):**
 - a) Madunaghat-Kalurghat 132 kV Double Circuit Underground Transmission Line: 7 km
 - b) Re-conductoring of Existing Comilla(South)-Chandpur 132 kV Double Circuit Overhead Transmission Line: 65 km

The details of the said project are given in Table-2.1.

Table-2.1: Project at a Glance

Project Title	:	400/230/132 kV Grid Network Development Project (Power System Expansion and Efficiency Improvement Investment Program- Tranche 3, Loan No: 3350-BAN)
Ministry/Division	:	Ministry of Power, Energy and Mineral Resources/Power
Executing Agency	:	Power Grid Company of Bangladesh Limited (PGCB)
Location of the Project	:	District: Comilla, Chandpur & Chittagong. Upazilla : Comilla Sadar, Hajiganj, Hathajari, Chandgaon.

- **Lot-1 (Sub-station):**

Construction and Completion of 132/33 kV AIS Substation at Kachua, 132/33 kV GIS Substation at Kalurghat and Upgradation of Existing 132/33 kV Madunaghat and Comilla (S) AIS Substation to GIS Substation on Turnkey Basis (Contract No. PSEEIP (TRANCH-3)/ADB/PGCB/P03/SS) has been signed

between PGCB and M/s. ABB India Ltd., India.

- **Lot-2 (Transmission Lines):**

Design, Supply, Erection, Testing & Commissioning of Madunaghat-Kalurghat 132 kV Double Circuit Underground Transmission Line and Re-conductoring of Existing Comilla(S)-Chandpur 132 kV Double Circuit Overhead Transmission Line on Turnkey Basis. (Contract No. PSEEIP (TRANCH-3)/ADB/PGCB/P03/TL) has been signed between PGCB and M/s. CCCE-ETERN-HANBAEK Consortium.

2.3 Project Progress Status and Implementation Schedule:

General Information:

Lot-1 (Substation):

Contract No: PSEEIP (TRANCH-3)/ADB/PGCB/P03/SS

Implementation Schedule:

The project completion date is August, 2019 which is 730 days from the effective date of the contract.

Lot-2 (Transmission Lines):

Contract No: PSEEIP (TRANCH-3)/ADB/PGCB/P03/TL.

Implementation Schedule:

The project completion date is March, 2019 which is 540 days from the effective date of the contract.

Present Status:

Financial Progress:

Lot-1 (Substation):	
Contract Price	USD 21,875,940.38 plus BDT 380,569,600.00
Total Expenditure up to December, 2018 (ADB Fund)	mUSD 13.55 + mBDT 84.31
Lot-2 (Transmission Lines):	
Contract Price	USD 12,290,399.91 plus BDT 32,171,049.33
Total Expenditure up to December, 2018 (ADB Fund)	mUSD 6.27 + mBDT 4.39

3.0 Compliance to National Regulations

3.1 Brief summary of status of compliance with Environmental Conservation Rules 1997:

Bangladesh Environmental Protection Act 1995 and subsequent amendments and relevant Acts including Environmental Conservation Rules (ECR) 1997 calls for environment-friendly execution of any Power Sector Development project in its all stages of Pre-Construction, Construction and Post Construction activities.

According to Environment Conservation Act 1995 and Environment Conservation Rules 1997, all projects have been classified into four categories (Green, Orange A, Orange B and Red). The power development projects are allocated to the red category, which triggers an automatic requirement for an Initial Environment Examination (IEE) followed by a full Environmental Impact Assessment (EIA) study. Subject to satisfactory review of the environmental assessment, the Department of Environment (DoE) issues an authorization for the project to proceed. The authorization consists of two parts: a "site clearance", which gives approval to the site proposed for the project and an "environmental clearance", which approves the content of the project.

A key requirement of the IEE/EIA for projects classified in the Red categories is an Environment Management Plan (EMP). The function of the EMP is to enable the project proponent PGCB to show the DoE how it will deliver the environmental performance assessed in the IEE/EIA (for which DoE approval is sought). The EMP must describe in detail organization and management responsibilities, give details of how mitigation measures identified in the IEE/EIA will be implemented and explain how monitoring will be carried out.

The PGCB, as the executing agency, is responsible for carrying out IEE and EIA studies of the project. PGCB has already engaged Center for Environment and Geographic Information Services (CEGIS) for conducting IEE and EIA study by splitting the total project between two sections: Section A for TRANCH-2 & Section B for TRANCH-3. IEE and EIA study has been completed for all those sections and based on the assessment; environmental clearance from DoE has been received for all the sections.

EMP has been made by CEGIS as a prerequisite of submitted EIA and getting approval from DOE. The EA (PGCB) has made its contractors concerned about the EMP and site activities are monitored to check the compliance with EMP.

3.2 Compliance to Environmental Covenants from the ADB Loan Agreement:

Civil construction works at different sites are running under the project. DOE's regulations and ADB's Safeguard Policy Statement (2009) are in general being complied with by the EA and its contractors. Provisions of the IEE and EMP updated with Hazard Safety issues to fill in by the working contractors and submitting regularly helped verification of compliance at site and so far did not call for any remedial actions to mitigate and making any specific event reference to ADB.

The contractors will submit report on the implementation of safety issues on regular basis with information that they were conducting awareness program and meeting up the gaps. Environmental Covenants are being complied with.



4.0 Progress of Implementation of EMP

4.1 Compliance to Environmental Management Plan:

As EMP is a key requirement for obtaining Environmental Clearance from DOE. PGCB has submitted an EMP with EIA study. The function of EMP is to identify the impacts on environment because of construction work, how to mitigate the impacts and explain how monitoring will be carried out. All personnel related to construction work are made aware of the EMP by regular meetings and currently, compliance of EMP is monitored by PGCB and safety officers of contractor. So far construction works are running with full compliance of EMP.

Table 4.1: Compliance with EMP

Time	Parameter/Indicator	Location	Frequency	Compliance Status/Remarks
Before Construction	Soil sampling	Substation sites (particularly those with existing structure and equipment dismantled)	Once before construction	Completed
	Local recruitment of workers and staff	Substations, transmission lines	Monthly	On Going.
	Orientation of Contractor(s) and workers on issues like HIV/AIDS, compliance to EMP, etc.	Substations and Transmission line	Once before construction, and as needed	Completed
Construction	Spraying of water to exposed land and before movements of construction vehicles	Substations and road basements when laying of underground cable to connect substations	<ul style="list-style-type: none"> Weekly at road basements (or as needed) Every day at substations sites during dry season and as needed during monsoon season 	Being complied
	Solid waste management	Substations, transmission lines	Every week	Being complied
	Danger and warning signs for safety of workers and the public	Substations and road basements affected by laying of underground cables, transmission lines	Once a month	Being Complied
	Announcement to the public of works schedule	Along the road basement affected by laying cables and substations	As needed	Being Complied

Time	Parameter/Indicator	Location	Frequency	Compliance Status/Remarks
	Erosion control measures such as temporary shoring	Substations, transmission lines (if needed)	Once	Being Complied
	Smoke belching construction vehicles	Sub stations and transmission lines	Weekly	Being Complied
	Dust and noise level	Substations, transmission lines	Twice a month	Being complied
	Housekeeping	Substations, and transmission lines	Weekly	Being complied

4.2 Implementation of Environmental Safeguards Policies

A focal person has been appointed for supervision of Environmental Management Plan. Consultants will be appointed for ensuring compliance of the Environmental Monitoring and Safeguards Policies, if required. Meanwhile, personnel from Environment Department, PGCB is now in charge of maintaining Environmental Management and Safeguards policy.

Equipment and construction materials are stored in sheltered spaces. All laborers are provided with Personal Protective Equipment.

5.0 Safeguards Monitoring Results and Unanticipated Impacts

The pertinent issues with reference to the Environmental Monitoring Plan (EMP) has been identified and correlated with the environmental standards where necessary. Such findings along with any unanticipated impact not included in the EMP have been placed with recommendations in **Table-5.1**. Assistance to EA and its Contractors in taking corrective action/measures and the steps thus taken / to be taken has also been pointed out therein.

In that context, attention has been drawn to take necessary actions particularly in respect of Institutional Requirement and Monitoring Plan for the Post Construction and Operational Phase as per EMP approved by DOE & ADB for the project. This would include assessment of the training and awareness requirement on occupational hazard & safety issues for the operational teams and evaluation of injury and incident reports of the working contractors as well.

Table-5.1: Findings, Recommendations & Assistance to EA & its Contractors in Monitoring EMMP


Sl. No.	Issues & Findings	Actions Taken by
1.	Monitoring Mechanism: This was required for implementing the EMMP	Health and Safety Officers have been appointed by the contractor.
2	Environmental Clearance Certificate (ECC) Renewal: ECC need to be renewed.	ECC will be renewed.
3.	Health & Safety Hazard Check List (HSCL):	Regular Tool Box Meetings are held at site for awareness of the workers. Contractors have been advised to prepare and maintain HSHCL and it is monitored by


Sl. No.	Issues & Findings	Actions Taken by
		EA.
4.	Environmental & Social Components: Environmental and Social Components were to be implemented with due diligence as per provision of the EIA.	PGCB is aware about the status of mitigation measures of potential impact on Environmental and social components.
5.	Environmental Parameters (EPs) Quality Monitoring.	No effluent from site falls into the river. Negligible amount of Green House Gas are emitted from the construction work.
6.	Sharing of information with Project Affected Persons (PAP) & Stakeholders' Response:	PGCB will continue keeping PAP informed in advance for remaining works on the ROW.

6.0 Conclusion and Recommendations

The objective and tools of monitoring and measuring the progress of implementation of the EMMP is basically to fulfill the safeguard requirements of ADB as well as that of DOE. Thus continuous updating of EMMP is required for unanticipated impacts standing currently apparent if any. Further, contract document has adequate coverage of Environmental and Occupational Health & Safety (EOHS) issues.

1. The copies of own policy documents of the contractors and their subcontractors pertaining to EHS & OHS along with Tender & contract provisions will be reviewed and evaluated periodically and followed for due assistance in implementing the EMMP. The gaps, if identified in the field through periodic inspection and verification, will be duly addressed.
2. Due safety training and awareness program will be continued particularly on Fire Hazards & Safety Orientation courses.
3. EMMP is a dynamic mechanism and hence the provisions contained in the available tools like EMP of EIA doc will be revisited from time to time.
4. PGCB will also follow up with DOE regarding renewal of validity of their Environmental Clearance for renewal of ECC.
5. PMU always follow up with the contractors about implementation of the recommendations.


(Engr. Sanjit Kumar Saha)
Dy. Project Director (S.E.)
400/230/132 Kv GND Project
PGCB, Dhaka


Md. Ohiduzzaman
Chief Engineer & Project Director
400/230/132 Kv GND Project
NLDC Complex, PGCB, Dhaka
