

Implementation of Resettlement Plan

#2 Quarterly Progress Report
For the period covered October to December 2016
Project Number: 44429-013
January 2017

IND: Climate Adaptation in Vennar Subbasin in Cauvery Delta Project

Prepared by the Water Resources Department of the Public Works Department, Government of Tamil Nadu for the Asian Development Bank.

This resettlement monitoring and evaluation report is a document of the borrower. The views expressed herein do not necessarily represent those of ADB's Board of Directors, Management, or staff, and may be preliminary in nature.

In preparing any country program or strategy, financing any project, or by making any designation of or reference to a particular territory or geographic area in this document, the Asian Development Bank does not intend to make any judgments as to the legal or other status of any territory or area.



**Loan 3394-IND Climate Adaptation in Vennar Subbasin in
Cauvery Delta Project**

Subject: Implementation of Resettlement Plan

**Quarterly Progress Report
October-December 2016**

18 January 2017

PMU Trichy

Water Resources Department

PWD, Government of Tamil Nadu-India

Abbreviations

ADB	Asian Development Bank
AEE	Assistant Executive Engineer
DP	Displaced persons
GoTN	Government of Tamil Nadu
Ha	Hectares
NGO	Non-Governmental Organisation
PAF	Project Affected Families
PAP	Project Affected People
PIU	Project Implementation
PMS	Project Management Specialist
PMU	Project Management Unit
PSC	Project Steering Committee
PWD	Public Works Department
RO	Revenue Officer
RP	Resettlement Plan
SDS	Social Development Specialist
SPS	Safeguard Policy Statement
Sq.ft	Square Feet
VAO	Village Administrative Officer
RDO	Revenue Divisional Officers
WRD	Water Resources Department

Preamble

1. The present Quarterly Report on Resettlement Plan implementation provides an overview of the project and activities undertaken for the implementation of resettlement plan in the project area between October and December 2016. Major progress made during this reporting period is summarized below.

Project Description

2. The Climate Adaptation in Vennar Sub-basin in Cauvery Delta Project (CAVSCDP) supports the implementation of the Government of India's National Action Plan on Climate Change (NAPCC) of 2008 and its National Water Mission (NWM). The project will improve irrigation water management in six channels namely Pandavaiyar, Vellaiyar, Harichandranadi, Adappar, Valavanar, and Vedharanyam Canal, covering a total command area of 78,000 hectare (ha) in the Vennar sub-basin of the Cauvery delta sprawl in *Thiruvavur* and *Nagapattinam* districts (Figure 1), of the state of TamilNadu, through investments in infrastructure, water resources management, and flood risk reduction.

3. Modernization of irrigation system by design, construction and improved management are the major tasks of the project. The important activities of the project are

- (i) re-sectioning of and embankment strengthening of river/canals,
- (ii) de-silting of river bed, and
- (iii) construction of new or rehabilitation of old or reconstruction of head regulators, cross regulators, drainage outfall, irrigation outfalls and infall of all six rivers of Vennar sub-basin.

4. Improved management will be delivered through non-structural interventions designed to (i) improve the management of surface water and ground water resources, and (ii) manage flood risks and flood events.


5. There-section also involves de-silting of river bed to the natural level, details of distance of rivers is given below in Table-1

Table-1 Details on Rivers and Distance

SI.No	Rivers	Distance in Kms
1	Harichandranadi	42.92
2	Adappar	41.19
3	Pandavaiyar	38.75
4	Vellaiyar	46.40
5	Valavanar	19.00
6	Vedharanyam Canal	46.20

Source: Census and Social Survey, October- November 2015

Figure 1: Project Area

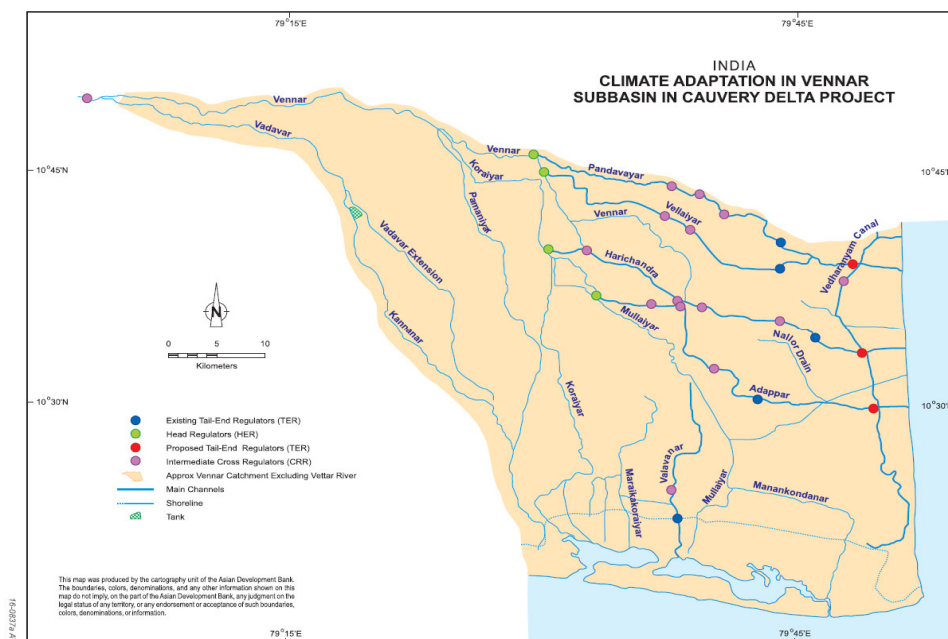

Source: ADB-Project Administrative Manual, May 2016

Land Required for Implementing RP

6. The project does not involve any land acquisition as the Right-of-Way (RoW) along the banks of the river/canal are WRD land and the RoW has been established in the field by the revenue officials using revenue records. However, the rehabilitation of the embankment will cause impact to the encroachers and squatters who have occupies the canal/river banks that are within the RoW.

7. The socio economic survey carried out in December 2015 identified that the proposed project will involve impact to encroachers and squatters living along the bunds of these rivers, and the resettlement plan has been prepared to mitigate the involuntary resettlement impacts. The RP is based on the census and socio-economic survey of the affected households (AHs) in the six rivers/channels proposed for improvement under this project viz.(i) Harichandranadi River; (ii) Adappar River; (iii) Pandavaiyar River;(iv) Vellaiyar River;(v) Valavanar River; and (vi) Vedharanyam Canal. The RP is based on the final detailed design prepared by WRD, GoTN.

8. The implementation of the project will require displacement of 3,235 private structures, comprising of 2,642 residential structures, 349 commercial structures, 129 residence cum commercial structures and 115 cattle shed/shelters. The total number of affected persons is 12,887. Further,157 common property resources will also be impacted. The involuntary resettlement (IR) impacts are summarized in Table 2 and Table 3.

9. Since the encroachers and squatters have occupied the embankments and are within the Right of Way (RoW), Implementation of RP has become indispensable as no civil works can happen until the squatters and encroachers are resettled and rehabilitated. For implementing RP in all six project rivers, it is estimated that 39 ha (i.e. almost 100 acres) of land is required either by identifying Government lands or purchasing Private lands for constructing houses for the affected households. For the purpose of housing, 1300 sq.ft of land has been worked out per house including common space.

Table 2: Details of Encroachers and squatters

S.No	Encroachers and squatters	Number of Impacted Structures
1	Residential structures	2642
2	Commercial structures	349
3	Residence cum commercial structures	129
4	Cattle shed / shelters	115
5	Common property resources	157

Source: Census and Social Survey, October-November 2015

Table3: Details on River wise Ownership of Impacted Structures

Tenure	Pandavaiyar	Vellaiyar	Harichandra Nadhi	Adappar	Valavanar	V - Canal	Total	Percentage
Owner	76	289	402	177	1	1	946	29.2
Encroacher	3	14	10	4			31	1.0
Squatter	320	697	657	305	6	35	2020	62.4
Squatter-Tenant	21	18	109	9	2	3	162	5.0
Tenant	5	6	64	1			76	2.3
Total Structures	425	1,024	1,242	496	9	39	3,235	100.0
Total AHs	425	1,024	1,242	496	9	39	3,235	
Total APs	1,687	4,219	4,931	1,865	45	140	12,887	

Source: Census and Social Survey, October-November 2015

Identification of Land for Resettlement of Affected households

10. The available RoW has been fully considered for the proposed improvement and the existing RoW for the river/channel were determined using village maps and field measurement books and verified at site. Since the available RoW is sufficient to meet the design cross section for the proposed improvements the project would not involve any private land acquisition. However, the project will impacts squatters living along the banks of the river/channel causing physical and economic displacement and thereby triggering involuntary resettlement safeguards.

11. For implementation of the Resettlement Plan of the project, lands are required for resettling the squatter households and relocating the common property resources affected by the project. Hence, it was decided to identify lands from Government sources and if sufficient lands are not available, lands from private

land owners who are willing to sell. The suitability of land for constructing houses with consideration of ideal conditions for resettlement of affected squatter households from all six project river and canal banks is being examined.

12. Sub-Divisional Officers, Assistant Engineers, Work Inspectors and Irrigation Assistants are engaged in identification of Government lands in their respective project areas by collecting data from Village Administrative Officers and Village Assistants of Revenue Department.

13. It was decided that the jurisdictional AEEs and AEs from the PIU and the special Project Division would be engaged in identifying the resettlement sites, not only the Government lands but also suitable private lands for their respective rivers allocated to them. The Special Project Officials are supported by the Social Development Specialist, Revenue Department and the WRD officials' in PMU Division (1 AEE and 3 AEs). The Social Development Specialist is working with the officials of WRD and Revenue Department in identification of land suitable for construction of houses for project affected persons.

Method adopted for visiting Locations

- (i) SDOs of respective rivers were contacted to depute AEs, Work Inspectors and Irrigation Assistants to visit the location
- (ii) VAOs and Village Assistants of particular village were contacted and requested to confirm the identified lands with the help of Field Measurement Book (FMBs)
- (iii) The team consisting of CAVSCDP officials, Revenue Officials and Social Development Specialist visited each and every site located in Pandavaiyar, Vellaiyar and Adappar.

Visits to all reported Government sites

14. AEs, Work Inspectors and Irrigation Assistants, Village Administrative Officer (VAO) of Revenue Department, along with Social Development Specialist have visited all reported sites located along Pandavaiyar, Vellaiyar, Adappar and Harichandranadhi. Of all reported sites, suitable sites were screened for further verification by SDOs and AEs for finalization of sites for resettlement of DHs appropriately. Suitable sites finalized by Social Development Specialist and the list of sites were sent to PIUs for finalization.

- (i) In some places revenue records like Field Measurement sketch and Adangal were collected.
- (ii) In some villages, new lands could be identified while having meeting with VAOs by explaining about the purpose and project details
- (iii) Large extent of lands available in Umbalacherry and Pushpavanam Villages, can be accommodated hundreds of PAFs, but could be done only by the decisions/preferences by the DHs.

15. Based on the meeting with District collector, RDO of Nagapattinam District has visited all Government Lands identified to resettlement to assess for its suitability.

16. Chief Engineer and Project Director of CAVSCDP, Superintending Engineer and Executive Engineer, PIU, Thiruvarur and the Project Management Specialist (PMS) have met both Nagapattinam and Thiruvarur District Collectors regarding allotment and enter upon permission for the identified Government lands for resettlement of PAFs. Collectors agreed to conduct meeting with Revenue Officials for the same.

Criteria adopted selecting locations

Government Land

- (i) Land identified should not be categorized as wet (Nanjai) and water body related lands in the Revenue records
- (ii) Free from encumbrance, if encumbrance exists, assess the magnitude, whether could be solved
- (iii) Proximity of the land identified for resettlement from the villages where DHs reside
- (iv) Road access to the land identified for resettlement of DHs
- (v) Feasibility to provide basic amenities such as drinking water, electricity and drainage
- (vi) Possibilities of continuing the livelihood activities of DHs even after resettlement
- (vii) Assess the location for any land preparation is required like land filling before construction, need to buy land for approach, construct a bridge to connect proposed site etc.

Private Lands

- (i) Land could be identified by the Villagers and Revenue Officials along with CAVSCDP personnel
- (ii) Verification of Revenue Records for genuineness of title including ownership, encumbrance
- (iii) Obtaining copies of documents and consent letter along with indicative selling price from the owner
- (iv) Examining access to road and other facilities

Identification of Additional Lands

17. It was decided to identify Government lands from adjoining villages where DHs reside. For carrying out confirmation of already identified lands and identifying

new lands for Pandavaiyar, Vellaiyar, Adappar and Harichadranadhi, it was decided to engage 4 SDOs, each supported by 2 AEs (total 8 AEs) . Following this, a meeting was conducted with AEEs and AEs of Thiruvarur, Thiruthuraipoondi and Nagapattinam at Thiruvarur to explain the method involved in identifying suitable land and the need to achieve target.

18. As a follow up, a meeting with AEs and Irrigation Assistants was held in PIU, Thiruthuraipoondi, for identifying lands by meeting VAOs and Village Assistants of respective adjoining villages of Harichandranadhi and Adappar. Extent of Government and Private lands identified is attached in **Annexure 1**

Excerpts of the meeting Conducted by the Project Director on Identification of Government Lands for Resettlement

- (i) Officials were requested to confirm the Government Lands identified in Pandavayar, Vellaiyar and Adappar
- (ii) Procure FM Sketches for the lands suitable by the AEs of their respective rivers
- (iii) The AEs were requested to examine the facilities available such as road approach, electricity, water facilities etc in the available lands for preparing cost estimation for all sites.
- (iv) The AEs those who are responsible for confirming Government lands are also need to identify suitable lands both Government and Private lands in the adjoin villages for resettlement.
- (v) Lands suitable for villages having proximity to more than one river could also be identified
- (vi) All FMBs received are to be handed over to the other team of AEs and they are responsible of drawing layouts
- (vii) Those layouts are to be sent to PMU for preparing cost estimation for each site.

19. Responsibilities of Officers and checklist for collecting information in the site were formulated and are presented in Annexure 2,3 4 and 5

Meeting with District Collector and Decisions

20. District Collector of Nagapattinam District organized a meeting with Revenue officials of the district. The meeting was attended by CAVSCDP, WRD-PWD.

Excerpts of the meeting

- (i) RDO informed about the purpose of the meeting to the participants and requirement of lands in all project affected villages

- (ii) District Collector informed the Revenue Officials that the government lands are required to resettle the project affected families residing in all six canals in Nagapattinam District.
- (iii) Collector enquired every VAO for availability of land in each village for resettlement
- (iv) Collector asked officials to search for suitable Private Lands as well.
- (v) Some of the VAOs assured that the lands could be identified and some of them do not find lands in their villages
- (vi) Collector asked VAOs to identify lands in the adjoining villages too if lands are not in their jurisdiction
- (vii) Collector asked the officers to identify lands for resettlement with the close proximity so as not to affect the culture and livelihoods of PAFs
- (viii) Collector asked the Revenue Inspectors to follow VAOs in identification of lands
- (ix) Social Development Specialist requested officers to identify lands available with private owners if the Government lands are not available.
- (x) Executive Engineer explained about the entitlements to the PAFs
- (xi) Social Development Specialist explained about the project, purpose of resettlement of PAFs, extent of land required, involvement of officials of WRD-PWD, facilities that would be provided to the PAFs during and after resettlement, process of joint verification of PAFs and requested Revenue Officials for their cooperation till the end of Project completion.
- (xii) Participants have assured to provide details of land with FM sketch to the RDO, Nagapattinam in 10 days time.

Identification of Land and Layout for Resettlement of DHs

21. Based on the ADB Mission visit between 05 and 07 December 2016 and Aide memoire, Government lands available were marked in the village maps. Suitability of all identified lands was carried out by the Social Development Specialist and suitability is being assessed by the WRD officials and are preparing the layout drawings simultaneously. Identification of Private Lands in all rivers is also progressing. A format for collecting updated data on Government and Private land identified and found suitable was prepared and sent to PIUs. The format will be used for consolidating fortnight progress report in a matrix. The details of layout completed is shown in Annexure-7

Project Director's Filed Visit

22. Project Director visited all six project rivers between 16 and 18 December 2016 and seen most of the resettlement sites identified.

23. The Project Director advised to undertake joint verification of DHs in Pandavaiyar and Vellaiyar immediately by the NGO and Officials concerned as civil

works are in advance stage in these 2 rivers. He has also advised to resettle the DHs whose houses fall within toe-to-toe first, so as to complete the civil works.

24. The Project Director along with EEs met both District Collectors of Nagapattinam and Thiruvavarur on 30 December 2016 regarding identification and allotment of Government and Private Lands for resettlement of DHs.

25. District Collector of Nagapattinam has assured to sanction enter upon permission to all possible lands identified Government Lands for construction of houses.

Grievance Redressal Committee

26. Grievance Redressal Committee (GRC) has been constituted in Thiruvavarur District for CAVSCD Project and the same is issued through the Proceeding of the District Collector of Tiruvavarur R.C. No. 9641/2016/B2 Dated 06.12.2016.

NGO Recruitment

27. Non-Governmental Organization - HEAVEN has been appointed for undertaking joint verification and other tasks in the project. Planned for providing orientation programme to the NGO personnel has been done and action plan was also prepared (**Annexure 6**). NGO personnel have also accompanied the CAVSCDP team during Project Director's visit.

28. A draft gist for disclosure required for Resettlement Plan implementation was prepared and will be printed in the Month of January 2017 for the distribution to the DHs during joint verification and public disclosure meetings.

Field Observations

29. The following patta lands are situated inside the boundary of Vellaiyar in Nagapattinam District where civil works are in progress. The patta holders protested and stopped civil works, claiming that the land belong to them. Some have houses and one brick kiln is located inside the RoW (Right of Way). The Executive Engineer has been informed about this for necessary action.

Details of Patta lands which fall inside the RoW in Vellaiyar

Sl. No	District	Taluk	Village	Patta Number
1	Nagapattinam	Thirukuvalai	Therkupanaiyur	42, 46, 59, 60a, 60b, 60c, 85a, 85b, 180/1, 180/2, 178, 182, 183, 185 and 186 (15 nos.)
2	Nagapattinam	Thirukuvalai	Melavalakarai	16,18 and 68/2
3	Nagapattinam	Thirukuvalai	Madapuram	12 and 24

Important concern for action

30. At 145.4 Km, Mr. S. Radhakrishnan S/o Mr. Santhanam (Late) has donated his land for constructing Cremation Shed replacing affected one on the Right Bank of Vellaiyar near Eravaikadu and construction has been started and progressing. In this regard, the land donated for the construction has not been properly documented and donated for the purpose. Hence, the land donated needs to do a proper documentation through registration process and then to proceed construction activities.

31. Similarly, another cremation centre gets affected on the opposite side of the same place in Vellaiyar, at village called Naatiruppu. People of Naatiruppu informed that the Government prompoko land is available in the village, that could be used for constructing cremation centre for Naatirupu village, Officers concerned could confirm the same and proceed in getting land details from VAO.

Advantages by field visits and meetings

- (i) Found new lands in the same village which could be used for resettlement
- (ii) Found that the PAFs were given pattas for lands that can be used for construction of houses, those PAFs could not construct houses due to lack of money and cost involved for land filling before construction

These are added advantages in the process involved in implementation of the RP and construct houses to DHs after confirmation of PAFs through joint verification

Limitations

- (i) Many Revenue Officials could not share land details as they require communication or order from their higher officials to provide data/information on availability of land
- (ii) Getting appointment with VAOs, because they are engaged in their regular works and also look after other villages as additional charge

Field Experience and Plan for the Future

- (i) Since Private lands categorized as Dry (Punjai) are lacking in the project area, identification of Government lands in neighbouring villages where DHs currently reside would be ideal.
- (ii) Need to form four teams of CAVSCDP officials to identify Government lands in Pandavaiyar, Vellaiyar, Adappar and Harichandranadhi as these four rivers have large numbers of DHs
- (iii) SDOs, AEs of respective rivers need to visit the suitable sites which were screened by the Social Development Expert for finalization of sites for construction of houses.

- (iv) Obtain Field Measurement diagrams of selected sites for all survey numbers from FMBs for preparation of building layouts
- (v) PIUs to initiate preparation of layout all sites for house construction using FM sketch by adopting the model prepared by PMU.

Annexure - 2

**Personnel involved in Identification of Government and Private Land for
Resettlement of DHs**

Name of the River – Pandavaiyar

Sl. No	Name	Designation and Division
Government Land		
1	Er. B. Ravichandran	Executive Engineer, Vennar Basin Division, Thiruvarur, (PIU-I)
2	Er. S. Marimuthu	Assistant Executive Engineer, Vennar Basin Division, Thiruvarur (PIU-I)
3	Er.V.Govindarajan	Assistant Engineer, WRD, Vennar Basin Division, Thiruvarur
4	Mr. Gunasekaran	Work Inspector, WRD, Vennar Basin Division, Thiruvarur
5	Mr. Jegadeesh	Irrigation Assistant, WRD, Vennar Basin Division, Thiruvarur
6	Mr. Kumar	Irrigation Assistant, WRD, Vennar Basin Division, Thiruvarur
7	Mr. Janagarajan	Irrigation Assistant, WRD, Vennar Basin Division, Thiruvarur
Private Land		
8	Er.P.Camillus	Assistant Executive Engineer, WRD, Project Management Unit, Trichy
9	Er.R.Kolanjinathan	Assistant Engineer, Project Management Unit, Trichy
10	Er.S.Selvakumar	Assistant Engineer, WRD, Project Management Unit, Trichy

Name of the River – Vellaiyar

Sl. No	Name	Designation and Division
Government Land		
1	Er. B. Ravichandran	Executive Engineer, Vennar Basin Division, Thiruvarur, (PIU-I)
2	Er. S. Marimuthu	Assistant Executive Engineer, Vennar Basin Division, Thiruvarur (PIU-I)
3.	Er. P. Sugendran	Assistant Executive Engineer, WRD, Vennar Basin sub Division, Thiruvarur
4	Er. Thangamuthu	Assistant Engineer, WRD, Vennar Basin Division, Thiruvarur
5	Er. Chidambaranathan	Assistant Engineer, WRD, Vennar Basin Division, Thiruvarur
6	Mr. Viswanathan	Irrigation Assistant, WRD, Vennar asin Division, Thiruvarur
7	Mr. Saravanan	Work Inspector, WRD, Vennar Basin Division, Thiruvarur
8	Mr. Devadoss	Irrigation Assistant, WRD, Vennar Basin Division, Thiruvarur

Sl. No	Name	Designation and Division
<u>Private Land</u>		
9	Er. K.Asokan,	Executive Engineer, Project Implementation Unit-III, Thiruthuraipoondi/Special Project Division, Thanjavur
10	Er.S.Ramesh	Assistant Executive Engineer-I, WRD, Project Implementation Unit-III, Thiruthuraipoondi/ Special Project sub Division, Thanjavur
11	Er.B.Kavitha	Assistant Executive Engineer-I, WRD, Project Implementation Unit-III, Thiruthuraipoondi/ Special Project sub Division, Thanjavur
12	Er.T.Vinoth	Assistant Engineer, Special Project Division, Thanjavur
13	Er. A Kannadassan	Assistant Engineer, Special Project Division, Thanjavur

Name of the River – Adappar

Sl. No	Name	Designation and Division
<u>Government Land</u>		
1	Er.P.MoorthyRaajan	Assistant Executive Engineer, WRD, Thiruthuraipoondi (PIU-I)
2	Er.S.Gnanamani	Assistant Engineer, WRD, Thiruthuraipoondi (PIU-I)
3.	Mr. Kalidoss	Irrigation Assistant, WRD, Vennar Basin Division, Thiruvarur

Annexure 3**Tasks to be carried out and Officers Responsible for Assigned Works**

Stage	Tasks	Rivers	Officers Responsible	Contact Nos.
I	1. Examining feasibility of already identified sites located in Pandavaiyar, Vellaiyar and Adappar 2. Identification of new Government lands in the adjoining villages of all rivers for resettlement	Pandavaiyar	1. Er. Sugendran, SDO 2. Er. Chidambaranathan, AE 3. Er. Dhanaram, AE	9487988845 9443975890 9962344232
		Velliyar	1. Er. Er. Kalayanasundaram, SDO 2. Er. Vairavel, AE 3. Er. Vinod, AE	9486927703 9551972002 9865440164
		Adappar	1. Er. Shankar, SDO - 2. Er. Surendra Mohan, AE 3. Er. Gnanamani, AE	9345641480 9787358901 9600260666 9865724228
		Harichandra nadhi	1. Er. Ramesh, SDO 2. Er. Chandran, AE 3. Er. Kannadasan, AE	9842876981 7373014228 8098890090
II	Letter to District Collectors of Nagapattinam and Thiruvavarur for transfer of Government lands identified		1. Er. Marimuthu, AEE, TPA, Thiruvavarur	9488033819
III	1. PMU – Preparation of project cost estimate for proposed building plan for all survey numbers 2. Rough cost for infrastructure such as roads, electricity, water supply, Sanitation, bridge and drainage		1. Er. Camillus, AEE 2. Er. Sara, AEE	9442360801 9500398492
IV	Preparation of Layout for houses	Pandavayar	1. Er. M.G. Rajendran, SDO 2. Er. Govindharaj, AE 3. Er. Kamalakannan, AE	9566606301 9751321680 9865314187
		Velliyar	1. Er. Vilvendhan SDO 2. Er. Elayaraja, AE 3. Er. Aiyanar, AE	9487257139 9095202699 9150402026
		Adappar	1. Er. MoorthyRajan, SDO 2. Er. Gnanamani, AE 3. Er. Thangamuthu, AE	9842703154 9865724228 9789714670
		Harichandra nadhi	1. Er. Kavitha, SDO 2. Er. Dhanaraj, AE 3. Er. Raguram, AE	9003754483 9865748823 8870724655

Annexure 4**Checklist for Verification of Government Land already visited Feasibility**

Sl. No	Details Need to be Verified/Collect	Response
1	Collect Field Measurement Sketch (FMB)	a) Yes b) No
2	Proximity to nearby village	Kms
3	Water Supply availability -Distance in Km from source	a) If yes Km b) No
4	Whether land filling needed	b) Yes b) No
5	Availability of Electricity -Distance in Km from nearest place	a) If yes Km b) No
6	Road access	
7	Indicate approach road to the selected site	
8	Indicate whether any encumbrance/disputes	
9	Distance from nearest encroached settlement	Kms

Annexure 5**Checklist for identifying additional Government Lands**

Sl. No	Details Need to be Verified/Collect	Check whether received
1	Collect Taluk map	
2	Identify nearby villages –in 5 Kms. radius from the river for identifying Government lands	
3	Meet VAO's and Village Assistants and get details of Govt. land	
4	Field Measurement Sketch (FMB)	
5	Survey Numbers	
6	Extent – how many acres / Ha	
7	Classification of the land	
8	Indicate whether any encumbrance/disputes	
9	Distance from nearest encroached settlement	
10	Get Contact numbers of VAO and Village Assistants	
11	Whether patta issued to the beneficiaries under any schemes e.g. Adi Dravida Welfare Department in the site identified	

Annexure 6.**NGO Action Plan – Sequence of Tasks**

1.	Receive a copy of Resettlement Action Plan and study the plan by the NGO personnel
2.	Receive all Baseline data filled in forms from PIU by submitting acknowledgement
3.	Reconnaissance visit to all 6 rivers
4.	Orientation to NGO personnel by Social Development Specialist
5.	Starting Joint Verification of PAFs and PAPS in Pandavaiyar
6.	updating of census and socio economic survey data
7.	updating/appendixing the survey data in the database
8.	disclosing the gist of the RP including details of contact of GRC
9.	facilitating the revenue cell and PIU in identifying suitable sites for resettlement
10.	identifying amenities and facilities required at resettlement site
11.	assisting PIU in getting the ID cards prepared
12.	issuing of identity cards
13.	Conduct HIV/AIDS Awareness to the construction labourers
14.	obtaining options from DPs, wherever applicable
15.	preparing list of eligible DPs for dissemination
16.	assisting PIU in disclosing draft list of PAPs along with details of impact and entitlements (micro plan)
17.	assisting PIU and revenue cell in receiving and hearing concerns and complains with regard to draft list of entitlement published
18.	disbursement of assistances
19.	assisting PAPs in relocating to the resettlement site
20.	providing guidance and counselling during the transition period
21.	facilitating disclosure of relevant information in a timely manner in Tamil
22.	holding periodic consultations with PAPs; and
23.	Identifying suitable training for skill development.
24.	Assist DPs in approaching the GRC, whenever required, and assist PIU in maintaining a record of grievances received/lodged and action taken/compliance.
25.	Attend monthly review meetings at PMU and be available during visit of ADB and external monitor.

Details of No. of Houses as per Layout

SI No	Name of River	District	Taluk	Village	Survey No.	No. of Houses Planned
1	Pandavaiyar	Thiruvarur	Needamangalam	Vengaramperaiyur	8/0	47
2	Pandavaiyar	Thiruvarur	Kodavasal	Thittanimuttam	39/1	46
3	Pandavaiyar	Thiruvarur	Kodavasal	Nalilondru	7/33, 7/34	34
4	Pandavaiyar	Thiruvarur	Kodavasal	Thiruvidaivasal	12/8	16
5	Pandavaiyar	Thiruvarur	Kodavasal	Thiruvidaivasal	8/18	14
6	Pandavaiyar	Thiruvarur	Kodavasal	Kankoduthavanitham	116/9	8
					Total	165
1	Adappar	Thiruvarur	Thiruthuraipoondi	Velur	191-2	154
2	Adappar	Thiruvarur	Thiruthuraipoondi	Korukkai	182-16	56
3	Adappar	Nagapattinam	Vedaranyam	Thulasapuram	151-3	70
4	Adappar	Nagapattinam	Vedaranyam	Umbalachery	5/1, 5/3, 10, 236/2A, 237/1, 273/3, 239, 240/2, 241, 242/2, 243, 244, 245/2, 246/1b, 247/3	150
5	Adappar	Nagapattinam	Vedaranyam	Pushpavanam	438	19
					Total	449
1	Vedharanyam Canal	Nagapattinam	Vedaranyam	Pushpavanam	438	14
2	Vedharanyam Canal	Nagapattinam	Nagapattinam	Karuvelankadai	70	14
3	Vedharanyam Canal	Nagapattinam	Nagapattinam	Prathaparamapuram	118/2	12
					Total	40
1	Vellaiyar	Thiruvarur	Thiruvarur	Pinnavasal	135	56*
2	Vellaiyar	Nagapattinam	Keevalur	Prathamapuram / Kudavasal	2 / 1c2	550
					Total	606
1	Harichandranadhi	Nagapattinam	South Keevalur	Karapidagai	446	157
2	Harichandranadhi	Nagapattinam	South Keevalur	Karapidagai	399	186
						343

Note: *Twin house in Ground and First floor (4 houses in Single plot)
