

Social Monitoring Report

Semi-Annual Report

Project Number: 51190-001
Loan Number: L3702 NEP
July 2021

Nepal: Disaster Resilience of Schools Project

Prepared by Central Level Project Implementation Unit (Education) of National Reconstruction Authority for the Government of Nepal and the Asian Development Bank.

This social monitoring report is a document of the borrower. The views expressed herein do not necessarily represent those of ADB's Board of Directors, Management, or staff, and may be preliminary in nature.

In preparing any country program or strategy, financing any project, or by making any designation of or reference to a particular territory or geographic area in this document, the Asian Development Bank does not intend to make any judgments as to the legal or other status of any territory or area.

ABBREVIATIONS

ADB	–	Asian Development Bank
BoQ	-	Bill of Quantities
CLPIU	-	Central Level Project Implementation Unit
COVID-19		2019 novel coronavirus
DRSP	-	Disaster Resilience Schools Project
DSC	–	Design and Supervision Consultant
DUDBC	–	Department of Urban Development and Building Construction
DLPIU	-	District Level Project Implementation Unit
EA	–	Executing Agency
EARF	-	Environmental Assessment and Review Framework
EEAP	-	Earthquake Emergency Assistance Project
EMP	-	Environmental Management Plan
EPR	-	Environment Protection Rules
GON	–	Government of Nepal
GRC	–	Grievance Redress Committee
IA	–	Implementing Agency
IEE	-	Initial Environmental Examination
LOC	-	Land Ownership Certificate
MoEST	-	Ministry of Education, Science and Technology
NRA	-	National Reconstruction Authority
PAM	–	Project Administration Manual
PD	–	Project Director
PIU	–	Project Implementation Unit
PPE	-	Personal Protective Equipment
RE	-	Residence Engineer
REA	-	Rapid Environment Assessment
Recon	-	Re-construction
RF	-	Resettlement Framework
RP	-	Resettlement Plan
SE	-	Site Engineer
Sq. m.	-	Square Meter/s
SM	-	Safeguards and GESI Monitors
SOP	-	Standard Operational Procedures
SSDP	-	School Sector Development Plan
TLC	-	Temporary Learning Center

TABLE OF CONTENTS

1. INTRODUCTION	3
1.1. Background of the Project	3
2. OBJECTIVE, APPROACH AND SCOPE OF SEMI-ANNUAL MONITORING.....	3
2.1 Objective of the Social Monitoring Report	3
2.2 Scope of Social Safeguard Monitoring:	3
3. OVERALL PROJECT PROGRESS AND STATUS.....	4
3.1 Physical progress	4
3.2 Social Safeguards Planning and Documentation	6
3.2.1 Submission of Due Diligence Report (DDR) of Recon-3:.....	6
4. SOCIAL SAFEGUARD MONITORING PARAMETERS.....	7
5. IMPLEMENTATION ARRANGEMENT.....	9
6. PROJECT IMPACT AND SOCIAL ACTIVITIES	10
6.1 Grievance Redress System and Mechanism.....	10
6.2 Redressed of Grievances	10
6.3 Current Status of GRM	10
7. MONITORING AND REPORTING ARRANGEMENTS	11
7.1 Social Safeguard Compliance Status	11
7.1.1 Resettlement Plan.....	11
7.1.2 Resettlement and Compensation.....	12
7.1.3 Livelihood and Employment.....	12
7.2 Monitoring Results/Finding	12
7.2.1 Consultation and information disclosure	13
7.3 Issues Identified During Reporting Period	13
7.4 Corrective Actions and Actions to be Undertaken	14
8. COMPLIANCE STATUS WITH ADB LOAN COVENANTS	14

LIST OF TABLES

Table 3-1: Remaining subprojects and physical progress under Recon-1	4
Table 3-2: Physical Progress under Recon-2 Subprojects.....	5
Table 3-3: Physical Progress in retrofitting sub- projects under DRSP	5
Table 3-4: DDR under preparation and Status.....	7
Table 4-1: Monitoring Parameters and Status	7
Table 6-1: GRC status as of June 2021 under Recon-1	10
Table 6-2: GRC formation status as of June 2021 under Recon 2.....	10
Table 7-2: Loss of Income and their impact due to Reconstruction of School's Buildings	13
Table 8-1: Compliance Status with the ADB Loan Covenants	14

LIST OF ANNEXES

Annex 1: Project safeguard support team.....	16
Annex 2: Photographs	20
Annex 3: Checklist of the Monitoring activity carried out by Safeguards Desk (Sample only) ...	23
Annex 4: Meeting Minutes regarding consultations.....	33

1. INTRODUCTION

1.1. Background of the Project

1. The earthquake in April 2015 in Nepal caused 8,700 deaths and 22,500 suffered severe injuries. There was a physical damage costing more than \$7 billion mostly in 14 of the country's 77 Districts. The Government of Nepal (GoN) requested and received support from a number of development partners, including the Asian Development Bank (ADB), to address the impacts of the damages. The National Reconstruction Authority (NRA) and the Ministry of Education, Science and Technology (MOEST) through central level project implementation unit [CLPIU (Education)] are wholly responsible for the implementation of ADB-financed projects, as agreed jointly between the borrower and ADB, and in accordance with the policies and procedures of the government and ADB. Monitoring of project performance, outcome and financial closure will be until 31 March 2023 including preparation of project completion report. The Disaster Resilience of Schools Project (DRSP) was conceptualized to support in disaster risk reduction and meeting the school reconstruction needs. The Project aims in achieving School Sector Development Plan (SSDP) objectives to improve the quality & access to school education and management. School safety is identified as an explicit objective in the 2016-2023 SSDP being implemented by the Ministry of Education, Science, and Technology (MoEST), GoN.

2. The project will improve disaster resilience of school infrastructure and communities in 14 districts (Kathmandu, Bhaktapur, Lalitpur, Kavrepalanchok, Sindhuli, Sindhupalchowk, Okhaldhunga, Ramechhap, Dolakha, Nuwakot, Dhading, Gorkha, Rasuwa and Makwanpur) of Nepal. The project will finance the school infrastructure investments, disaster risk management, and institutional strengthening and capacity building. More specifically, the project has taken initiative to upgrade at least 130 district schools through reconstructing and 180 schools through retrofitting the damaged buildings.

3. The project has covered Kathmandu, Bhaktapur, Kavrepalanchok, Sindhuli, Sindhupalchowk, Okhaldhunga, Ramechhap and Dolakha in Recon1 (First Batch) with 66 schools while Nuwakot, Dhading, Gorkha and Makwanpur has been added in Recon2 (Second Batch) with 106 schools.

4. Altogether, there are 209 schools (under Recon1, 2 and 3) that have been identified for the reconstruction and 168 school projects have been identified for the retrofitting works. All these schools are spread over the 14 most earthquake affected districts. The construction for the 66 schools under Recon1 are substantially completed without any safeguards issue. Similarly, construction of 106 schools under Recon2 is ongoing. Construction activity in 143 schools selected for retrofitting are started during this bi-annual gradually after tendering. Altogether 9 contract packages have been planned for tendering of schools for retrofitting which has been started with awarding of packages and construction is ongoing. However, 3 schools selected for retrofitting are under Disaster and Risk Management (DRM) consultant for its monitoring and supervision. Whereas, minor damage buildings of 22 schools under Recon3 are also proposed for retrofitting and are yet to be awarded.

2. OBJECTIVE, APPROACH AND SCOPE OF SEMI-ANNUAL MONITORING

2.1 Objective of the Social Monitoring Report

5. The objective of the Semi-Annual monitoring report is to assess progress on safeguard plan implementation of the subprojects as per safeguard planning document, implementing actions and provisions specified in resettlement framework, RP including DDRs, grievance redress procedure, impact assessment, public consultation and disclosure process.

2.2 Scope of Social Safeguard Monitoring:

6. The scope of social safeguard monitoring are as follows;

- Ensure screening procedures, impact assessment, safeguard planning and implementation as per Resettlement Framework endorsed by the government.
- Ensure the timely and adequate implementation of provisions specified in resettlement framework for each school will prepare screening report, and required safeguard planning documents (DDR, RP etc.) and will submit these documents to ADB for approval and clearance and will ensure that all activity comply with the applicable national and local laws and regulations, in addition to SPS 2009.
- The NRA and CLPIU ensures that all required budget and human resources are available in a timely manner to ensure payment of all entitlements prior to displacement of affected persons.
- Further, NRA and CLPIU will ensure that all construction-based contracts are implemented in an environmentally and socially sustainable and responsible manner.
- The CLPIU and DLPIUs will be responsible to ensure mitigation measures are implemented on time and reported to ADB in the project progress reports with non-compliances, if any.

3. OVERALL PROJECT PROGRESS AND STATUS

3.1 Physical progress

7. The total physical progress of accomplished construction work under Recon1 is 89.39%. Of which, out of 66 schools, 58 schools are completed substantially and handed over to the concern School Management Committees (SMCs) after complying all the social safeguards, environmental, health and safety issues.

8. Construction activities are still ongoing in the remaining 8 schools (7 schools in Okhaldhunga and 1 school in Sindhuli District). The progress is quite varied from school to school however, structural works and outer plaster has been completed significantly. The major ongoing works are construction of retaining wall, stone masonry wall, installation of doors, and windows, construction of apron drain and breast wall, and stair case pavement works etc.

9. Construction works of 106 schools under Recon2 is ongoing.

10. Moreover, due to the novel corona virus (COVID-19), the construction activities of schools under Recon-1 and Recon-2 including retrofitting works have been hampered in all DRSP districts. However, with the efforts of CLPIU, DLPIU and the DSC team, there has been an average physical progress under remaining 8 schools (7 school in Okhaldhunga district and 1 school in Sindhuli district) under Recon1 is 77.36%. The details of physical progress are presented in the following table.

Table 3-1: Remaining subprojects and physical progress under Recon-1

S.N	School	District	% Physical Progress
1	Sunkoshi SS	Okhaldhunga	73.71
2	Gramodaya Yugkabi Siddhicharan SS	Okhaldhunga	83.00
3	Katunje SS	Okhaldhunga	68.00
4	Fulmati SS	Okhaldhunga	62.24
5	Jalpa SS, Kalimati	Okhaldhunga	94.50
6	Himaganga SS	Okhaldhunga	54.50
7	Jalpa SS, Tarkerabari	Okhaldhunga	86.00
8	Chilaune Danda SS	Sindhuli	97.00
Total remaining subprojects : 8			
Average Progress: 77.36%			

Table 3-2: Physical Progress under Recon-2 Subprojects

S.N	District	No. of school	Progress in %			Remarks
			Lowest	Highest	Average	
1	Okhaldhunga	13	9	24	16.3	Highest in Panchakanya SS and Lowest in Patle SS
2	Sindhuli	15	36	94	58.86	Highest in Prabhat SS and Lowest in Kamala SS
3	Ramechhap	17	29	72	50.02	Highest Khanteshwor SS and lowest in Kalika SS
4	Dolakha	11	21.5	59	45.36	Highest Janajyoti SS and lowest in Lapilang SS
5	Kavreplanchwok	9	19	73	57.89	Highest Sarbamangala SS and lowest in Srikhandapur SS
6	Sindhupalchwok	8	65	93	81.25	Highest Rameshwor SS and lowest in Bhadrakal SS
7	Bhaktapur	7	52	80	61.43	Highest Adarsha Ajadh SS and lowest in Bagiswori SS
8	Kathmandu	8	58	90	72.81	Highest Janaudhhar SS and lowest in Pasupati Mitra SS
9	Nuwakot	6	64	75	70.01	Highest Shree Chandi SS and lowest in Shree Krishna SS
10	Dhading	5	59	88	78.8	Highest Shree Prakash SS and lowest in Shree Bal Mandir SS
11	Gorkha	4	42	65	57.75	Highest Siddhartha SS and lowest in Suryodaya SS
12	Makwanpur	3	76	91	84.33	Highest Vyas SS and lowest in Bal Ujjwal SS
	Total	106				
	Average Progress	55.91				

Table 3-3: Physical Progress in retrofitting sub- projects under DRSP

S.N	District	No. of School	Physical Progress in %			Remarks
			Lowest	Highest	Average	
1	Sindhuli	10	0.00	71.00	41.3	Highest in Shree SS, Chilaune Dada and lowest in Pachrukhi SS
2	Ramechhap	4	29	85.28	57.32	Highest in Sthanapati SS, and lowest in Kalidevi SS
3	Dolakha	4	11	31	20.5	Highest in Mahendrodaya SS, and lowest in Ajadi SS
4	Sindhupalchok	2	2	21	11.5	Highest in Rajeshwori SS, and lowest in Jankalyan SS
5	Kavrepalanchok	7	0	75	44.29	Highest in Dapcha SS, and lowest in Mahakali SS
6	Bhaktapur	3	6	36	19.33	Highest in Devi SS, and lowest in Mahendra Gram SS
7	Kathmandu	19	0	57	8.47	Highest in Mahendra Bouddha SS, and lowest in Kavresthali SS
8	Lalitpur	3	8	13	11	Highest in Shramik Shanti SS, and lowest in Phulchoki SS

S.N	District	No. of School	Physical Progress in %			Remarks
			Lowest	Highest	Average	
Total Schools: 52						
Average Progress: 25.18%						

3.2 Social Safeguards Planning and Documentation

11. In terms of Social Safeguard perspective, followings are the key activities performed under Social Safeguards component during the biannual period.

3.2.1 Submission of Due Diligence Report (DDR) of Recon-3:

12. During this biannual period, following achievement has been done in terms of preparation and submission of DDR.

13. The Design and Supervision Consultant (DSC) recruited under the DRSP has reviewed the Due Diligence Report prepared for each school, Master Plan, Bill of Quantity (BoQ), and bidding documents for the 37 schools planned to be undertaken in Recon3 (Third Batch) during this biannual. The DSC has prepared the design and drawings, BoQ, and bidding documents for Recon3 and Retrofitting 3 to 9 packages, and provide assistance for bid evaluation, and supervise all Recon1 and 2 and Retrofitting civil works contract packages.

i) DDR Recon3, Package 1: In this Package, total 14 Secondary Schools (SS) from different districts have been selected. Out of these, 12 schools (Shree Bal Bikash SS, Bal Uddhar SS, Bansbari SS, Vijaya Memorial SS, Dhumra Barah SS, Jana Uddhar SS, Jhor Mahankal SS, Kirtipur SS, Mansingh Dharma SS, Purano Guheshwori SS, Saraswati SS, and Siddhi Ganesh SS) from Kathmandu district, 1 school (Mahendra Gram SS) from Lalitpur District and 1 school (Ganesh SS) from Bhaktapur District. The DDR of Recon 3, Package-1 has been prepared and submitted to the CLPIU by DSC in January 2021.

ii) DDR Recon3, Package 2: In this package, total 9 schools have been selected. Out of 9, 5 schools (Adarsha SS, Bageshwori SS, Machhindra SS, Mahalaxmi SS, and Pashupati SS) from Dhading District and 4 schools (Bhawani SS, Kalika SS, Shree Rastriya SS and Shree Surya SS) from Makwanpur District. The DDR of Recon 3, Package 2 have been prepared and submitted to the CLPIU by DSC on March 10, 2021.

iii) DDR Recon3, Package 3: Under this Package, total 14 schools have been selected. Out of these, 3 schools from Kavrepalanchowk district (Gokule SS, Shree Janakalyan SS & Kalidevi), 7 schools from Sindhuli district (Gaumati Namuna SS, Jalkanya SS, Devasthan SS, Shree Madhyamik Vidhyalaya, Majuwa Dobhan, Janata SS, Shree Kamala SS & Phikkal SS), and 1 school (Tripurasundari SS) from Sindhupalchowk district. Similarly, 3 schools (Bhimeshwar Rudra SS, Himganga SS & Shree Chandeshwori SS from Ramechhap district respectively. The DDR of Recon-3, Package 3 have been prepared and submitted to the CLPIU by DSC on March 26, 2021. Overall, there are total 37 schools have been selected under Recon-3 for reconstruction and retrofitting purpose.

14. **DDR for Repackaging of Retrofitting Packages 3, 4, 5, 6, 7, 8, and 9:** In these, Packages, Retrofitting Package-3 has 14 schools selected, such as 2 schools from Bhaktapur District and 12 schools from Kathmandu District, similarly, in Retrofitting Package-4 which include 9 schools. Out of 9, 3 schools from Lalitpur District and 6 schools from Kathmandu District. The aforesaid Packages were reshuffled and updated during the biannual. On the other hand, Retrofitting Package-5 comprises 19 schools from Nuwakot District, Package 6 comprises 21 schools from Sindhuli and Okhaldhunga Districts, Package 7 comprises 18 schools from Ramechhap and Dolakha Districts, Package 8 has 15 schools from Ramechhap and Dolakha Districts, and Package 9 comprises 19 schools from Dhading and Gorakha Districts. Overall, there are in total 114 schools from different Districts under those Packages.

DSC has updated and repackaged DDRs of the retrofitting schools and submitted to the CLPIU by DSC on March 2, 2021.

Table 3-4: DDR under preparation and Status

Package	Activities	Impact upon	RP/DDR Status
I. Reconstruction of Heavily Damaged Schools			
RECON-1 Package-1 Package-2	Reconstruction of in total 29 Schools (package-1: 18, and package-2: 11)	No LAR impacts. N/A	Submitted. Updated DDR to ADB approved
RECON-2 Package 7, 8, & 9	Reconstruction of in total 61 Schools (package-7: 20, package-8: 22 and package-9: 21)	No LAR impacts. N/A	Submitted. Updated DDR to ADB approved
RECON-3	Site investigation, preparation of DDRs for Packages 1, 2, and 3 (total 37 schools)	No LAR impacts. N/A	Submitted. Updated DDR to ADB approved
II. Retrofitting			
Retro- Package 3, 4, 5, 6, 7, 8, and 9	Updating and repackaging of DDR for total 114 schools	No IP impacts. Due diligence reports	DDR is prepared and submitted to ADB. RAP is under preparation for 22 business activities established in 5 schools under package 3 and 4.

4. SOCIAL SAFEGUARD MONITORING PARAMETERS

15. The following parameters have been applied during social safeguard monitoring:

Standard monitoring checklist/indicators have been developed and provided with orientation training conducted both at DRSP head office and at respective sites during field visits to all the Safeguards and GESI monitors (SM) for monitoring social safeguard activities. The Following table gives the overall status of monitoring progress.

Table 4-1: Monitoring Parameters and Status

S. N.	Parameters	Status	Remarks
A. Preconstruction activities and resettlement plan activities			
1.	Assessment of new resettlement impacts due to changes in project design (if required)	RP is under preparation for 22 shops to be affected due to retrofitting of existing 5 school building of the Kathmandu Valley.	Construction activity limited to existing school premises in most of the cases.
2.	Land for school construction owned by school (existence of land ownership certificate/ User's Right document)	Implementing schools have provided either LOC or User's Right Document from local bodies.	
3.	Additional land acquired (if any) through voluntary donation; verification of donation, Deeds and LOCs	N/A	
4.	Preparation/updating of resettlement plan(s) based on final detail design	Updating and preparation of RP for temporary displacement of 22 business activities under retrofitting package 3 and 4	
5.	Disclosure of updated resettlement plan to affected people and communities	To be disclosed	22 business activates temporary during retrofitting

S. N.	Parameters	Status	Remarks
6.	Submission for review and approval of the final/ updated resettlement plan from ADB	Suggestions received from ADB on RP submitted by DSC	DSC updating RP
7.	Disclosure of approved final RP(s) in ADB and EA websites	To be disclosed	
8.	Establishment of grievance redress committee	GRCs are established in total 138 schools (66 schools under Recon1 and 72 schools under Recon2). Establishment to be continued for remaining schools.	
9.	Number of cases registered with the GRC, level of jurisdiction (first, second, and third levels), number of hearings held, decisions made, and the status of pending cases;	No any grievances recorded during reporting period due to COVID-19 pandemic	Grievance record books maintained by all GRCs
10.	Lists of cases in process and already decided upon	No cases due to pandemic	
11.	Verification of displaced persons census list; assessment on compensation and assistance, and readjustment	Ongoing	
12.	Impacts on livelihoods	22 business activates temporary during retrofitting of existing school buildings	
13.	Preparation/selection of the temporary relocation sites for the hawkers	N/A	
B. Resettlement plan implementation			
1	Payment of compensation to displaced persons	After finalization of RP	
2	Special measures for vulnerable groups	N/A	
3	Reinstallation of public utilities	N/A	
4	Reestablishment of businesses	Retrofitting of affected building is ongoing and shops will be reestablished after completion of retrofitting activities.	
5	Temporary relocation of hawkers and vendors	No hawkers and vendors existed in any site	
C. Indigenous Peoples			
1	Impact upon indigenous people	Children of the indigenous peoples and non-indigenous peoples both follow the similar modes of educational system. Implementation of the project activities neither directly nor indirectly affects the dignity, human rights, livelihood systems, or culture of indigenous people.	Till date there is no impact upon indigenous people.
D. Social measures during construction as per contract provisions			
1	Prohibition of employment or use of children as labor	No under children engaged as labour in any site	

S. N.	Parameters	Status	Remarks
2	Prohibition of forced or compulsory labor	No forced labour observed	
3	Ensure equal pay for equal work to both men and women	Being complied	
4	Implementation of all statutory provisions on labor like health, safety, welfare, sanitation, and working conditions	Being complied	
5	Maintenance of employment records of workers	Contractors have maintained workers employment record.	

16. **Land Acquisition and Management:** All schools have already managed adequate land as per the requirement for new proposed schools building for construction with evidence of land ownership certificates and user right documents received from the local governments. Land acquisition issues had addressed in DDR reports.

5. IMPLEMENTATION ARRANGEMENT

17. National Reconstruction Authority (NRA) is the project's Executing Agency (EA), and Central Level Project Implementation Unit (CLPIU) is the implementing agency (IA). District Level Project Implementation Units (DLPIUs) have been established under CLPIU in each project district for the implementation and monitoring of the project at district level. Further, Design and Supervision Consultant (DSC) is in place under CLPIU for the design, monitoring & supervision of individual schools proposed for reconstruction.

18. Resettlement framework is in place in order to provide policy and procedural guidance to avoid, minimize and mitigate involuntary resettlement impacts; and in identifying institutional requirements for preparing social safeguard planning documents for subprojects based on detailed design. The framework also provides guidelines for updating safeguard planning documents. The government has endorsed the resettlement framework.

19. Similarly, Design Supervision Consultant (DSC) Environment Safeguards Specialist/Expert has already been mobilized have prepared safeguard monitoring checklists covering all the issues mentioned in DDR. Moreover, Safeguards and GESI Monitors (one in each project district) have started monitoring for the safeguards issues during construction. The safeguard monitor at DLPIUs have been monitoring compliance by using standard monitoring checklist prepared by safeguards experts for each individual school. Further, the monitors have maintained daily safety observation checklists and instructed contractor for any rectification required in maintaining safety, occupational health of labour as well as any issue related to social safeguards. Also, the monitors are filling the checklist prepared for safeguards desk on a monthly basis for each under construction schools and monthly progress reports are being submitted.

20. Safeguard monitors from each DLPIUs also supported in preparing DDRs of the schools selected for retrofitting during this reporting period. The monitors have carried out preliminary assessment in case of land ownership status of each school selected for retrofitting. The project safeguard team supporting the DRSP (L-3702 NEP) is presented in the Annex 1.

6. PROJECT IMPACT AND SOCIAL ACTIVITIES

21. Regular consultations and meetings are being held by DLPIU and DSC with stakeholders and School Management Committee (SMC) and other stakeholders to facilitate implementation of social safeguards component. Besides these, the other social activities such as campsite management, health and safety measures, wage rate to construction workers and issue of child labor have been regularly monitored. Orientation on awareness in maintaining compliances of the social activities as per social safeguard documents of the project was provided to contractor. Further, Standard Operating Procedure (SOP) prepared by NRA in order to avoid and minimize risk from COVID-19 pandemic has been distributed and oriented contractor in order to follow strictly during the construction.

6.1 Grievance Redress System and Mechanism

6.2 Redressed of Grievances

22. There were neither significant grievances nor any issues recorded under GRC-1, GRC-2 and GRC-3. However, some major issues were raised in terms of preparation the DDR under Recon-3 Package 1, package-2 and package 3 that is given below.

6.3 Current Status of GRM

23. Under Recon1, out of 66 schools 58 schools are handed over and 7 schools of Okhaldhunga district and one school (Chilaune Danda SS from Sindhuli district) is ongoing. However, in Chilaune Danda SS, almost all building construction work is substantial completed and only work of land slide is under construction. In terms of the establishment of GRC-1, all 66 schools have established GRC1. Similarly, under Recon-2, total 106 subprojects are under implementation. Out of these, as of June, 2021, 72 Grievance Redressing Committees at school level (GRC1) and 6 GRC-1 out of 51 Retrofitting schools have also been established. In addition, 8 districts (Okhaldhunga, Sindhuli, Kavrepalchok, Sindhupalchok, Bhaktapur, Gorkha, and Nuwakot) have established GRC-2 under Recon1, Recon2 and Retrofitting Subprojects and 4 districts (Kathmandu, Ramechhap, Dhading and Makawanpur) have not reported yet. Any grievances raised at the schools has been resulted by GRC1. No any grievances forwarded to GRC2 & 3 except in case of Rajylaxmi SS of Okhaldhunga district. Details of GRC-1 and GRC-2 is given in the following tables.

Table 6-1: GRC status as of June 2021 under Recon-1

Sn.	District Name	Number of ongoing schools	Formation of GRC1 at School level	Formation of GRC2 at DLPIU level	Formation of Safeguards Desk at DLPIU	Remarks
1.	Sindhuli	1	1	Established	Established	58 completed schools are not included
2.	Okhaldhunga	7	7	Established	Established	
	Total			2	2	

Table 6-2: GRC formation status as of June 2021 under Recon 2

Sn.	District Name	Number of Recon2 schools	Formation of GRC1 at School level	Formation of GRC2 at DLPIU level	Formation of Safeguards Desk at DLPIU
1.	Sindhuli	15	13	Established	Established
2.	Okhaldhunga	13	0	Established	Established
3.	Gorkha	4	3	Established	Established
4.	Makwanpur	3	3	Established	Established
5.	Dhading	5	5	Established	Established
6.	Nuwakot	6	6	Established	Established

Sn.	District Name	Number of Recon2 schools	Formation of GRC1 at School level	Formation of GRC2 at DLPIU level	Formation of Safeguards Desk at DLPIU
7.	Kavrepalanchowk	9	9	Established	Established
8.	Dolakha	11	11	Established	Established
9.	Ramechhap	17	0	Established	Established
10.	Kathmandu	8	7	Established	Established
11.	Bhaktapur	7	7	Established	Established
12.	Sindhupalchowk	8	8	Established	Established
	Total	106	72	12	12

7. MONITORING AND REPORTING ARRANGEMENTS

24. Regular monitoring activities are being carried out for assessing safeguard plan implementation of the subprojects and its progress and identifying potential difficulties and problems during the construction of school buildings under Recon-1, Recon-2 and Retrofitting project schools. Safeguards and GESI monitors assigned in each project district have been involving in monitoring for the GESI and Social aspects. Safeguard monitors have carried out 253 times field visit during the reporting period for identification of potential difficulties and problems and to monitor safety issues during construction. Further, the monitors inspected for the land ownership issue, involuntary resettlement, influence upon indigenous people, and construction of disable friendly toilets, installation of ramps, and incinerator, installation of information boards as well as signboards related to health and safety during construction as well as OHS related to COVID-19. Further, monitoring to avoid child labor, employment opportunity to locals and equal wages to women etc. have also been carried out.

25. Internal monitoring at school level have been under taken by the DLPIUs with the support from safeguards monitors of DSC visiting every schools every month for monitoring frequently using a checklist prepared by DSC and has been submitted social safeguards performance through quarterly progress report. Similarly, package wise DDR reports for all schools selecting either for reconstruction or retrofitting has been prepared and in place. Package wise DDRs for 66 school under Recon1, 106 schools under Recon2 and 59 new schools selected for retrofitting are in place. DDR reports have assessed schools requiring resettlement or relocation issues.

7.1 Social Safeguard Compliance Status

7.1.1 Resettlement Plan

26. Resettlement Plan (RP) is under preparation. In this regard, two schools under package 3 (Nepal Adarasha Secondary School, Shrama Rastrya Secondary School of Kathmandu) and three schools under package 4 (Bal Udhhar SS, Nepal Rastriya Nirman SS, of Kathmandu and Shramik Shanti SS of Lalitpur) comprise ongoing 22 business activities respectively that are likely to be affected due to retrofitting of the existing school buildings. The business owners will be affected temporarily by the disruption of their business caused by retrofitting of school's buildings and its impact on their income.

27. In terms of preparing the RP, the DSC safeguard team had carried out a field observation to ensure the impact on displacement, and loss of incomes /livelihoods of private business owners due to retrofitting activities within the school's boundary. In spite of the visit, Baluddhar Secondary School, Shram Rastriya and Nepal Rastriya Secondary School were visited at Kathmandu district. During field observation, discussion was made among with SMC's members and the business owners about their livelihoods and socio-economic impacts and given instruction to the SMCs to provide necessary documents as require. Remaining schools are to be planned within in July, 2021 for observation and RP will be developed if the pandemics situation caused by COVID-19 returns to normal. The RP is

expected to be completed by August 2021.

7.1.2 Resettlement and Compensation

28. DRSP has not needed to paid any compensation for the land, because they have own land for the construction of schools. The DDR Part-2: RP emphasizes that compensation should enable project-affected people to maintain the existing to better standard of living. RP compensation and mitigation measures include the compensation for business and shops that experience complete closure during construction period. Preparation of RP for Retrofitting 5 schools of (Kathmandu 4 and Lalitpur) is ongoing. The RP identified impacts and estimated shifting assistance cost and income restoration assistance. The business loss AP will submit all legal testimonies (MOU, business registration) and receive shifting assistances.

7.1.3 Livelihood and Employment

29. Total 22 businesses were running under 5 schools in Kathmandu and Lalitpur districts (Kathmandu, 4 and 1 at Lalitpur districts) under Retrofitting Subprojects. as per the income after deduction of expenditures, cost is calculated based upon the information received from 18 business owners of 3 schools (Baluddhar SS, Shram Rastriya SS and Nepal Rastriya SS), based on those 22 businesses will loss about NPR 34,357,000.00. This figure of amount may be changed while final RAP will be prepared and is planned to be prepared within August 2021. Now all businesses are shifted from existing places. Required information is under collection. Details will be presented in Resettlement Plan.

30. In terms of generating employment under this project as observed during field visit of the social safeguard team and the information from the technical team of DSC, in an average 50% labor are placed in each subproject. Whereas, the local labors are found about 30% working as temporally and about 20% of permanently basis during constriction period. Of which, the composition of labor shown as skilled labour are 20% and unskilled are 80% from the local community during the construction period of the project. In this regard, to get exact picture, the DSC safeguard team will develop a checklist in upcoming month and will be provided to the DLPIU and also will included in Management Information System (MIS) under DSC that may support to analyze the information related to this.

7.2 Monitoring Results/Finding

31. Up to the reporting period, the implementation of DDR together with the master plan of each sub-project is continuing. The impacts are avoided by limiting the construction activity with the boundary specified by the master plan and land ownership of the individual school. The safeguard team has been working closely with construction supervision team to avoid the adverse impact. The grievances related to social safeguard is treated immediately within the project entitlement framework and the numbers of grievances related to social safeguard are few and insignificant. The assessment, monitoring, evaluation, and reporting of the safeguard activities has been undertake by the project team.

32. The monitoring and assessment / evaluation of the contractors' safeguard activities has been carried out by using formats specific to each project and visiting the sites during working hours. The format presents list of issues in one column for monitoring whereas monitor will note status of work, problems, mitigation measures adopted by the contractors etc. in the remarks column. Such information is being presented in the site visit report of the safeguards monitor. Therefore, safeguards monitors' site visit report has been a basis for consultant's monthly and quarterly report on Environmental and Social Safeguards. Moreover, Safeguards Desk established at each district have conducted monthly monitoring and the filled monitoring checklists (as a sample only) including meeting minutes are presented in the Annex section.

33. Further, Resettlement Action Plan is under preparation incorporating measured to address impact upon loss of businesses temporarily under retrofitting school buildings of

package 3 and 4 and included with the entitlements, assistance and benefits, provision of business loss, institutional arrangements, tasks and responsibilities of each level of the agencies involved in resettlement planning for the project. However, no significant adverse impacts and livelihoods were observed in local people but there is some business disruption of about 22shop/business owner rented on school buildings.

7.2.1 Consultation and information disclosure

34. A series of consultation meetings were carried out at school level during the construction of school buildings. The participants during the consultation meetings are SMC members, contractor's representatives and school teachers. Especially instruction and suggestions were provided to contractor in order to maintain safeguards and safety especially during construction. The meeting minutes (as a sample) of such consultations is presented in the Annex section. Further, consultation both formal and informal were carried out during the preparation of Resettlement Plan (RP) for the loss of businesses temporarily under retrofitting school buildings of retrofitting package 3 and 4.

35. Consultation were conducted using questionnaire and checklists developed for the collection of further required information in order to accomplish RP. However, RP is under preparation and is yet to be disclosed.

7.3 Issues Identified During Reporting Period

36. Loss of Income due to Reconstruction of School's Buildings and their Impact: According to information gathered during data collection for the preparation of the Resettlement Plan, some business owners will lose income due to disruption of business or employment, which may have an impact on their livelihoods, due to the construction or reconstruction of school buildings, primarily in retrofitting subprojects.

Table 7-1: Loss of Income and their impact due to Reconstruction of School's Buildings

Activities	Existing scenario	Remarks
Loss of residential and commercial structures and other assets and mitigation measures	No impact	
Loss of income/ livelihood due to disruption of business, land or employment	Under the Retrofitting Subprojects, a total of 22 firms were operating in Kathmandu and Lalitpur districts (4 schools in Kathmandu and 1 in Lalitpur). Cost is computed based on information provided by 18 business owners from three schools, after expenses have been deducted (Baluddhar SS, Shram Rastriya SS and Nepal Rastriya SS). As a result, 22 business will lose temporary during retrofitting. This number may fluctuate while the final Resettlement Plan is being prepared, which is expected to be completed by August 2021. All businesses have now relocated from their previous locations. The necessary data is being gathered.	
Loss of cultural and community structures/ public facilities (drinking water, foot trail etc.) or community forests and mitigation measures	Under Recon 1, 4 school had foot trail issues and were addressed in GRC -1	

Activities	Existing scenario	Remarks
Loss of crops, fruits and timber trees	No impact	

37. Further, the Adarsha Secondary School of Dhading District selected under Recon3 had proposed traditional graveyard of local Tamang community for the construction of new school building. The safeguards team had visited the site and arranged consultation meeting in presence of SMC, local government (ward representatives) and the concerned community stakeholders and locals to assure and to resolve the cultural issue that might be raised due to construction of school buildings during the preparation of DDR. After rigorous discussions, all the concerned stakeholders are agreed to provide existing land of graveyard to the Adarsha Secondary School for the construction of all infrastructures as planned in master plan prepared by the DSC/DRSP. The consultation meeting minutes is presented in the Annex section.

7.4 Corrective Actions and Actions to be Undertaken

38. Safeguards team of DRSP will undertake corrective actions to fill the gaps identified during this biannual and will focus in the next biannual report are as follows;

- Meeting frequency GRC1 should be increased in order to resolve and improve working condition;
- Considering issues identified in approved DDR during the time of project implementation;
- Status of shifting of 22 shops to be displaced temporarily for retrofitting of the existing school buildings of 5 schools under retrofitting package 3 and 4;
- Providing compensation payment based on the endorsed resettlement plan;
- Ensure all compensation paid to the owner or owner shifted to same location and reinstated their business;
- Keeping record of Implemented livelihood restoration plan for the affected business owners in reference to RP;
- Status of GRC recorded and state of resolution of grievances if any raised during the reporting period.

8. COMPLIANCE STATUS WITH ADB LOAN COVENANTS

39. Compliance status with the ADB loan covenants have been monitored according to the indicators provided in the ADB loan covenants. The findings for compliance status with the ADB loan covenants presented in the following

40.

41. **Table 8-1.**

Table 8-1: Compliance Status with the ADB Loan Covenants

Indicators	Issues	Activities	Compliance Status	Remarks
Human and financial resources to implement safeguard requirement	DRSP should arranged available manpower, financial budget for proper implement of the project and completely implement the EMP.	DRSP contract with different construction agency whose has sufficient manpower, financial support and other related resources for the implementation of EMP.	Complied partly	Both human and financial resources management follow the ADB and safeguard requirements.

Indicators	Issues	Activities	Compliance Status	Remarks
Safeguards related provisions in bidding document of works and work contracts	Comply with the measures and requirements related to the contractor set forth in the EMP, make available budget for all such environmental and social measures.	-	Complied properly	-
Safeguard Monitoring and Reporting	Any anticipate results that were not considered in the RF and the EMP promptly inform ADB and proposed for mitigation in corrective action plans The monitoring and the reporting would be completed based on any potential breach of compliance with the measures and requirements set forth in the EMP	Reviewed the EMP provided in the ESMF all compliance status prepared based on selected indicators provided in the checklist.	Properly Complied	Safeguard monitoring and reporting complied
Labour Standard	Comply with all applicable labor law, treaty obligations of the borrowers and child labor law of Nepal. Provided safe working condition for male and Female workers. Carry out HIV/Aids and Human trafficking presentation and awareness complains in the campsites and corridor of influences.	With the respective stakeholders by DRSP and Social Safeguard and Environmental expert	Properly complied	

Annex 1: Project safeguard support team

Sn.	Name	Designation/Office	Office no.	Email Address	Roles	
1. CLPIU						
1.	Youb Raj Paudyal	Deputy Project Director, CLPIU		yrpudyal@gmail.com	Implementing agency and will look after the overall safeguards compliance of the project.	
2.	Udhab Nepal	Civil Engineer, CLPIU		Edhab73@gmail.com		
3.	Suraj Parajuli	Engineer, CLPIU		surajparajuli327.sp@gmail.com	Environment Safeguards Focal Person	Safeguards Desk comprising focal persons at CLPIU will organize routine meeting at central and local levels, respectively, to review safeguard compliance performance, emerging issues, agree for corrective actions, and coordinate with technical team/contractors to implement them.
4.	Kiran Kumari Lekhak	Section Officer, CLPIU			GESI/Social Safeguards Focal Person	
2. Name of DLPIU Unit Chief						
1.	Arjun Rajamajhi	Kathmandu	01-5242164	arjuneji5@gmail.com	GRC2-Chair	To support and resolve complaints/grievances as quickly as possible at the local level through a process of consultation; and, if that is not possible, to provide clear and transparent procedures for appeal.
2.	Guna Raj Pokharel	Lalitpur	01-5538417	pkrl.gunaraj@gmail.com	GRC2-Chair	
3.	Bharat Bahadur Shrestha	Bhaktapur	01-6614401	shresthabb2001@yahoo.com	GRC2-Chair	
4.	Yuba Raj Bagale	Dhading	010-521402	bagaleyb@gmail.com	GRC2-Chair	
5.	Dina Nath Gautam	Nuwakot	010-560347	dngreddhankuta@gmail.com	GRC2-Chair	
6.	Bishnu Prasad Mishra	Gorkha	064-420105	mishrabp53@gmail.com	GRC2-Chair	
7.	Badri Bahadur Pathak	Makawanpur	057-520869	bpathak071@gmail.com	GRC2-Chair	
8.	Dwarika Prasad Pokharel	Kavrepalnchowk	011-490117	dwarikapokharel164@gmail.com	GRC2-Chair	Responsible for monitoring compliance by using standard monitoring checklist prepared by ES for each individual school. The DLPIU will verify and submit safeguard monitoring report in a standard format to CLPIU and ADB. The reports will contain summary of work progress during the reporting
9.	Govinda Raj Sedhai	Rasuwa	010-540086	govindaraj.sedhai@gmail.com	GRC2-Chair	
10.	Yam Bahadur Khadka	Sindhupalchowk	011-620085	khadkaybk@gmail.com	GRC2-Chair	
11.	Dev Kumar Baral	Dolakha	049-421795	debkumarbaral@yahoo.com	GRC2-Chair	
12.	Shiva Kumar Sapkota	Sindhuli	047-520640	sapkotashiba@yahoo.com	GRC2-Chair	
13.	Nirmal Kumar Ghimire	Ramechhap	048-540549	nirmire@yahoo.com	GRC2-Chair	
14.	Bal Bahadur Karki	Okhaldhunga		balabahadurkarki@gmail.com	GRC2-Chair	

Semi-annual Monitoring Report January-June 2021

Sn.	Name	Designation/Office	Office no.	Email Address	Roles	
						period, quality of safeguards compliance, recommended corrective actions, and follow-up on corrective actions agreed in the last report.
	3. DLPIU engineers					
1.	Ajay Kr. Yadav	Engineer, DLPIU, Bhaktapur	01-6614401	ajay6456@gmail.com	Environment Safeguards Focal Person	Responsible for undertaking overall environmental social and GESI compliance in the subproject activities in the district.
2.	Shyam Babu Sha	Technical Assistant, DLPIU, Bhaktapur			GESI/Social Safeguards Focal Person	
3.	Rajendra Shrestha	Engineer, DLPIU, Dolakha	049-421105	rajendra.stha158@gmail.com	Environment Safeguards Focal Person	
4.	Pratik Raj Karki	Engineer, DLPIU, Dolakha			GESI/Social Safeguards Focal Person	
5.	Sovit Shrestha	Engineer, DLPIU, Kavrepalanchok	011-490117	sovit09086@gmail.com	Environment Safeguards Focal Person	
6.	Yadu Bikram Thapa	Engineer, DLPIU, Kavrepalanchok		yadu2038@gmail.com	GESI/Social Safeguards focal person	
7.	Sagar Paudel	Engineer, DLPIU, Kathmandu	01-5242164	poudelsagar47@gmail.com	Environment Safeguards Focal Person	
8.	Kopila Gyawali	Section Officer, DLPIU, Kathmandu			GESI/Social Safeguards focal person	
9.	Anil Kumar Yadav	Engineer, DLPIU, Sindhuli	047-520640	yanil0070@gmail.com	Environment Safeguards Focal Person	
10.	Durga Prasad Kafle	Section officer, DLPIU, Sindhuli			GESI/Social Safeguards focal person	
11.	Sabin Lama	Engineer, DLPIU, Okhaldhunga	037-520236	mrnibas09@gmail.com	Environment Safeguards Focal Person	
12.	Om Prasad Gautam	Section officer, DLPIU, Okhaldhunga			GESI/Social Safeguards focal person	
13.	Sundar Shyam Ghimire	Engineer, DLPIU, Ramechhap	048-540549	ssghimire1971@gmail.com	Environment Safeguards Focal Person	
14.	Kumar Prasad Subedi	Non Gazzetted First class, DLPIU, Ramechhap			GESI/Social Safeguards focal person	

Semi-annual Monitoring Report January-June 2021

Sn.	Name	Designation/Office	Office no.	Email Address	Roles
15.	Sher Bdr Pujara	Engineer, DLPIU, Sindhupalchwok	011-620085	sherp7@gmail.com	Environment Safeguards Focal Person
16.	Monika Joshi	Sub-Engineer, DLPIU, Sindhupalchwok			GESI/Social Safeguards focal person
17.	Indra Lal Maharjan	Engineer, DLPIU, Lalitpur	01-5538417	imaharjan55@gmail.com	Environment Safeguards Focal Person
18.	Bichari Prasad Adhikari	Section officer, DLPIU, Lalitpur			GESI/Social Safeguards focal person
19.	Baburam Devkota	Engineer, DLPIU, Gorkha	064-420105	baburamdevkota1@gmail.com	Environment Safeguards Focal Person
20.	Jyoti Thapa Magar	Sub-Engineer, DLPIU, Gorkha			GESI/Social Safeguards focal person
21.	Suman Pokhrel	Engineer, DLPIU, Nuwakot	010-560347	sumanp_1981@yahoo.com	Environment Safeguards Focal Person
22.	Bodhraj Pathak	Section officer, DLPIU, Nuwakot			GESI/Social Safeguards focal person
23.	Achut Raj Neupane	Engineer, DLPIU, Rasuwa	010-540157	neupane.achyut1990@gmail.com	Environment Safeguards Focal Person
24.	Manohar Dhakal	Sub-Engineer, DLPIU, Rasuwa.			GESI/Social Safeguards focal person
25.	Sandeep Adhakari	Engineer, DLPIU, Makwanpur	057-520869	ersaans@gmail.com	Environment Safeguards Focal Person
26.	Harichandra Sapkota	Section officer, DLPIU, Makwanpur			GESI/Social Safeguards focal person
27.	Nirmal Bogati	Engineer, DLPIU, Dhading	010-520124	nirvikalpa2013bg@gmail.com	Environment Safeguards Focal Person
28.	Sher Bahadur Khatri	Sub-Engineer, DLPIU, Dhading			GESI/Social Safeguards focal person
4. DSC-Safeguards Experts					
1.	Rikesh Chitrakar	Environment Safeguards Expert/KTM head quarter	01-5245144	chitrakar.rikesh@gmail.com	Implementation, monitoring and reporting of environmental safeguards works of DRSP Schools of L-3702 NEP
2.	Ratna Meher Bajracharya	Social Safeguards Expert/KTM head quarter	01-5245144	ratna.mehar.b@gmail.com	Guide and monitoring and supervision of social safeguards works of DRSP Schools of L-3702 NEP

Semi-annual Monitoring Report January-June 2021

Sn.	Name	Designation/Office	Office no.	Email Address	Roles
3.	Prakash Panday	GESI Expert/KTM head quarter	01-5245144	ppanday029@hotmail.com	Monitoring, supervision and implementation of GESI action plan of DRSP Schools of L-3702 NEP
5. DSC Safeguards and GESI Monitors					
1.	Ambika Ghimire	Sindhupalchok	9801860098	ambika.ghimire45@gmail.com	Supporting the project in implementing environmental and social safeguards requirements by educating, and creating awareness at school level and district level. Monitors are also responsible for the collection of required data and monitoring during the construction phase.
2.	Kapil Giri	Gorkha	9801877675	girikapil752@gmail.com	
3.	Sneha Khaling	Makwanpur	9801860028	snehakhaling02@gmail.com	
4.	Mingma Y. Sherpa	Ramechhap	9801877665	mingma155@gmail.com	
5.	Nabina Karki Gautam	Bhaktapur	9801860059	karkinabina99@gmail.com	
6.	Saru Pokharel	Kathmandu	9801860074	sarupokharel111@gmail.com	
7.	Pawan Thapa	Nuwakot	9801877654	thapapawan5311@gmail.com	
8.	Perina Pathak	Dhading	9801877664	perina.pathak15@gmail.com	
9.	Anjula Shrestha	Okhaldhunga	9801860053	anjula.cdes@gmail.com	
10.	Rojeena Rijal	Kavrepalanchowk	9801860069	rijalrojeena228@gmail.com	
11.	Deepa Katuwal	Sindhuli	9801860043	dipakatuwal15@gmail.com	
12.	Shova Subedi	Dolakha	9801860079	shova9.subedi@gmail.com	

Annex 2: Photographs



Fig. 1 & 2: Site barricading at Prabhat SS, Sindhuli Recon2



Fig. 3: Safety information board at Prabhat SS, Sindhuli_Recon2



Fig.4 :Safety sign board at Shree SS, Ladabhir_Recon2



Fig. 5 :First Aid box at Shree SS, Ladvir_Sindhuli_Recon2



Fig. 6 :Hand washing facility at Shree SS, Gadauli_Sindhuli Recon2

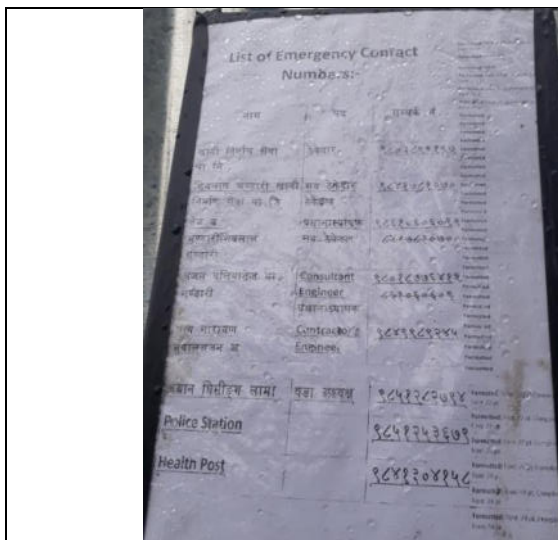


Fig. 7 :Emergency contact number established at Shree Sansari Mai SS_Sindhupalchowk Recon2



Fig. 8 :First Aid Box- at Shree Sansari Mai SS_Sindhupalchowk Recon2

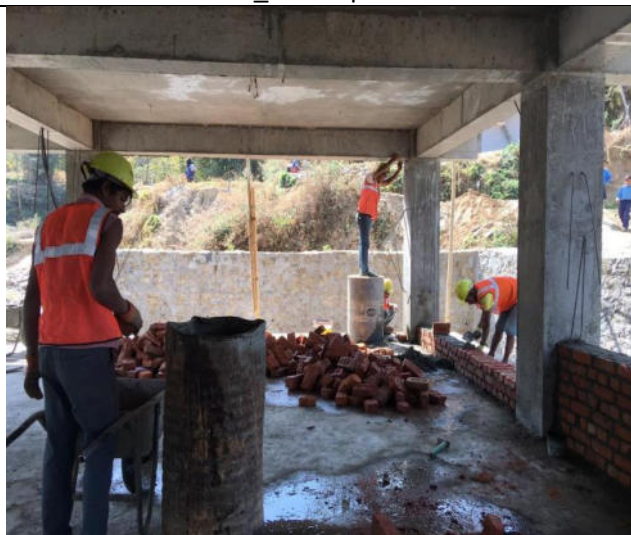


Fig. 9 :Workers with PPEs at a school in Nuwakot



Fig. 10 :Separate toilet for male and female at Sansari Mahendra SS



Fig. 11 :Labour camp of Siddhartha SS, Gorkha



Fig. 12 :Labour toilet at the Siddhartha SS, Gorkha



Fig. 13: Barricade at Kamala SS, Sindhuli



Fig. 14 :Labour Camp at Kamala SS, Sindhuli



Fig. 15 :Safety Signage and Covid Information Board at Shree Devi SS, Dolakha



Fig. 16 :Labour camp at Suryodaya SS, Gorkha



Fig. 17: Measuring body temperature by using thermal gun at Shree Janajagarn SS, Sindhuli



Fig. 18 :Handwashing facility at Shree Janajagarn SS, Sindhuli

Annex 3: Checklist of the Monitoring activity carried out by Safeguards Desk (Sample only)

Monthly safeguards Desk checklist filled for Shree Janajyoti SS, Dolakha

Monthly Checklist for Safeguards Desk-DRSP (Construction Phase)

Name of School : Shree Janajyoti Ma. Vj (50 DOHA JANA RECON2)

Location: Leptung

Sn.	Issues	Status		Remarks
		Yes	No	
1.	Building safe from landslide, erosion and no risky area existed close to the school area.	✓		
2.	No impact on forest and agricultural land.	✓		
3.	Drainage and surface runoff around the school managed.	✓		
4.	No water logging around the school.	✓		
5.	Physical safety barrier on slab edge, staircase barrier, and around the construction boundary in place.	✓		Instructed for complete site barricading and physical safety barrier on slab.
6.	Safety Sign boards, Emergency Phone Numbers, caution tape around under construction area in place.			Safety sign board on place.
7.	Good Housekeeping of construction material.	✓		
8.	Use of PPEs by labour.	✓		
9.	No occupational health and safety issues.	✓		
10.	Health and sanitation around the camp maintained.	✓		
11.	No child labour during construction.	✓		
12.	Female worker are provided with equal wage.			No female workers.
13.	Consultations with SMC and local community (Women, Poor, Dalits, IPs, disadvantage groups).	✓		
14.	First aid box in site.	✓		
15.	Waste from construction and from camps managed.	✓		
16.	Employment opportunity to local.			Local shops are benefited
17.	No Social and GESI issues.	✓		
18.	All raised grievances handled and resolved properly.			No grievance recorded
19.	Compensation paid for temporary acquired land.			No temporary acquired land
20.	Other issue, if any.		✓	

Sn.	Safeguards Members	Name/Signature/Office Stamp
-----	--------------------	-----------------------------

Page 1 of 2





Semi-annual Monitoring Report January-June 2021

Monthly safeguards Desk checklist filled for Bhringeshwori SS, Kotgaun, Ramechhap

Monthly Checklist for Safeguards Desk-DRSP (Construction Phase)

Name of School: Bhringeshwori SS (RAAP QHRT RECON2)
 Location: Kotgaun Date: 8th March 2021

Sn.	Issues	Status		Remarks
		Yes	No	
1.	Building safe from landslide, erosion and no risky area existed close to the school area.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.	No impact on forest and agricultural land.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.	Drainage and surface runoff around the school managed.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.	No water logging around the school.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.	Physical safety barrier on slab edge, staircase barrier, and around the construction boundary in place.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6.	Safety Sign boards, Emergency Phone Numbers, caution tape around under construction area in place.	<input type="checkbox"/>	<input type="checkbox"/>	Emergency number not found at site
7.	Good Housekeeping of construction material.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
8.	Use of PPEs by labour.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
9.	No occupational health and safety issues.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
10.	Health and sanitation around the camp maintained.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
11.	No child labour during construction.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
12.	Female worker are provided with equal wage.	<input type="checkbox"/>	<input type="checkbox"/>	No female workers
13.	Consultations with SMC and local community (Women, Poor, Dalits, IPs, disadvantage groups).	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
14.	First aid box in site.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Instructed to add medical supplies.
15.	Waste from construction and from camps managed.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
16.	Employment opportunity to local.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
17.	No Social and GESI issues.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
18.	All raised grievances handled and resolved properly.	<input type="checkbox"/>	<input type="checkbox"/>	No grievance till date
19.	Compensation paid for temporary acquired land.	<input type="checkbox"/>	<input type="checkbox"/>	
20.	Other issue, if any.	<input type="checkbox"/>	<input type="checkbox"/>	

Sn.	Safeguards Desk Members	Name/Signature/Office Stamp
1.	Safeguards Focal Person, DLPIU - DRSP :	
2.	Safeguards and GESI Monitors, PSC - DRSP:	
3.	Contractor's focal person for safeguards:	 

Page 1 of 2

Monthly safeguards Desk checklist filled for Shree Vyas SS, Makwanpur

Monthly Checklist for Safeguards Desk-DRSP (Construction Phase)

Name of School: Shree Vyas SS (107 MAUR VYAS RECON2)

Location: Kailash-6, Pakari

Date: 17 March 2021

Sn.	Issues	Status		Remarks
		Yes	No	
1.	Building safe from landslide, erosion and no risky area existed close to the school area.	✓		
2.	No impact on forest and agricultural land.	✓		
3.	Drainage and surface runoff around the school managed.	✓		
4.	No water logging around the school.	✓		
5.	Physical safety barrier on slab edge, staircase barrier, and around the construction boundary in place.		✓	Instructed to provide soft barricades
6.	Safety Sign boards, Emergency Phone Numbers, caution tape around under construction area in place.	✓		Instructed to provide emergency phone numbers
7.	Good Housekeeping of construction material.	✓		
8.	Use of PPEs by labour.	✓		
9.	No occupational health and safety issues.	✓		
10.	Health and sanitation around the camp maintained.	✓		
11.	No child labour during construction.	✓		
12.	Female worker are provided with equal wage.	✓		
13.	Consultations with SMC and local community (Women, Poor, Dalits, IPs, disadvantage groups).	✓		
14.	First aid kit available at construction site.	✓		
15.	Waste from construction and from camps managed.	✓		
16.	Employment opportunity to local.	✓		
17.	No Social and GESI issues.	✓		
18.	All raised grievances handled and resolved properly.	✓		No grievances yet
19.	Compensation paid for temporary acquired land.	✓		
20.	Other issue, if any.	✓		

Sn.	Safeguards Members	Name/Signature/Office Stamp
1.	Safeguards Focal Person, DLPIU - DRSP:	
2.	Safeguards and GESI Monitors, DSC - DRSP:	<i>Conchapa</i>
3.	Contractor's focal person for safeguards:	



Monthly Checklist for Safeguards Desk-DRSP (Construction Phase)

Name of School: Mahendrodaya SS.

Location: Dhunibesi - 8, Dhading

Date: 2021 March 1

Sn.	Issues	Status		Remarks
		Yes	No	
1.	Building safe from landslide, erosion and no risky area existed close to the school area.	✓		
2.	No impact on forest and agricultural land.	✓		
3.	Drainage and surface runoff around the school managed.	✓		
4.	No water logging around the school.	✓		
5.	Physical safety barrier on slab edge, staircase barrier, and around the construction boundary in place.	✓		Staircase barrier was absent
6.	Safety Sign boards, Emergency Phone Numbers, caution tape around under construction area in place.	✓		
7.	Good Housekeeping of construction material.	✓		
8.	Use of PPEs by labour.	✓		
9.	No occupational health and safety issues.	✓		
10.	Health and sanitation around the camp maintained.	✓		
11.	No child labour during construction.	✓		
12.	Female worker are provided with equal wage.			No female workers
13.	Consultations with SMC and local community (Women, Poor, Dalits, IPs, disadvantage groups).	✓		
14.	First aid box in site.	✓		
15.	Waste from construction and from camps managed.	✓		
16.	Employment opportunity to local.	✓		
17.	No Social and GESI issues.	✓		
18.	All raised grievances handled and resolved properly.			No any grievances
19.	Compensation paid for temporary acquired land.			No temporary land acquired
20.	Other issue, if any.			

Sn.	Safeguards Desk Members	Name/Signature/Office Stamp
1.	Safeguards Focal Person, DLPIU - DRSP:	 Sandip Adhikari
2.	Safeguards and GESI Monitors, PSC - DRSP:	Perina Pathak Tewina
3.	Contractor's focal person for safeguards:	 Nabin Gahatry

Semi-annual Monitoring Report January-June 2021

Monthly safeguards Desk checklist filled for Gramodaya SS, Okhaldhunga




Disaster Resilience Schools Project (DRSP)
Monthly Checklist Safeguard Desk

DATE 2021-03-25

Name of School: Gramodaya Yu.Si.SS

Location: Gramnamtar VDC

SN	Issue/Indicator	Status		Remarks
		Yes	No	
1.	Condition of slope of stability around school area is good.	✓	✗	
2.	No impact on forest and agricultural land		✓	
3.	Landslide/erosion and no risky area existed close to the school area that may cause risk to the school infrastructure.		✓	
4.	Provision of drainage and its proper management and surface runoff around the school		✓	
5.	No water logging around the school		✓	
6.	Impact upon top soil/cultivated land		✓	
7.	Dust/air pollution due to construction activity/ movement of construction vehicle		✓	
8.	Group Insurance Documents of workers		✓	
9.	Physical safety barricade on slab edge, staircase and around the construction boundary		✓	
10.	Project Information board		✓	
11.	Safety Sign boards, caution tap under construction area		✓	
12.	Good Housekeeping of construction material		✓	
13.	Emergency phone number around construction area in place		✓	
14.	First aid box available at construction site	✓		No any essential materials only First Aid Box available
15.	Use of PPEs by labor		✓	
16.	Fatal accident during construction		✓	
17.	Labor camp in good condition with proper ventilation, lighting		✓	
18.	Child labor during construction		✓	
19.	Female worker during construction		✓	
20.	Female worker as provided with equal wages		✓	
21.	Separate male and female toilets, clean toilets with adequate supply of water; maintain hygiene		✓	
22.	Health, hygiene and sanitation around the camp		✓	
23.	Use alcohol and other forms of intoxication by laborer's; gambling, quarrel with locals, disrespect local culture and religion, and may promote socially undesirable activities		✓	
24.	Cleaning site after construction and disposing waste properly		✓	Cutting mud was on the School construction area.
25.	Waste management from construction and from camp	✓		
26.	Other issue, if any			

S N	Safeguards Members	Name/ Signature/ Office stamp
1	Chief, DLPU - DRSP	
2	Safeguards and GESI Monitors, PSC- DRSP	Anjula Shrestha 
3	Safeguards focal Person, DLPU-DRSP	

Monthly Safeguard Desk Monitoring Checklist of Netrakali SS, Sindhuli

Monthly Checklist for Safeguards Desk-DRSP (Construction Phase)

Name of School: Netrakali SS

Location:

Date: 2021/05/05

Sn.	Issues	Status		Remarks
		Yes	No	
1.	Building safe from landslide, erosion and no risky area existed close to the school area.	✓		
2.	No impact on forest and agricultural land.	✓		
3.	Drainage and surface runoff around the school managed.	✓		
4.	No water logging around the school.	✓		
5.	Physical safety barrier on slab edge, staircase barrier, and around the construction boundary in place.	✓		Contractor are instructed to install it
6.	Safety Sign boards, Emergency Phone Numbers, caution tape around under construction area in place.	✓		
7.	Good Housekeeping of construction material.	✓		
8.	Use of PPEs by labour.	✓		NO use of PPEs
9.	No occupational health and safety i	✓		
10.	Health and sanitation around the camp maintained.	✓		
11.	No child labour during construction.	✓		No any child labour
12.	Female worker are provided with equal wage.	✓		No female worker
13.	Consultations with SMC and local community (Women, Poor, Dalits, IPs, disadvantage groups).	✓		
14.	First aid box in site.	✓		
15.	Waste from construction and from camps managed.	✓		
16.	Employment opportunity to local.	✓		
17.	No Social and GESI issues.	✓		
18.	All raised grievances handled and resolved properly.	✓		
19.	Compensation paid for temporary acquired land.	✓		
20.	Other issue, if any.			

Sn.	Safeguards Desk Members	Name/Signature/Office Stamp
1.	Safeguards Focal Person, DLPIU - DRSP:	Shree B. Pujara
2.	Safeguards and GESI Monitors, PSC - DRSP:	Dipa Khatiwala
3.	Contractor's focal person for safeguards:	

Monthly Safeguard Desk Monitoring Checklist of Shree Lapilang SS, Dolakha

Monthly Checklist for Safeguards Desk-DRSP (Construction Phase)

Name of School : Shree Lapilang Ma. Vj (51, DOLLA LANG, RECON2)

Location: Lapilang

Sl.	Issues	Status		Remarks
		Yes	No	
1.	Building safe from landslide, erosion and no risky area existed close to the school area.	✓		
2.	No impact on forest and agricultural land.	✓		
3.	Drainage and surface runoff around the school managed.	✓		
4.	No water logging around the school.	✓		
5.	Physical safety barrier on slab edge, staircase barrier, and around the construction boundary in place.	✓		Distracted for physical safety barrier on slab.
6.	Safety Sign boards, Emergency Phone Numbers, caution tape around under construction area in place.			Safety sign board on place.
7.	Good Housekeeping of construction material.	✓		
8.	Use of PPEs by labour.	✓		
9.	No occupational health and safety issues.	✓		
10.	Health and sanitation around the camp maintained.	✓		
11.	No child labour during construction.	✓		
12.	Female worker are provided with equal wage.			No female workers
13.	Consultations with SMC and local community (Women, Poor, Dalits, IPs, disadvantage groups).	✓		
14.	First aid box in site.	✓		
15.	Waste from construction and from camps managed.	✓		
16.	Employment opportunity to local.			Local shops are benefited
17.	No Social and GESI issues.	✓		
18.	All raised grievances handled and resolved properly.			No grievance recorded
19.	Compensation paid for temporary acquired land.			No temporary acquired land
20.	Other issue, if any.		✓	

Page 1 of 2

Monthly Safeguard Desk Monitoring Checklist of Shree Janajyoti SS, Dolakha

Monthly Checklist for Safeguards Desk-DRSP (Construction Phase)

Name of School : Shree Janajyoti Ma. Vi (50 DOHA JANA RECON2)Location: Leptung

Sn.	Issues	Status		Remarks
		Yes	No	
1.	Building safe from landslide, erosion and no risky area existed close to the school area.	✓		
2.	No impact on forest and agricultural land.	✓		
3.	Drainage and surface runoff around the school managed.	✓		
4.	No water logging around the school.	✓		
5.	Physical safety barrier on slab edge, staircase barrier, and around the construction boundary in place.	✓		Instructed for complete site barricading and physical safety barrier on slab.
6.	Safety Sign boards, Emergency Phone Numbers, caution tape around under construction area in place.			Safety sign board on place.
7.	Good Housekeeping of construction material.	✓		
8.	Use of PPEs by labour.	✓		
9.	No occupational health and safety issues.	✓		
10.	Health and sanitation around the camp maintained.	✓		
11.	No child labour during construction.	✓		
12.	Female worker are provided with equal wage.			No female workers.
13.	Consultations with SMC and local community (Women, Poor, Dalita, IPs, disadvantage groups).	✓		
14.	First aid box in site.	✓		
15.	Waste from construction and from camps managed.	✓		
16.	Employment opportunity to local.			Local shops are benefited
17.	No Social and GESI issues.	✓		
18.	All raised grievances handled and resolved properly.			No grievance recorded
19.	Compensation paid for temporary acquired land.			No temporary acquired land
20.	Other issue, if any.		✓	


Sn.	Safeguards Members	Name/Signature/Office Stamp
-----	--------------------	-----------------------------

Monthly Safeguard Desk Monitoring Checklist of Bhringeshwori SS, Bijulikot, Ramechhap

Monthly Checklist for Safeguards Desk-DRSP (Construction Phase)

Name of School: Bhringeshwori SS RAAP BKOT RECON2)
 Location: Bijulikot Date: 2nd May 2021

Sn.	Issues	Status		Remarks
		Yes	No	
1.	Building safe from landslide, erosion and no risky area existed close to the school area.	✓		
2.	No impact on forest and agricultural land.	✓		
3.	Drainage and surface runoff around the school managed.	✓		
4.	No water logging around the school.	✓		
5.	Physical safety barrier on slab edge, staircase barrier, and around the construction boundary in place.			Instructed to keep barrier on slab & staircase.
6.	Safety Sign boards, Emergency Phone Numbers, caution tape around under construction area in place.	✓		
7.	Good Housekeeping of construction material.	✓		
8.	Use of PPEs by labour.	✓		
9.	No occupational health and safety issues.	✓		
10.	Health and sanitation around the camp maintained.	✓		
11.	No child labour during construction.	✓		
12.	Female worker are provided with equal wage.			No female workers
13.	Consultations with SMC and local community (Women, Poor, Dalits, IPs, disadvantage groups).	✓		
14.	First aid box in site.	✓		Add medical supplies.
15.	Waste from construction and from camps managed.	✓		
16.	Employment opportunity to local.	✓		
17.	No Social and GESI issues.	✓		
18.	All raised grievances handled and resolved properly.			No grievance yet
19.	Compensation paid for temporary acquired land.			
20.	Other issue, if any.			

Sn.	Safeguards Desk Members	Name/Signature/Office Stamp
1.	Safeguards Focal Person, DLPIU - DRSP :	
2.	Safeguards and GESI Monitors, BSC - DRSP:	
3.	Contractor's focal person for safeguards:	Sanjay Kumar



Page 1 of 2

Monthly Safeguard Desk Monitoring Checklist of Bhringeshwori SS, Kotgaun, Ramechhap

Monthly Checklist for Safeguards Desk-DRSP (Construction Phase)

Name of School: Bhringeshwori SS RAAP BHR/RECON2
 Location: Kotgaun Date: 2nd May 2021





Sn.	Issues	Status		Remarks
		Yes	No	
1.	Building safe from landslide, erosion and no risky area existed close to the school area.	✓		
2.	No impact on forest and agricultural land.	✓		
3.	Drainage and surface runoff around the school managed.	✓		
4.	No water logging around the school.	✓		
5.	Physical safety barrier on slab edge, staircase barrier, and around the construction boundary in place.			Instructed to keep barriers on slab
6.	Safety Sign boards, Emergency Phone Numbers, caution tape around under construction area in place.	✓		No emergency number at site
7.	Good Housekeeping of construction material.	✓		
8.	Use of PPEs by labour.	✓		
9.	No occupational health and safety issues.	✓		
10.	Health and sanitation around the camp maintained.	✓		
11.	No child labour during construction.	✓		
12.	Female worker are provided with equal wage.			No female workers
13.	Consultations with SMC and local community (Women, Poor, Dalits, IPs, disadvantage groups).	✓		
14.	First aid box in site.			
15.	Waste from construction and from camps managed.	✓		
16.	Employment opportunity to local.	✓		
17.	No Social and GESI issues.	✓		
18.	All raised grievances handled and resolved properly.			No grievance yet
19.	Compensation paid for temporary acquired land.			No land acquired
20.	Other issue, if any.			

Sn.	Safeguards Desk Members	Name/Signature/Office Stamp
1.	Safeguards Focal Person, DLPIU - DRSP :	
2.	Safeguards and GESI Monitors, DSC - DRSP:	
3.	Contractor's focal person for safeguards:	





Page 1 of 2

Annex 4: Meeting Minutes regarding consultations (Filled Samples)

Meeting minutes at Mahendrodaya SS, Dhading

   			
Project name:	L3702 & G0601/0602 _ DRSP – DISASTER RESILIENCE OF SCHOOLS PROJECT		
Local:	CLPIU		
Place:	Shree Mahendrodaya SS, Thunibesi, Dhading		
Presences:	DSC RE, DSC SE, DSC ESM, Contractor SE, contractor		
Date/Time:	2021 January 12		
MEETING TOPICS			
NO	SUBJECT	RESPONSIBLE	TARGET DATE
1.	Retaining wall works ongoing behind 3-6c(XS).		
2.	Brickwork in staircover top slab, terrace work ongoing. Skilled labor - 8 Unskilled - 10.		
	Previously continuous labor used to be around 28 numbers. Labor are returned to home to celebrate maghe sankranti. Retaining wall work will be stopped for 5 days due to maghe sankranti from January 14.		
3.	Reduce height of retaining wall to adjust ground level. No need to raise retaining wall above existing ground level in upper part.	DSC SE Contractor	2021-01-15
	Maintain slope and top dimension of wall according to height. Reduce height of wall → 8.5m, top width 675mm.	"	"
4.	Demolish duct wall and re construct making align with window opening. No need to plaster inside duct (In both blocks)	"	"
5.	Repair plaster work. Need to be in plumb and alignment. Kopla in beam, column wall must be uniform. Check using thread, plumb, spirit level.	Contractor	"
6.	Physical barrier to be provided in superstructure.	"	2021-01-15
7.	Barricading behind lab block need to be completed / repair. Also need along road side.	"	"
8.	Plastering in staircase wall to be finished with beam according to drawing.	"	"
9.	Do not stack / dump brick and other material in huge quantity above slab.	"	"
10.	Enough PPE to be provided. Maintain well house keeping.	"	"
11.	Provide emergency number. Reduce ht. of information board. Fill all the information.	"	"
Attendees: Nareesh Kasula, DSC RE, Gekala. Perina Patrak, DSC ESM, Terina. Umah Thapa, SE, DSC, Thapa. Pradip Thapa.		Keshav Paudel (H.M.)	

Meeting minute at Shree Deurali SS, Dhading











UMAR MUNSHI ASSOCIATES
 CONSULTING, SURVEILLANCE, PROJECT MANAGEMENT, & CONSTRUCTION

Project name: L3702 & G0601/0602 _ DRSP – DISASTER RESILIENCE OF SCHOOLS PROJECT
 CLPIU
 Location: Shree Deurali SS, Saha, Dhading
 Time: DSCRE, DSCSE, DSCESM, Contractor Project Engineer, Contractor SE, Contractor REP
 Date: 2020 March 22

AGENDA TOPICS

SUBJECT	RESPONSIBLE	TARGET DATE
Availability & monitor PPE to all workers on daily basis.	Contractor	
Maintain proper housekeeping & site clearance on regular interval.	"	
Install pamphlets showing information on COVID 19.		2020 March 28

Attendees:
 Suraj Kunwar, DSC-RE 
 Chandra Limbu, DSC, SE 
 Rishi Golafay, PK, Workshop 
 Hemant Shrestha, SE/Contractor 
 Prerna Pathak, DSC, ESM 

Meeting minutes at Panchakanya SS, Sisneri, Sunkoshi RM-3, Okhaldhunga

Date _____
Page _____

Today on 19 March, 2021, Instruction has been given on meeting between DSC and contractor representatives in Panchakanya SS, Okhaldhunga

2021-03-19

Presences

Name	Post	Signature
1. Bal Bahadur Neuki	Chief, DLPIO	[Signature]
2. Dipendra Dutt	RE	[Signature]
3. Anjula Shrestha	SM	[Signature]
4. Sachin Khimchong Rai	SE Contractor	[Signature]
5. LUNA Rai	Contractor representative	[Signature]
6. Surendra Thakur	SE, DSC	[Signature]

Topic for Discussions

- About Project Information Board, Safety Sign Boards, Emergency Phone Number, Covid Information Pamphlets and Equipments
- About PPEs Kit
- About progress of work
- About increment of manpower
- About coarse aggregate

Decisions

- Agreed to have project Information Board, Safety Sign Boards, Emergency Phone Number Pamphlets, Covid Information Pamphlets & Equipments within a week.
- Agreed to have add PPEs for workers and also for visitors
- The excavation & soling work of both 3C7 block is completed.
- There are only 3 workers seemed at the site, so there needs to increase the manpower.
- The coarse aggregate stocked at site seemed to be 12 mm down so needs to be of 20 mm down.

Dipendra [Signature] [Signature] Anjula [Signature] [Signature]

Meeting minutes of Shree Pashupatinath SS, Makwanpur



Project name:	L3702 & G0601/0602 _ DRSP – DISASTER RESILIENCE OF SCHOOLS PROJECT
Name of the Meeting	Weekly Meeting/Monthly Meeting/Adhoc Meeting
Place:	Shree Pashupatinath SS
In Attendance:	Roshan Dev, Sneha Rai, Bibek Chandra Das, Bikash Pm Magar, Laxman Gautam, Mukesh Jaiswal
Date/Time:	06 April 2021.

MEETING TOPICS

NO	SUBJECT/TOPIC/ISSUES	RESPONSIBILITY	TARGET DATE
1.	No PPE available. Contractor's safety supervisor was instructed to provide PPE	Contractor's Safety Supervisor	15 April 2021
2.	Contractor safety supervisor was instructed to provide first aid box and emergency phone numbers.	Contractor's Safety Supervisor	15 April 2021
3.	Labor camp was shifted from the ongoing construction building	—	—
4.	Contractor's safety supervisor was instructed to maintain good house keeping & clean the site	Contractor's safety supervisor	15 April 2021
5.	Contractor's safety supervisor was instructed to keep the labor camp area clean.	Contractor's safety supervisor	Regular

Name: Roshan Dev (RE, DSC) Signature: [Signature]

Name: Sneha Rai (ESM, DSC) Signature: [Signature]

Name: Bibek Chandra Das (Contractor, RE) Signature: [Signature]

Name: Bikash Pm Magar (SE, Contractor) Signature: [Signature]

Name: Laxman Gautam (Safety supervisor, Contractor) Signature: [Signature]

Name: Mukesh Jaiswal (SE, DSC) Signature: [Signature]


Name: _____ Signature: _____

Name: _____ Signature: _____

Name: _____ Signature: _____

Consultation meeting minutes with the Adarsha SS, SMC, and locals

Page No.:
Date :



आज मिति २०७७ साल कार्तिक ३ गते बुधबुङका दिन -
यस श्री आदर्श माध्यमिक विद्यालय आर्क-२ दोभोचौर
छात्राङ्को विद्यालय व्यवस्थापन समिति को बैठक विद्या-
लय व्यवस्थापन समितिका अध्यक्ष श्री भुमिबहादुर -
तामाङ्को अध्यक्षमा बसी निम्न प्रस्ताव माथि छलफल
गरी निर्णय गरियो।

उपस्थिति:-

क्र.सं.	नाम	पद	मोबाइल नं.	सही
१	श्री भुमिबहादुर तामाङ्	पुनःस्थापना	९८२११२६३३६	सही
२	श्री प्रेम बज्रगोपाल	सदस्य	९८४१२८०२८४	सही
३	श्री गंगाधर तामाङ्	सदस्य	९८४३००३३९२	सही
४	श्री निर्मला तामाङ्	सदस्य	९८४६९४६१८	निर्मला
५	श्री रामभगत चिन्क	सदस्य	९८०३६६१६१२	रामभगत
६	श्री मतकुमारी जिम्बा	सदस्य	९८५६१२४९१६	मतकुमारी
७	श्री माइली तामाङ्	सदस्य		माइली
८	श्री वसन्तकुमार आचार्य	सदस्य	९८४५६२२९४६	वसन्त
९	श्री विष्णु शर्मा जोशी	सचिव	९८४९८३०६०९	विष्णु

प्रस्तावहरू:-

१. विद्यालय निर्माणका लागि जग्गा उपलब्ध गराउनेर आवश्यक सहयोग गर्ने सम्बन्धमा,
२. विद्यालयको जग्गाको चार किल्ला खुलाउने सम्बन्धमा,
३. निर्माणको क्रममा निरुद्धका दुग्गा, सिमेन्ट, फलाम - आदिको व्यवस्थापन दुग्गाबाट खन्याउने सम्बन्धमा,
४. T/LC आवश्यक भएको नभएको आवश्यक भएमा T/LC निर्माण गर्ने खात खर्च, तथा उक्त जग्गाको भौगोलिक

२. विद्यालय बालिकाओं के लिए सड़क आदि जोड़ा जाने
या जगहों पर, उक्त सड़कों के निर्माण तथा सड़क नालों
विद्यालयों जगहों पर निर्माण होने सम्बन्धमा,

६. निर्माण यापनी शरण इन्जिनियरिंग सम्बन्धमा,

७. निर्माणों सम्बन्धमा निर्माण कामदारहरूलाई शरण
अर्थात् यात्रा अथवा जगह उपलब्ध गराउने सम्बन्धमा,

८. विद्यालय निर्माणकाट धार्मिक यादृष्टिकु सम्बन्धमा
आदिमा प्रत्यक्ष तथा अप्रत्यक्ष अर्थ हुने सम्बन्धमा

९. विद्यालय निर्माणकाट स्थापना प्रत्यक्ष वा अप्रत्यक्ष
अर्थ हुने सम्बन्धमा,

१०. कतावरणीय दृष्टिले विद्यालय वरिष्ठी रहेका भौतिकी
क्षेत्रहरू अर्थात् वन, पहाड, नदी शरण क्षेत्र आदि सम्बन्धमा,

११. प्रस्तावित विद्यालय निर्माणकाट व्यवस्थापन समितिबाट सर्व
सम्मत स्वीकृति गरिएको सम्बन्धमा,

निर्णयहरू:-

१. हालको श्री आदर्श माध्यमिक विद्यालयको भवन रहेको ठाउँ
कक्षा १२ सम्मको पठनपाठनका लागि भवन निर्माण गर्ने
नपुग्ने भएकै विद्यार्थीहरूलाई खल्लोदान नभएको, त्रिभुवन
राजपथको वरिष्ठी भएकै भित्र पर्ने देखिएको भवनको
कुल भत्कन हुने भएकाले पछि विद्यालय स्थापना गर्ने
सम्बन्धमा गरि विद्यालय भूजिक सर्वेक्षण भित्रको बि.नं. ३३६को
सार्वजनिक जग्गा भवन बनाउने सर्वसम्मत निर्णय गरियो साथै

प्रेम

तम्रा:-

निर्णय नं 6, भवन निर्माण कार्य हेतु निर्माण काजदार को
भवन स्थापना के लिये प्रत्येक को बस का लिये निर्माण कार्य
नियमों के अनुसार शाखा निर्माण 2 कमरे प्रत्येक भवन स्थापना के लिये
निर्णय गतिमी।

निर्माण नैऋत, प्रस्तुतवित्त्व्यात्मन भवत निर्माण गर्वा बहो
 धारो, धारा पद्यो, मन्दिर, जडागल। गुठी प्रस्तुत धर्मि
 लाष्टुतिव प्रोतात्वि २ एतिहासि व्वात्ताह कुन वाधा
 नपुन प्रतिवस्वता दाहित निर्माण गतिमौ।

निर्वाह में ५ विद्यालय भवन उक्त प्रस्तावित स्थापना निर्मा
ण एवं विकासका प्रयासों को कम किसिम का है। इनके विकास
में २ रुपया है। प्रत्येक वर्ष के लिए निर्वाह गारंटी।

निर्णय नं १०, विद्यालय भवन निर्माण का लागि प्रस्तावित
स्वातन्त्रतावादीय दृष्टिकोणबाट उपयुक्त रहेकोले उक्त
स्वानामा भवन निर्माण गर्दा वहाँ प्रयोग हुने कर्मचारीहरूको
भुक्तिको सुविधा नहुने, कुनै सहयोग क्षेत्र नभए,
नेहरूको लागि सन्तुलन नबिग्रेन प्रतिवद्धता जनाउने
निर्णय गरियो।

निर्णय नैवेद्य, यद्यपि प्रस्ताव भाषित किया हुआ गुर्दा हल
विद्यालय रहे, स्वामी को दुर्गति मोटा बारी रहे कोर
सुडको २२ गिरि क्षेत्र में मोटा जमाई साधना, खेल भेदा
को भुगव भए कोले उपयुक्त स्थान में विद्यालय स्वामी लो
गर्नुपन पहिले दोखि है आवश्यक्ता भएपुन भए कोले
आम भूमिमा लब्ध समस्तका लब्धाले है मध्यम मर गदु
विन्म. लो को कुराधम लम्बान्वित निष्कृष्य बर भो
गाधिकारका लागि प्रस्तावित किनै सुकध को लाने निष्कृष्य
विद्यालय लो मर गदु को लो जमाई भवत निर्माण र
निष्कृष्य लब्धाले लागि विद्यालय लब्धाले लाने लो
आम को लो लो लो लो लो लो लो लो लो लो लो लो
निष्कृष्य लो लो लो लो लो लो लो लो लो लो लो लो

A. Consultation Meeting Minute with stakeholders related to existing graveyards

25. श्री गंगाधर तामाडो विजय सफल	श्री	(5063202380)
26. श्री रमक धलान (स्वामीय)		
27. श्री चन्द्रलाल तामाडो स्वामीय - सावट		(500164649)
28. श्री अजली तामाडो	श्री	
29. श्री सलोनी तामाडो	सलोनी	
30. श्री मनभाया तामाडो	मने भाया	
31. श्री तुल कदापुर (वास्का)	श्री	(5063202380)
32. श्री पदम. वाईवा	पदम	(5063202380)
33. श्री सुजय तामाडो	सुजय	(5063202380)
34. श्री प्रमल तामाडो	प्रमल	(5063202380)
35. श्री दिलीपमा पिडो	दिलिपमा	(5063202380)
36. श्री सुरेकुमारी तामाडो	सुरे कुमारी	(5063202380)
37. श्री मिना देवी तामाडो	मिना	(5063202380)
38. श्री साउली तामाडो	साउली	(5063202380)
39. श्री दिपेन्द्र बापले	दिपेन्द्र	(5063202380)
40. श्री दिल कर्षे	दिल	
41. श्री दिलाल काईवा	दिल	(5063202380)
42.		
43.		
44.		
45.		
46.		
47.		
48.		
49.		

प्रामाणिक अतिथि :-

22. भूपेन्द्र अर्मात - सम्राज विकास विद्या, PRSP-DSC - 9851039940	श्री
23. रिकेश चित्रकार - चातावरण विद्या, ।। - 9801877684	श्री
24. प्रकाश पाठे - लैङ्गिक समानता समीक्षा विद्या, 9851550815	श्री
25. पेरीना पाठक - सामाजिक तथा वातावरण सुरक्षा मन्त्रि PRSP-DSC-9801877674	श्री
26. इ.इ.जी. साह - DCPZP (एन इ.जी.जी.) 984473057	श्री

प्रस्तावहरू :-

१. चिहनाघाट (धुर्खी) अन्यत्र व्यवस्थापन गरि विद्यालय भवन निर्माण गर्ने सम्बन्धमा ।

१. च. वडा निर्वाचन
वसुन्धरा
गोर्खा प्रदेश, नेपाल

निर्णयहरू :-


निर्णय नं. १, प्रस्ताव नं १ माथि छलफल गर्दा यस धात्रे गाउँपालिका वडा नं-२ र इन्भेन्चुरमा अवस्थित डि. नं-३३६ को करिब १० रोपनी भित्रफल जग्गा सार्वजनिक जग्गा सार्वजनिक जग्गा परम्परागत रूपमा धुर्खी (चिहनाघाट) को कुपमा प्रयोग गर्दै आएकोमा यस गाउँपालिका वडा नं-२ को चौम संचालनमा रहेको छि आकर्म मा.वि. संचालन का लागि विद्यालयलाई आवश्यक पर्ने भए संचालन हक निर्माण गर्ने परीत जग्गा नभएकोले हाल परम्परागत रूपमा सडकद गर्दै आएको धुर्खी (चिहनाघाट) लाई हालको स्थानबाट तल्लो अन्यत्र व्यवस्थापन गर्ने निर्णय गरियो ।

निर्णय नं २,

निर्णय नं १ मा उल्लेखित हाल संचालनमा रहेको धुर्खी (चिहनाघाट) व्यवस्थापन गर्ने सम्बन्धमा भविष्यमा निर्माण गरिने विद्यालयको संचालन हक २ विद्यालय संचालनका लागि धात्रे गाउँपालिकाको कार्यालय रहेको बेसो धात्रेको भिति २०७५/०८/०८ को पर्स ०६/०८ च. नं. ००६ को पत्र तथा निर्णय नं १० मा उल्लेखित डि. नं-३३६ को करिब १० रोपनी भित्रफल जग्गा विद्यालय लाई भोगाधिकार गर्न दिइकोले उक्त जग्गा कुम्भाङ्ग भन्दा बाहिर कुम्भाङ्ग २०० मिटरको दुरीमा पर्ने प्रस्तावित चिहनाघाट स्थल नं १ नुरेकुम डाँडा रहेको सार्वजनिक जग्गा का उक्त विद्यालय कुम्भाङ्ग होखि करिब १२० मिटर पूर्व, बाटोदेखि दक्षिणमा रहेको सार्वजनिक जग्गा प्रस्तावित स्थल नं २ को सार्वजनिक जग्गा संचालन गर्दा वातावरणीय प्रदूषण र धार्मिक, सामाजिक तथा सांस्कृतिक रूपमा कुनै असर नपर्ने भन्नेकोले हालको स्थानबाट प्रस्तावित स्थानमा धुर्खी (चिहनाघाट) व्यवस्थापन गरि डि. नं-



Page | 42



लिखितम आज मिति २०७८ साल वैशाख २० गते आइतबारका दिन हामी दुम्भेभञ्ज्याङ स्थित दाह संस्कार स्थलको सरोकारवाला थाके ५ (दोमचौर, सल्ले र ठूलो तसर्पु निवासी) हरुको समूह थाके वडा नं ५ को वडा कार्यालयमा भेला भइ निम्न विषयमा छलफल गरी निम्न निर्णय गरेका छौ ।

उपस्थिति:

- १) भुमि वडा तामाङ थाके ५ सल्ले
- २) रामलाल तामाङ — मेठडाँडा — सोमलाल
- ३) राजु तामाङ — मेठडाँडा सल्ले — शम्भु
- ४) काँडेभद्र तामाङ — मेठडाँडा सल्ले — कृष्ण
- ५) रसुमन्हा तामाङ — मेठडाँडा —
- ६) बाबुरा तामाङ — सल्ले — शम्भु राम
- ७) विमलाल तामाङ — सल्ले —
- ८) राजकुमार तामाङ — सल्ले —
- ९) शम्भु माया तामाङ — सल्ले —
- १०) बाबु वडा तामाङ — ठूलो तसर्पु —
- ११) भुमि वडा थाके ५ ठूलो तसर्पु —
- १२) भुमि वडा थाके ५ ठूलो तसर्पु —
- १३) भुमि वडा तामाङ — ठूलो तसर्पु —
- १४) सुरेश नेगी, दुम्भेभञ्ज्याङ (बडादफला) — सुरेश
- १५) जयवहादुर नेगी तामाङ —
- १६) कुल वडा तामाङ थाके ५ सल्ले —

प्रस्तावहरु:

१) चिहान खाने सहमति दिने सम्बन्धमा ।

निर्णयहरु


प्रस्तुत प्रस्ताव उपर छलफल गर्दा थाके गाउँपालिका वडा नं ५ स्थित दुम्भेभञ्ज्याङमा रहेको सार्वजनिक जग्गा (जहाँ हामीले मृत शरीरका अस्थु विसर्जन गर्छौ) मा यस वडाको एक मात्र माध्यमिक तहको विद्यालय श्री आदर्श मा.वि.को भवन स्थापना गर्ने र सो स्थान भन्दा करिव ५०० मिटर माथि रहेको अर्को सार्वजनिक जग्गामा आधुनिक किसिमको शवदहन स्थल बनाउने कुरामा हाम्रो मञ्जुरी रहेकोले हाम्रा बालबालिकाहरुको शैक्षिक भविष्य निर्माणका लागि हामी राजी खुशीका साथ हाम्रा अग्रजहरुका अस्थु विसर्जन स्थलमा डोजर लगाइ विद्यालय भवन निर्माणका लागि जमिन खाने दिने सहमतिका साथ विद्यालय भवन निर्माणमा कुनै अवरोध सिर्जना नगर्ने वरु विद्यालय निर्माणको कामको स्वागत गर्दै आवश्यक सहयोग पुर्याउन प्रतिवद्धता जाहेर गर्दछौ ।

सोमलाल शम्भु कृष्ण

प्रधानाध्यापक

नोटर

९



लिखित आज मिति २०७८ साल वैशाख २६ गते आइतबारका दिन हामी जुरेथुम निवासी निम्न व्यक्तिहरु थाके ५ डुम्रेभञ्ज्याङमा भेला भई निम्न विषयमा छलफल गरी निम्न निर्णय गरि दियौ ।

उपस्थिति

- १) श्री खीर वं ताम्राङ थाके-५ जुरेथुम — खीर
- २) श्री विजिता ताम्राङ थाके-५ जुरेथुम — विजिता
- ३) श्री खीर वं ताम्राङ — थाके-५ जुरेथुम — खीर
- ४) श्री कालि ताम्राङ — थाके-५ जुरेथुम — काली
- ५) श्री छेछु विडो ताम्राङ थाके-५ जुरेथुम — छेछु
- ६) श्री उल्लो म्या ताम्राङ थाके-५ जुरेथुम — उल्लो
- ७) श्री डिङ्ग वं ताम्राङ थाके-५ जुरेथुम — डिङ्ग
- ८) श्री प्रंगल वं ताम्राङ थाके-५ जुरेथुम — प्रंगल
- ९) श्री नवरत्न ताम्राङ थाके-५ जुरेथुम — नवरत्न
- १०) श्री लुक्छे गजी थाके-५ जुरेथुम — लुक्छे
- ११) श्री मल वं ताम्राङ थाके-५ जुरेथुम — मल
- १२) श्री हङ्ग वं विडो थाके-५ जुरेथुम — हङ्ग
- १३) श्री विमल ताम्राङ थाके-५ जुरेथुम — विमल
- १४) श्री लुक्छे ताम्राङ थाके-५ जुरेथुम — लुक्छे
- १५) श्री जोङ्ग वं ताम्राङ थाके-५ जुरेथुम — जोङ्ग
- १६) श्री तिल वं ताम्राङ थाके-५ जुरेथुम — तिल
- १७) श्री रत्न वं ताम्राङ थाके-५ जुरेथुम — रत्न
- १८) श्री अरुण म्या, थाके-५ जुरेथुम — अरुण

प्रस्तावहरु: श्री विमल ताम्राङ प्रस्ताव —

१) शवदहन स्थल सम्बन्धमा ।

निर्णयहरु

प्रस्तुत प्रस्ताव उपर छलफल गर्दा थाके गाउँपालिका वडा नं ५ स्थित डुम्रेभञ्ज्याङमा रहेको सार्वजनिक जग्गामा थाके गाउँपालिका वडा नं ५ का केहि टोलहरुका मृत शरीरका अस्थि परम्परागत रुपमा विसर्जन गर्दै आइरहेकोमा हाल उक्त स्थलमा विद्यालय भनव बनाउने भनी सिंगो समुदायले निर्णय गरेपछि डुम्रेभञ्ज्याङबाट ५०० मिटर माथि रहेको स्थल नं १ मा शवदहन स्थल सार्दा यस टोललाई कुनै असर नपर्ने निर्णय गरियो ।

खीर काली विजिता छेछु
 डिङ्ग प्रंगल नवरत्न लुक्छे
 मल हङ्ग विमल तिल
 रत्न अरुण

प्रमाणित
 प्रधानाध्यापक

(१०)
