

Social Monitoring Report

Project Number: 44425-013

March 2015

Period: January 2014 - December 2014

Bihar State Highways II Project - Additional Financing

Prepared by

Bihar State Road Development Corporation Ltd., Government of Bihar

This report has been submitted to ADB by the Bihar State Road Development Corporation Ltd., Government of Bihar and is made publicly available in accordance with ADB's public communications policy (2011). It does not necessarily reflect the views of ADB.

This social monitoring report is a document of the borrower. The views expressed herein do not necessarily represent those of ADB's Board of Directors, Management, or staff, and may be preliminary in nature. In preparing any country program or strategy, financing any project, or by making any designation of or reference to a particular territory or geographic area in this document, the Asian Development Bank does not intend to make any judgments as to the legal or other status of any territory or area.

Asian Development Bank




Bihar State Road Development Corporation Ltd.

Bihar State Highway Project Package - II

CONTRACT PACKAGE NO. 2 & 3 (SH-86 & SH-87)

Consultancy Services for Construction Supervision for civil Works of Package-Il (SH-86 &SH-87) under BSHP-II AF Loan No.-2894-IND

Annual Report 2014

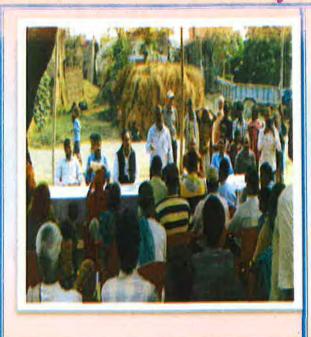



Monitoring of Implementation and Resettlement Plan



Submitted By



Egis International S.A in JV with Egis India Consulting
Engineers Pvt. Ltd. in association with
Transtek Engineers & Services Pvt. Ltd.
Saffron Square, 12/6 Delhi - Mathura Road,
Faridabad - 121003, Haryana.

SL No.			PARTICULARS	PAGE:		
	ABBF	REVIATI	ON	5-6		
1	PROJ	ECT BR	IEFING AND PROJECT BACKGRO	7		
	1.1	Projec	et Background	7		
	1.2	Projec	et Description	8		
2	IMPL PROJ		ATION OF RESETTLEMENT PLAN: A COMPONENT OF THE	8		
3			NAL ARRANGEMENTS FOR IMPLEMENTATION OF ENT PLAN (RP)	8		
4	EXTE	RNAL M	IONITORING	9		
5	OBJE	CTIVES	& TASKS OF EXTERNAL MONITORING	10		
6	MON	ITORIN	G AND REPORTING	10-29		
	6.1	Appoil	ntment and Mobilization of NGO	11		
	6.2	1	fication and Verification of Affected Persons and Jounity Properties (CPRs)	12		
		6.2.1	Training to Survey Staff for Identification and Verification Work by NGO	12		
		6.2.2	Verification of Affected Households	13		
		6.2.3	Verification of Affected Community Structures(CPRs)	14		
		6.2.4	Relocation/ Enhancement Status of Affected CPRs	15		
	6.3		sure and distribution of Public Information Brochure (PIB)	16		
	6.4	Couns	eling (Consultation) with Entitled Persons	16		
	6.5	Prepar	ration of Micro Plan (NTH) and Compensation Schedule	17		
	6.6		atus of Land Acquisition Process and Declaration of Award ected Families	18		
Ī	6.7	Status	on Preparation and Distribution of Identity Card (ID Card)	19		
	6.8	Opening of New Bank Account/ Verifying of Old Bank Account				
İ	6.9	Distribution of Compensation and Assistance				
	6.10	Trainir	ng Programme for Income Restoration	23		
	6.11	Apprai	sal of Other R & R Issues	24		
		6.11.1	Addressing HIV/AIDS Issues in Road Development Projects	25		

SL No.			PARTICULARS	PAGES			
		6.11.2	Action on HIV/AIDS Awareness/Prevention Campaigns	26			
		6.11.3	Compliance of Labour Laws, Prohibition of Child Labour	27			
		6.11.4	Compliance of Gender Issues	28			
		6.11.5	Grievance Redressal	28			
		6.11.6	Problem Encountered and Resolved	29			
7	RECO RP	DMMEND	ATIONS FOR PROPER AND TIMELY IMPLEMENTATION OF	29			
÷ 1	7.1		olementation Consultant (NGO)'s Compliance on Objectives Assignment	29			
	7.2	Comple	etion of Land Acquisition Process on Fast Track	30			
	7.3	Meeting	g of Grievances Redressal Committee	30			
	7.4	Training	g Programme for Income Restoration	30			
	7.5	Records of Relocation of DPs after Compensation Payment					
	7.6	Special Assistance to Vulnerable APs					
	7.7		ut for Completion of Work even after the Terms of RP nentation Consultant is matured	31			
ANNEX	URE	S:					
	1	Public 1	Information Disclosure Plan				
	2	Details	of Consultation Meetings				
	3	Sanctio	oned Letter of Micro Plan of TH & NTH				
	4	Sample	e of Identity Card & Verification Report				
1	5	Сору о	f Bank Account of a Sample passbook				
	6	Sample	e of Compensation Payment format				
	7	Sample	e of Cheque				
	8	Sample of Receiving of Compensation					
	9	AIDE N	MEMOIRE of ADB				
	10	GRC M	leeting				

ACKNOWLEDGEMENT

As External Monitor, we have initiated the monitoring work of implementation of Resettlement Plan (RP) for Bihar State Highways Project- Phase-II (95.667km). Besides other R&R issues, the main task of the External monitor is to monitor the disbursement of compensation and assistance to all affected people and community, so that the rehabilitation of these identified roads could be take place without any hindrance. However, it would not be possible to monitor the progress in implementation work without the kind support and help of many individuals and organizations to whom we came across during implementation. We would like to extend our sincere thanks to all of them.

The Monitoring team was adequately assisted by the Social Development Unit (SDU) team during the site visits and interaction with the APs particularly in community consultation meetings. We would like to express our gratitude to Mr. S. M. Singh, DGM (Tech), Muzaffarpur PIU who extended their kind support in collecting relevant information from several stakeholders and organizing several meeting with the NGO, appointed for the smooth implementation of RP. We also extend our thanks to Mr. Om Prakash, Manager (Tech) and Mr. Anuradha Chandra Manager (Tech) ,PIU, Muzaffarpur for their assistance at different occasions and accompanying me to visit of their concern project affected villages for consultation with the affected people and Village Head so that the verification of the various components of the RP implementation can be completed.

We also extend our sincere thanks to Mr. Ramesh Kumar, DGM(tech) and designated in-charge of Environmental and Social Safeguards sections of BSRDC, Patna, and others who provided valuable help and guidelines as and when required for implementation of RP.

We owe a great many thanks to a great many people who helped and supported us during monitoring of the implementation work.

Lastly, relentless co-operation of the project affected persons, the resettled families at R&R site during the community consultation and FGD sessions held, sometimes, at odd hours is gratefully acknowledged.

Dr. Gagan. C. Patra

R&R Expert

ABBREVIATION

ADB --- Asian Development Bank

AF --- Affected Family

AP --- Affected Person

BPL Below Poverty Line

BSHP --- Bihar State Highways Project

BSRDC --- Bihar State Road Development Corporation

COI --- Corridor of Impact

CPRs --- Community Property Resources

CRADLE Consultants for Rural Area Development Linked

Economy

DF — Displaced Family

DP --- Displaced Person

EA --- Executing Agency

FGD Focused Group Discussion

GoB --- Government of Bihar

GoI --- Government of India

HH --- Household

KII --- Key Informant Interview

MP --- Micro Plan

NGO --- Non-Government Organization

PH Physical Handicapped

PIU Project Implementation Unit

PMU --- Project Management Unit

R&R --- Resettlement and Rehabilitation

ROW --- Right of Way

RP --- Resettlement Plan

SC --- Schedule Caste

SDU --- Social Development Unit

SH --- State Highway

SHG --- Self Help Group

ST --- Schedule Tribe

ToR --- Terms of Reference

Monitoring and Resettlement Plan Implementation Report (Annual R & R Report 2014)

1. PROJECT BRIEFING AND PROJECT BACKGROUND

1.1 Project Background

With ADB assistance under BSHP project loan 2894-IND, two (2) stretches of existing state highways with total length of !The Formula Not In Tablekms under present contract, which were identified for rehabilitation & up-gradation in the state of Bihar falling in the districts of the Muzaffarpur and Sitamarhi.

The proposed project is part of widening and strengthening of existing State Highways from single lane carriageway into two-lane carriageway. The Bihar State Highways Project (BSHP)-IIAF aimed at strengthening the deteriorated state roads and upgrade some newly declared state roads to provide reliable road transport services in the state of Bihar. 2 sub-projects road sections under present contract, consisted of SH-86 and SH-87 with total length of !The Formula Not In Tablekms were selected for widening.

1.2 Project Description

This Annual Report of RP Implementation is concerned with the 2 sub-project roads i.e. SH-86 and SH-87. The details of concerned sub-projects are presented in **Table-1**, the RPs of which is being implemented as a part of project component:

Table-1: List of Sub-project Roads and Length of BSHP II AF

SI. No.	SH No.	Name of the Sub-project Road	Length (in Km.)	District Covered
1	86	Saraiya - Motipur	28.181	Muzaffarpur
2	87	Runisaidpur - Bhiswa	67.486	Sitamarhi
		Total	95.667	

Source: Resettlement Plan of all concerned sub-project road, BSRDC

The project will rehabilitate the deteriorated and damaged state road corridors to provide reliable road transport services and, hence, reduce poverty in the long term. As far as possible the project aimed at up-gradation and rehabilitation of existing state highways with limited amount of land acquisition following the existing alignment. Land acquisition is acquired for construction of new Bypass, realignment and geometric improvement and land will be acquired for all four project roads. The purpose of adopting up-gradation and rehabilitation within ROW and following the existing alignment was nothing but to reduce the social impact in its immediate environment to the maximum extent possible.

The condition of the existing road was poor as at many places the pavement was no more exists. There were villages in regular interval with many squatters and encroachers living or doing business along the road.

Anuradha Chang

The section of State Highways (SH-86) is located in Muzaffarpur It starts from Saraiya(connecting NH-102) and terminates at NH-28 near Motipur. It passes throughRaghunathpur, Jaitpur, Basra, Distolia, MishrauliaChowk in the district of Muzaffarpur (Bihar). The start point of Project road is at Saraiya (Km. 0.000) and end point is at Motipur (Km. 28.181). The total length of the road is 28.181 Km.

Another section of State Highways (SH-87) is located in Sitamarhi District. It start from Runnisaidpur to Bhiswa is connecting NH-77 near Runnisaidpur, SH-52 near Pupri and NH-104 near SursandandBhiswa near. It Passes through Nanpur, Pupri, Sursand, Parihar and Bhiswa in the district of Sitamarhi (Bihar). The start point of Project road is at Runnisaidpur (Km. 0.000) and end point is at Bhiswa (Km. 67.486). The total length of the road is 67.486Km.

2.0 IMPLEMENTATION OF RESETTLEMENT PLAN: A COMPONENT OF THE PROJECT

The execution of Resettlement Plan of the project is an important component of the project implementation, which has several activities to be performed such as appointment and mobilization of NGO, verification of Affected Persons, preparation of Micro Plan and Identity Card, distribution of compensation and appraisal of other R & R Issues, which is to be executed either before construction work or in between implementation of the project. For compliance of ADB's Resettlement policy, DGM of respective PIU were made accountable and responsible for implementation of Resettlement plan with the help of NGO, appointed for the exclusive task.

Fresh land acquisition is required for rehabilitation of road because of construction of new bypasses, realignment and geometric improvement.


3.0 INSTITUTIONAL ARRANGEMENTS FOR IMPLEMENTATION OF RESETTLEMENT PLAN (RP)

Bihar State Road Development Corporation (BSRDC), Govt. of Bihar is the executing agency of the Project. The BSRDC Ltd, Patna has established PIU for execution of sub-projects and for proper implementation of Resettlement Plan of concern projects. The Implementation of Resettlement Plan of the project SH-86 and SH-87 is being carried out by the Project Implementation Units (PIU), Muzaffarpur. The PIU headed by Deputy General Manager (Tech), has overall responsibility for policy guidance, coordination and planning, internal monitoring and overall reporting of the project and he is the designated Resettlement Officer (RO) at PIU Level.

An Assistant Resettlement Officer (ARO) of the rank of manager (tech)has been placed at the Sub-project level to coordinate the process of RP implementation and to address the adverse impacts on the people along the sub-project roads, if any. NGO was appointed by the EA to assist the PIUs in the effective, timely and efficient implementation of RP.

Manager (Tech.)

In addition, an Expert has been appointed by the Executing Agency through the Supervision consultant to monitor the progress of the RP implementation. The institutional arrangement of EA for the RP implementation is also outlined by the following Chart:

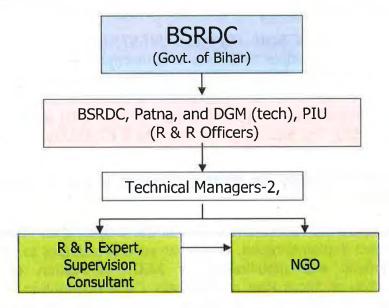

4.0 EXTERNAL MONITORING

Monitoring is a key activity in RP implementation in order to achieve resettlement objective as per ADB's Policy of Involuntary Resettlement. The Policy says "Monitoring provides both a working system for project managers and channel for the resettle to make known their needs and their reactions to resettlement execution."

External monitoring of RP implementation will provide PIU an effective basis for assessing resettlement process and identifying potential difficulties and problem area for rectification.

The present monitoring exercise deals with a number of selected tasks, which is mentioned in the agreement. The Social Development Unit (SDU) of BSRDC at headquarter and PIU level is monitoring the resettlement progress with the help of R&R cum Social Development Expert of Supervision Consultant internally by way of reviewing the progress of the activities carried out by the RP implementing agency (NGO) engaged for the purpose of day-to-day activities. It is also obvious that these are documented.

5.0 OBJECTIVES & TASKS OF EXTERNAL MONITORING

The main objective of External Monitoring of resettlement work is to provide an insight and guidelines to the management for assessing the progress of

Anuradha (Mandra)
Manager (Terri

resettlement. Its objective is to identify probable difficulties and problem area, like a RADAR system providing an early warning system, which need correction.

In order to ensure effective implementation of the RP and achievement of the set targets, monitoring of R&R components of the project has been carried out by the EA with the help of R&R cum Social Development Expert of Supervision Consultant so that it could enable timely adjustment of implementation set up and procedures.

The Quarterly report, which will assess the achievement of execution of main activities of RP implementation from January 2014 to December 2014, will outline and discuss the following issues in the subsequent Para:

- Appointment and Mobilization of NGO
- Verification of Affected Persons and Community Properties (CPRs)
- Translation of Resettlement Plan (RP)/EM in Local Language
- Counseling (Consultation) with Entitled Persons
- · Preparation of Micro Plan and Compensation Schedule
- The status of Land Acquisition process and Declaration of Award to Affected Families
- Status on preparation and Distribution of Identity Card
- · Opening of New Bank Account/ Verifying of Old Bank Account
- Distribution of Compensation and Assistance
- Proper Training to Displaced Persons (DPs) as a part of livelihood support
- Appraisal of other R & R Issues (Special Assistance to Vulnerable APs, Compliance of labour laws, prohibition of child labour and gender issues, HIV/AIDS Awareness/ Prevention Campaigns and Grievance Redressed)
- Assessment of Executing/ Implementing Agency

6.0 MONITORING AND REPORTING

As discussed above, monitoring of the RP implementation is a critical activity in involuntary resettlement. Monitoring involves periodic checking to ascertain whether activities are carried out according to the RP and in accordance with the existing laws of Govt. of India, Govt. of Bihar), and ADB Guidelines etc. It provides the necessary feedback for project management to keep the programme on schedule.

The implementation of the Resettlement Plan has been closely monitored by the R&R cum Social Development Expert and has been maintaining a close

Questins (Tech.)

interaction with affected people/ communities and the implementing agency for trouble free implementation of the plan.

The overall progress of the RP implementation from Jan 2014 to December 2014, as a part of Annual Report, is delineated in the subsequent paragraphs:

6.1 Appointment and Mobilization of NGO

The first task in the process of smooth implementation of the RP was appointment of NGO. The RP implementation work was awarded to NGO, named CRADLE (Consultants for Rural Area Development Linked Economy)by the Chief General Manager, BSRDC, Govt. of Bihar. The details of contract Agreement and NGO mobilization with other details are outlined in the table below:

Table-2: Details of contract Agreement and NGO mobilization with

SL No.	Name of Road	Name of NGO	Date and Contract reference of Commencement of Agreement	Date of mobilization and Office Address
1	SH-86	CRADLE	25 th January 2012	Address: M/sCRADLE Flat-K404, Patliputragram, Bajrangpur,Biskoman Colony,Gaighat,Patna- 800007, Bihar
2	SH-87	CRADLE	25 th April 2012	Contact Persons- MrParmanandDubey Tel- +91-7564901049 +91-9973388441

The duration of the RP Implementation Works Contract is for 36 months for both SH-86 and SH-87, commencing from date of mobilization in respective subprojects. The task performed by the NGO periodically, is documented in the various progress reports, submitted at monthly and quarterly interval of RP implementation.

Besides, appointment of NGO, compensation reimbursement committees was also formed at PIU officeMuzaffarpur, where representatives of the resettled families are made responsible for operation and maintenance of the community assets, upkeep of common facilities. Their initiatives helped formation of SHG, setting up of Information/ Grievance Redress Centres and networking with the local NGOs.

Anuradha Chardra (Shuri Manager (Tech.)

6.2 Identification and Verification of Affected Persons and Community Properties (CPRs)

6.2.1 Training to Survey Staff for Identification and Verification Work by NGO

Training was provided to survey staffs, who have been working for identification and verification of affected properties/ persons. These training was organized and provided by the key professional and Experts of different domains. The detail of training, provided to concerned survey staff, is clarified in the table below:

Table 3: Training to Survey Staff by NGO

SI. No.	Name of NGO, who Organized the Training Programme	No of survey Staff, attended the Training	Date of Training Programme	Name of Trainers/ Domain Specialist
1	CRADLE	6	27 th Jan to 2 nd Feb 2012 (SH-86) and 26.04.12 to 02.05.12 (SH-87)	 RampujanSahni – Field Supervisior. Upendra Kumar Singh – Field Supervisor Raj Narayan Bhagat – Technical Support professional Mr. Prem Kumar, Technical Support professional, CRADLE Mr. Madhukar Kumar, Technical Support Professional, CRADLE Mr. Sanjay Kumar, Technical Support Professional, CRADLE Mr.Sanjay Kumar, Technical Support Professional, CRADLE

Source- Different progress report submitted by the NGO

Monitoring and Resettlement Plan Implementation Report (Annual R & R Report 2014)

Page 12

Anuralla, Chandra

6.2.2 Verification of Affected Households

The NGOsappointed for RP implementation, successfully working on the assignment as per TOR. Resettlement Plan Report, prepared at the time of detailed Design of the project was updated, keeping in mind the impact on population as per final design. At the time of updating of RP, verification of affected households was done by the NGOs. Accordingly, the final list of affected households was prepared in the process to update the list of affected people. It was observed that there was sharp diminution in the number of affected households from approved RP to final updated list. As per updated list of APs, which will form the basis of preparation of Micro Plan, the details of affected households are presented in **Table-4**.



Table-4: Comparative Chart of No of Affected Household as per Approved RP and after verification of affected households

S. No.	Impacts	Catego ry of APs	Impac	t In RP	time Imple	t at the of RP mentation	Remarks
			SH-86	H-86 SH-87 SH- 86	SH-87		
1	Total	TH	125	1117	10	154	i.SH-86-Microplan of TH and NTH
	number of Affected Structures/ Properties	NTH	Sq-5 Total – 5	Enc-86 Sq-88 Total- 174	166	324	has been approved ii.SH-87-Microplan of NTH has been approved but For
	Total number of		463	2799	623	1101	TH it is under

Monitoring and Resettlement Plan Implementation Report
(Annual R & R Report 2014)

Aruradha Chandra

Manager (Tech.)

	households affected	TH					process and the data is
2		NTU	-	174	166	22.4	tentative.Due to change of Alignment
		NTH	5	174	166	324	* As per AIDE MEMORIE (Annexure-9)

Source- Approved Resettlement Plan of sub-projects and different progress report submitted by the NGO

6.2.3 Verification of Affected Community Structures (CPRs)

Impact on CPRs is a very critical issue for the point of view of community. The community feeling is attached with the community properties especially with the religious structures. It was observed by the monitor that there are different figures on the impact of CPRs in approved RPs and in the verified list of CPRs by the supervision consultant, submitted by the NGO. At the implementation stage, the impact on CPRs increased because of unaccounted at the time of DPR stage.

When enquired about, it was explained by the executing agency, NGO and supervision consultant that keeping in mind the importance of these CPRs for the community, the demolition of these CPRs were avoided for all the sub-projects and where it was not possible to avoid the demolition, the impact was minimized. The details of CPRs mentioned in approved RP report and actual impact on CPRs at the time of implementation stage presented in **Table-5**.



Monitoring and Resettlement Plan Implementation Report (Annual R & R Report 2014)

Anuradha Chandra

^{*} AIDE MEMORIE -19th May 2014 of ADB. I) An engineering solution such as provision of RE wall/toe wall will be considered and adopted to minimize the land acquisition. ii.) If land acquisition within a reasonable time is not considered feasible, works will be undertaken within the existing ROW.

Table-5: Community Structures as per Approved RP and Micro Plan

_	Duniant	Structures			eact on Community tructures (CPRs)	
S. No	Project Road	As per RP	As per NGO List Report	Verified by Supervision Consultant	Remarks	
1	SH-86	14	Religious- 20 Govt09 Total-29	29	At implementation stage, there is significant increase in number of	
2	SH-87	8	Religious- 31 Govt19 Total-50	50	CPRs. It happens due to execution of work within available ROW with implementing the engineering solution as per site condition.	
_	Total	22	79	79		

Source- Approved Resettlement Plan of sub-projects, micro plan and different progress report and project completion report, submitted by the NGO

It is important to mention here that even during interaction of the R&R cum Social Development Expert of Supervision Consultant with community people; it was revealed that the EA has resolved such issue with proper public consultation and providing engineering solution by avoiding impact on common property.

6.2.4 Relocation/ Enhancement Status of Affected CPRs

At this juncture of implementation the status on shifting, installation, constructions and reconstruction of CPRs is in progress and at different stages of relocation. The status of impacted 29 CPRs (20 religious structures & 9 Govt. Structures) in SH-86 and the status of impacted 50 (religious - 31, & Government - 19) CPRs in SH-87 sub-project is progressed up to finalization of relocation site are in progress. Consent from local community has been received for almost all the CPRs in both the sub-projects. The Relocation/ Enhancement status of affected CPRs presented in **Table-6**.

Table-6: Community Structures as per Approved RP and Micro Plan

S. No	Project	Relocation/ Enhance	cement of Community Structures

Monitoring and Resettlement Plan Implementation Report
(Annual R & R Report 2014)

Anuadha Chandra

Manager (Tech.)

	Road		CPRs)	
		Verified by Supervision Consultant	Verification of Relocation Site	Achieved Percentage
1	SH-86	29	29	0 %
2	SH-87	50	50	0%
	Total	79	79	5000.00%

6.3 Disclosure and distribution of Public Information Brochure (PIB) and Entitlement Matrix

Translation of the summary and entitlement matrix of RP in vernacular language and its disclosure to the affected people was done by Executing Agency. This task is important because it discloses the entitlement provision of compensation and assistance to the affected people of different categories under Resettlement Framework. During field verification and consultation with stakeholder's, it was revealed that the NGO has distributed the translated version of RP to affected people and other stakeholders and same was disclosed to affected people at various identified locations to make them acquainted with the provision of compensation and assistance to affected people. The dates of disclosure are given in **Table-7** and disclosure plan is annexed as an **Annexure - 1**.

Table-7: Details of RP Disclosure

S. No.	Resettlement Plan Report for Project Roads	Date of RP disclosure to the affected AP's
1	SH-86	March 2012
2	SH-87	June 2012

Source- MPR/QPR Report submitted by SPS & CRADLE

6.4 Counseling (Consultation) with Entitled Persons

During and after disclosure of Resettlement Plan in local language many meetings were organized by the DGM with consultants, R&R officials, NGO and successfully convinced the APs about the importance of the project for their betterment.

The concerned NGO organized several meetings with affected families for hearing of any issues regarding project implementation. In these meetings people were made aware about Resettlement and compensation issues, redressal of grievances, if any, advantages of the project and documented their suggestion regarding project.

The interactions and consultations with other stakeholders especially the village headman (Mukhiya) have brought in an interesting dimension for the consideration of the project authorities in terms of minimizing the further squatting and encroachment across the project stretch. Village headman assured

Anurall of Chandra
(Tech.)

that they would assist in removing encroachments and suggested that notices should be put along the highway to prevent further encroachments. The consultations with the officials of district administration including land/ revenue officials conducted under the Chairmanship of District Magistrate have helped in getting assurance from them in terms of all the co-operation and support for the implementation of the project.

The consultations were centered around formation of Self Help Groups (SHGs) and livelihood options exploration as quite a large percentage of APs fall under the category of labours who primarily work in the agricultural fields during the season and during other period, most of these either remain unemployed or go to the nearby towns for other works of unskilled nature. The detail of consultation meeting at different locations of the sub-projects with the number of participants is briefed in **Annexure-2**.

6.5 Preparation of Micro Plan (NTH) and Compensation Schedule

In accordance with the updated RP and after joint verification of affected people, a Micro Plan was prepared by the NGO. The prepared micro plan was duly verified by the ARO of concerned PIU and final submission was made by NGO for approval. The Micro plan of SH-86and SH-87 is approved by Executing Agency. The summary of micro plan, which has all the details of affected households with compensation and assistance, is presented in **Table-8** and **Table-9**.

Table-8: The Number of Affected Households as per Micro Plan

Name of	No. of Affected Family				
Name of Road	Squatte rs	Encroache rs	Tenants/ Others	Total	
SH -86	116	50	0	166*	
SH -87	132	192	0	324	

Source- Monthly progress Report (MPR), Micro Plan

166*= 154 NTH+8 Enc NV+4 TH

Similarly, the total R&R budgets for the proposed sub-project i.e., (SH-86) and (SH-87) which included the cost of compensation of structures, assistance and training support etc.are**Rs.** 41,38,553.**00 and Rs.** 78,34,303.**00 respectively**. However, the Resettlement budget of SH-86 &SH-87 for Non-Titleholder has been approved by General Manager, BSRDC-L in month of November 2013(**Annexure-3**). The detailed Resettlement budget for SH-86 and SH-87 sub-projects roads are summarized in the **Table-9**.

Anuradha Chandra Manager (Tech.)

Table 9: Resettlement Budget as per approved Micro plan under Different Category

SH No.	Structure Compensa tion	Shifting Assistan ce	Training Assistanc e	Special Assistan ce to Vulnera ble APs	Total Amount as per Micro Plan	Approved net Amount as per Micro Plan	Remarks
SH- 86	6,91,238	5,45000	4,16,000	53,5,000	21,87,329	41,38,553	Approved Resettle ment Budget is less from approved Micro Plan due to change in number of APs
SH- 87	16,87,964	805000	3,04,000	16,03,380	44,00,452	78,34,303	Approved Resettle ment Budget is less from approved Micro Plan due to change in number of APs

Source- Monthly progress Report (MPR), and Micro Plan

The Micro plan has been prepared for non-titleholders APs only as the identification and verification of titleholders are still in progress.

The Micro Plan for titleholders will be prepared only after completion of land acquisition process and declaration of award by the Competent Authority.

6.6 The Status of Land Acquisition Process and Declaration of Award to Affected Families

As it is already explained that Micro Plan of Titleholders are still pending due to delay in land Acquisition Process. The PIU is liaising with the land acquisition officials for completion of land acquisition process, which has already been

Monitoring and Resettlement Plan Implementation Report (Annual R & R Report 2014)

Anural! - Chandra
(Tech.)

progressed up to notification 4/6, notification 7/17, section 11 and section 12 are completed. The updated status of land acquisition progress is summarized in **Table-10.**

Table-10: Package wise Status of Land Acquisition

		Status o	Remarks				
Sr. No.		Notificatio n 4/6 Completed	Notificati on 7/17 Complete d	11	Sectio n 12 Compl eted	Disbu rseme nt Status	
1	SH-86	21	21	21	21	4	Payment under process
2	SH-87	39	36	0	0	Nil	Under Rate approval
	Total	60	57	21	21	4	

Source- Different progress report submitted by the NGO

6.7 Status on Preparation and Distribution of Identity Card (ID card)

The NGOs hascompleted the process of preparation and distribution of ID card of NTH as per the approved Micro Plan of SH-86and SH-87 respectively. The road wise status of ID Cards of APs is delineated in the **Table-11**.

ID card is duly signed by representative of NGO and representative of BSRDC. The ID cards were prepared in two copies of each AP, one copy for distribution to AP and another was kept with PIU for verification during the disbursement of assistance. The ID card, thereafter, is being distributed to APs before disbursement of compensation and assistance (Annexure - 4).

Table 11: Status of ID Cards of APs

Name of Road		Progress			
	Total no. of ID Card to be Prepared	No. of ID Card Prepared	No. of ID Card Pending for preparation	No. of ID Card Distributed	achieved (in %age)
SH-86	166 *	158	Nil	154	100%
SH-87	324	324	Nil	324	100%

Remarks: 166*= 154 NTH+8 Enc NV+4 TH

SH-86: Out of 166 APs, 8 APs are Encroacher NV. They are not eligible for the assistance as per the Entitlement Matrix. 4ID cards returned to PIU by NGO as these are now affected due to change in alignment and comes under TH category.

SH-87: Distribution of ID card is completed.

Anuradha Chandra

6.8 Opening of New Bank Account/ Verifying of Old Bank Account

Among the other issues and activities, which were the part of RP implementation, opening of new bank account and verifying the old bank account of APs, is an important task to be carried out by NGO to facilitate the compensation payment to APs? It is an essential task to be accomplished before payment of compensation and after approval of Micro Plan. The NGO has started the activities after getting approval of Micro Plan for SH-86 and SH-87. The NGO is following the necessary procedures for opening of Bank Accounts including completion of the documentary requirements for opening of bank accounts. NGO representatives assisted in opening of new bank account of each entitled person (EPs) for payment of compensation and assistance.

Moreover, while opening the new bank account it was ensured by the Executing Agency that the APs, who are having old bank account and they want to transfer the compensation amount in their old bank account, need not to open the new Bank account. The new bank account is being opened to those APs only, who do not have any bank account by their name in any bank. The road wise details of APs with Bank Account are drawn in the **Table-12 (Annexure-5)**.

Table-12: Effective Number of APs with a Bank Account

SH- No	Name of Bank/ Post Office	need to be	Verified Old Account	New Bank Account	NO. OT	Achievement Percentage
SH- 86	Nationalized Bank	166	57	109	166	100.00%
SH- 87	Nationalized Bank	324	91	233	324	100.00%

Source- NGO's Information sample verification by Supervision Consultant

6.9 Distribution of Compensation and Assistance

Distribution of compensation & assistance is in progress in SH-86 and SH-87. Out of 154 APs of non-titleholder category, compensation of all 125 APs in both the stages has been paid through cheques amounting to Rs. 21,87,329/- in SH-86 sub-project.

Out of 324 APs of non-titleholder category, compensation of 109 APs in both stages has been paid through cheque amounting to Rs. 30,01,144/- in SH-87 sub-project.

Both the sub-project roads i.e. SH-86 and SH-87 total 482 APs need to be paid and till the month of December 2014 where NGO contract is likely to be end, 247APs still not paid any R&R compensation or assistance. About 48.76% of APs has been paid so far up to December 2014.

Monitoring and Resettlement Plan Implementation Report
(Annual R & R Report 2014)

Anurall - (!andra
N -ch.)

Table-13 (a): Status of distribution APs wise (upto July 2014)

	No of APs Paid/ Unpaid			Achievem	Achievem		
SH	Part Payme nt	Full Payme nt	Unpai d/not to be paid	part	ent % in Full Payment	Remarks	
SH- 86	109	109	45	70.78	70.78	Compensation Payment to DPs is	
SH- 87	110	108	216	33.95	33.33	still lagging behind even if NGOs terms are matured.	

Table-13 (b): Status of distribution in Amount (upto July 2014)

SH No.	Compensation Amount Approved	Amount Paid as Compensatio n	Balance to be paid	Progress (in %age)
SH-86	41,38,553	16,58,399	24,80,154	40.07%
SH-87	78,34,303	30,01,144	48,33,159	38.31%

Table-13 (c): Status of distribution in Amount (upto Dec 2014)

	No of APs Paid/ Unpaid			Achievem	Achievem		
SH	Part Payme nt	Full Payme nt	Unpai d/not to be paid	part	ent % in Full Payment	Remarks	
SH- 86	125	125	29	81.17	70.78	Compensation Payment to DPs is	
SH- 87	237	108	216	33.95	33.33	still lagging behind even NGOs terms are matured.	

Table-13 (d): Status of distribution in Amount(upto Dec 2014)

SH No.	Compensation Amount Approved	Amount Paid as Compensatio n	Balance to be paid	Progress (in %age)
SH-86	41,38,553	21,87,329	19,51,224	52.85%
SH-87	78,34,303	44,00,452	34,33,851	56.17%

Acting upon the entire development, team member with support staff of NGO and Executing Agency has visit the designated location for distributing the cheques to all the eligible APs.

After close consultation with local PRI leader, a time table and locations of convenience need to be finalized by the NGO and Executing Agency for delivering the cheque to the APs after taking the signature on payment register.






ARO presenting cheque to AP in SH-86

ARO presenting cheque to AP in SH-87

Anuradha Chandra
Ma : Ter

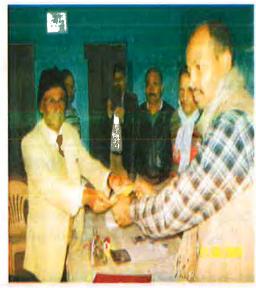



Distribution of Cheque amongst Land owner(TH)

6.10 Training Programme for Income Restoration

The training of APs was an essential component in the implementation of the R&R activities. The objective being to upgrade/enhance the skills of the APs so that they may utilize these skills in income generating or any other economic activity so that the quality of life or the socio-economic condition of the APs is improved.

Each entitled AP has got training toolkit, that contained one bag, Pen, Pad, Training book and Training material to start the income earning/enhancing pursuits. Each AP who attended training program has been distributed Training certificate also. Breakfast, lunch and transport facility has also given to each AP.

Training program has to be organized the details are presented in table below.

Table -14 Proposed date for Training Programme in SH-86 Sub-project

Batch	Village/Place	Date of	No of Eligible APs			Name of the Training Scheme
No.		Training	Male	Female	Total	Training Scrience
1	Mohamadpur Via - Chakia	11 th Jan to 13 th Jan 2015	25	0	25	a. Candle Making b. Agarwati
2	, - Do-	16 th Jan to 18 th Jan 2015	25	6	31	making and c. Paper bags

Baseline socio-economic survey of the APs has been completed as per approved Micro Plans of SH-86 and SH-87 sub-project. Identification of willingness of training trade, trainer, scope of business opportunities are in progress. Convergence & dovetailing with line department central & state government schemes like, thrift & credit societies (SHGs) of horticulture & dairy federation, SGSY, SIDBI and MNREGA etc. are in progress.

During public consultation & disbursement of compensation, NGO is identifying the willingness of training trade. Training program will be organized by NGOwith the help of all the concerned PIU at different locations of project area for income restoration of eligible affected persons. Training schedule will be prepared with the help of village head and representative of APs as per their convenience.

6.11 Appraisal of Other R & R Issues

An interaction with officials of BSRDC-L and other stakeholders and site visit was done by the R&R cum Social Development Expert to substantiate the status of RP implementation executed by the executing agency with the help of NGO. During the field verification, the R&R cum Social Development Expert also had interaction with the community people and asked their view on the handling of resettlement issues by the NGO.

However, during Focus Group Discussion (FGD) and verification of affected persons the R&R cum Social Development Expert reviewed the progress of RP implementation being executed by the NGO. These are related to appraisal of R & R issues, which is delineated in the subsequent para.

Monitoring and Resettlement Plan Implementation Report (Annual R & R Report 2014)

Anuradles Plandra

6.11.1 Addressing HIV / AIDS Issues in Road Development Projects



Though road project emphasizes more on engineering aspect like technical and economic viability of the project but in ADB assisted project, social responsibility becomes important. Prevention and control of HIV/AIDS transmission is one of the important social responsibility. Hence prevention and control of transmission of HIV/AIDS have become important social responsibility of present road projects. It is well established that because of improvements of road, mobility of CSWs and truckers also increases and chances of transmission of HIV/AIDS. Having understood the requirement of action for the HIV/AIDS Awareness Programme at construction stage in road project.

- a) Action to increase the level of awareness about prevention and control of HIV/AIDS among the different communities in project road.
- b) Action to promote safe sex behavior through promotion of condom use and developing referral awareness for medical care and treatment of STD.
- c) Action for Institutional strengthening capacities of various stakeholders in order to enable an effective behavior change among high-risk groups and vulnerable populations towards the prevention of HIV/AIDS.

6.11.2 Action on HIV/AIDS Awareness Prevention Campaigns



In order to make the people aware about the fatal highway diseases, the NGO with the help of Contractors have been conducted HIV/AIDS Awareness Prevention Campaign by conducting HIV/AIDS awareness Camps at different Locations on sub-project roads.

Road construction workers' follow up activities have been conducted in construction camp to provide counseling/ advisory on HIV/AIDS (condom provision), voluntary confidential counseling for testing (VCCT) and STI treatment, provision of condoms and to promote and ensure provision of health and environmental sanitation through latrines and safe drinking water at labour camps of SH-86 and SH-87 sub-project (Raghunathpur and Kupri Camp).

To increased (100%) condom use, the program plans to distribute condoms for community, construction workers and high risk groups along the SH-86 and SH-87 sub-project. Approximately 1500 sets of condoms have been distributed in the program. The distributions of condoms have been done carefully so as to facilitate at camp sites of the road construction workers and stakeholders.

In addition, the NGO has initiated individual interviews, personal contacts, and group discussion at possible hot spots like hotel/ dhaba owners, the potential HIV/AIDS carrier-truckers and their helpers and assistant, pedestrians, local community people etc. for generating awareness among them to prevent the incidence of fatal diseases. The details are presented in table below:

Monitoring and Resettlement Plan Implementation Report
(Annual R & R Report 2014)

Anuadha Chand

Table-15: Public Consultation on HIV/AIDs Related Issues

SI.	Williams / Location of FCD	Partic	cipation of c	ommunity
No.	Village/ Location of FGD	Male	Female	Total
		SH-86		
1	Raghunathpur	16	0	16
2	Nawada	17	0	17
3	Mahamadpur	14	10	24
4	Jaitpur	14	9	23
- 5	Chakia	13	0	13
6	Jahangirpur	14	8	21
7	Distolia	13	4	17
		SH-87		
8	Kwari	12	7	19
9	Nawadih	18	5	- 23
10	Rasulpur	12	5	17
11	Sarifpur	18	7	25
12	Ganguli	11	0	11
13	Chainpur	15	4	19
14	Naravanpur	18	9	27
15	Barahi	06	0	06

6.11.3 Compliance of Labour Laws, Prohibition of Child Labour

Children below the age of 14 years should be restricted from getting involved in the construction activities and wage employment. It is the responsibility of PIU, Project Manager and NGOs to ensure that no child labour is engaged in the activities. This requires close coordination with the Supervision Consultants for effective monitoring for control on child labour. Any complaint received in this regard necessary action as per the Child Labour (Prohibition & Regulation) Act, 1986 will be taken up. This may include (i) imposing penalty, (ii) Black listing of the firm and (iii) taking other legal measures.

NGO is continuously assisting; the Engineers (Supervision Consultants) for ensuring the Contractors are abiding by the various provisions of the applicable laws, concerning the worker's safety, health and hygiene and the child labour issues. According to laws, there were specifications regarding the facilities/requirements at the construction camp/site, including basic health care facilities and facilities for vaccinations, day crèche facilities, etc. It is being monitored by the R&R cum Social Development Expert of Supervision Consultant with the help of Resident Engineer and or representative of the Contractors, to ensure the compliance of Labour Laws and prohibition of Child Labour in a satisfactory manner and in compliance with Contract agreement.

Anuradha Chand

6.11.4 Compliance of Gender Issues

From the specific consultation with women group it is revealed that the status of women in the project area which is characterized by low female literacy, distressed health and nutritional conditions, low proportion of women in work participation, etc. There are 9 women headed affected families in SH-86 Sub-Project, 19 women headed affected families in SH-87 Sub-Project. During consultations, it was found that majority of them often uses road for collection of fuel wood, travelling for market place and social work and crosses road quite frequently.

NGO is also assisting; the Engineers (Supervision Consultants) for ensuring the Contractors are abiding by the provisions of the applicable laws, concerning the gender issues. According to laws, there were specifications regarding the facilities/ requirements at the construction camp/site, including basic health care facilities, Mother and Child Welfare units etc. It is also being monitored by the R&R cum Social Development Expert of Supervision Consultant with the help of Resident engineers and or representative of the Contractors, to ensure the compliance of Gender Issue in a satisfactory manner. Hence no gender disparity was identified by the Monitoring Team during field investigation.

6.11.5 Grievance Redressal

It would be pertinent here to refer the Asian Development Bank's policy, which requires proper mechanisms for resolution of disputes that may arise from any aspect of the compensation and development process. The mechanisms should be "affordable and accessible," and third parties independent of the implementers should be available at the appropriate point in the process. The grievance procedure need to be simple, administered in the first instance at the local level to facilitate access, flexibility and open to various proofs taking into account the need for speedy, just and fair resolution of their grievances.

In the course of RP implementation for this project, the Executing Agency facilitated with the help of NGO for the constitution of Grievances Redressal Committee (GRC) at district level for all the sub-project roads. The status of constitution of GRC at sub-project level is summarized in the table below:

Table-16: The Status of Constitution of GRC at Sub-Project Level

	Districts for Constitution of GRC	Initiative taken By PIU for Constitution of GRC	Status of Constitution of GRC	Remarks
SH-86	Muzaffarpur	Yes	Yes	Constituted
SH-87	Sitamarhi	409 date 19.05.12	305 date 16.04.13	Constituted

Monitoring and Resettlement Plan Implementation Report (Annual R & R Report 2014)

Anuradhe Chandra

Moreover, one grievance received/ reported from the field which has been addressed by Additional Collector. During the field visit of R&R cum Social Development Expert grievances were received from the affected population. (Annexure- 10).

6.11.6 Problems Encountered and Resolved

There was no major dispute and grievances, received from the affected persons, however, any grievances and doubts of the APs was redressed by the Executing Agency with the consultation of local community/ authorities, and through awareness campaign etc. however, there is need to work on other activities of RP implementation apart from Micro-plan and ID card preparation, which has no direct relation with approval of Micro Plan. Such activities are related with:

- HIV/AIDS Awareness programme/ Workshop,
- Identification of training Need and Training programme for NTHs,
- Information on Labour on Construction site, etc.
- Speed up of Land Acquisition process

Moreover, no major problem has been noticed/ observed by the External Monitoring team during field verification to incorporate in the report.

7.0 RECOMMENDATIONS FOR PROPER AND TIMELY IMPLEMENTATION OF RP

As indicated above a system of random assessment was followed to permits qualitative reporting on performance and effectiveness in the resettlement, compensation, and livelihood restoration on the participation of community and concerned authorities, and on the overall performance of grievance/ complaints resolution etc.

Up to this stage the RP is being implemented as per provision of Approved RP report and is complied with the applicable State laws, National laws, and ADB's Involuntary Resettlement policy (1995). However certain steps need to be taken by BSRDC for its smooth and timely implementation of RP.

7.1 RP Implementation Consultant (NGO)'s Compliance on Objectives of the Assignment

The best practice for smooth and timely implementation of RP is to complete its major tasks on or before commencement of actual construction work or mobilization of Contractors. However, for these sub-projects, it seems that action on many activities is either delayed or unheeded, such as mobilization of named key professional on regular basis, no. of visit of key professionals especially women key professionals and outcome of the women's consultation with proper

Manager (Tech.)

Monitoring and Resettlement Plan Implementation Report
(Annual R & R Report 2014)

Anuadha Chandra

documentation and action plan on Gender specific issues, database record of Affected Persons (APs/DPs), training programme for Income Restoration, especially for SH-86 and SH-87 sub-project and disbursement of compensation payment etc., which has hampered the timely implementation of Resettlement Plan.

The Executive Agency ensure the timely completion of all major tasks by instructing the RP Implementation Consultant (NGO)

7.2 Completion of Land Acquisition Process on Fast Track

The Land acquisition process is progressing on very slow pace, which is inviting delay in RP Implementation Process. The Executing Agency need to speed up the tasks required for accomplishment of Land acquisition process so that RP implementation could be completed within the time frame.

7.3 Meeting of Grievances Redressal Committee

There is no reporting on meeting of GRC from any sub-project road, while GRC meeting is mandatory on regular interval as per ADB Guidelines. In case, there are no grievances, the MPR /QPR report of NGO should mention that no grievances are received from any sub-project road.

7.4 Training Programme for Income Restoration

There is a provision of assistance for Income restoration of affected people (APs) and a budgetary provision has been made it by the Executing Agency as per entitlement. It has been observed that the NGO, appointed for SH-86 and SH-87 have not organized any training program for Income restoration of eligible affected persons at this stage.

It is suggested, the training amount, meant for eligible APs, should be paid to those APs, for income restoration, even if they were not willing to join the training programme as it was under their entitlement and it should be paid to them.

7.5 Records of Relocation of DPs after Compensation Payment

It was expected that NGO should record and report in its MPR /QPR that how many structures have been relocated from the project site after receiving the Compensation payment. However, no record is being furnished by any NGO in any of its reports.

It is suggested that the Executing Agency should instruct the NGO that they should record date wise relocation / evacuation of DPs from the existing location.

Anuradha Chandra

Manager (Tech

7.6 Special Assistance to Vulnerable APs

Hardly any special arrangements were made by the NGO for those vulnerable people, who by any reason are not able to come or arrange their own transportation to come to the set locations for opening of Bank Account and receiving cheques. As per ADB safeguards policy, the vulnerable people need be given special assistance in receiving their compensation payment.

The following measures are suggested herewith to be taken by the Executing Agency and the NGO for vulnerable persons:

- Vulnerable persons should be given special consideration on reaching the Centres/ Bank for opening the Bank Account and receiving the Cheques;
- Transport facilities should be provided to those who wanted to reach the Centres for receiving the cheques and were having no transportation facilities;
- For those who are not able to reach the meeting Centre, the representative of NGO/ Executing Agency should visit the AP to his residence, to help them their deserving compensations.


7.7 Way out for Completion of Work even after the Terms of RP Implementation Consultant is matured

The terms of RP Implementation Consultant is either matured or on the verge of maturity, while major tasks of assignment are significantly incomplete. The RP implementation work for titleholders are still at preliminary stage and none involvement of NGO at this stage of RP implementation activities may cost to the project implementation. It may be treated as non-compliance of ADB Safeguards Policy.

Hence, a way out is required from Executing Agency to make sure that RP implementation work should be continued uninterrupted.



ANNEXURES



ANNEXURE-1





बिहार स्टेट रोड डेवलपमेन्ट कॉरपोरेशन लिमिटेड,

परियोजना क्रियान्वयन इकाई, पथ निर्माण कैम्पस माड़ीपुर, मुज्जफरपुर, बिहार

पान्त्रता सारणी

SH -86 & SH 87



मुख्यालय:- क्रेंडल, C-258, रोड नं० 1-C,अशोकनगर, राँची प्रोजेक्ट कार्यालय:- क्रेडल, शहबाजपुर, भीखनपुर कोठी, उमानगर, मुजफ्फरपुर

पात्रता सारणी

र्व क्षेत्र कुर्युक्त्रोत्त क

हानि के प्रकार	प्रभावित परिवार की पहचान	अधिकार	विवरण
अ. भूगि की हानि	He was a second of the second		
12577.45 17 _7 12 1 -42	क. भूस्वामि ख. परंपरागत अधिकार प्राप्त प्रभावित व्यक्ति		अ. प्रतिस्थापन भूमि या नगद मुआवज प्रतिस्थापन मूल्यानुसार जो बिहार पुर्नस्थापना ए पुर्नवास के तहत बी.एल.ए.आर.आर.पी. 2007 प आधारित है। ब. अगर शेष भूभाग कृषि योग्य नहीं है अर्थात प्रमावित व्यक्ति सीमांत किसान हो जाता है त ऐसी अवस्था में प्रभावित व्यक्ति के पास तीविकल्प हैं: • प्रभावित व्यक्ति शेष भूभाग पर काबिज रहेगा और जितनी भूमि अधिग्रहित के गई है उत्तनी भूमि का मुआवजा ए सहायता देय होगा। • अगर प्रभावित व्यक्ति शेष भूभाग का भी अधिग्रहण चाहता है तो कार्यान्वयन संस्था शेष भूभाग का अधिग्रहण करेगा मुआवजा एवं सहायता राशि सम्पूष भूभाग के लिए दी जाएगी जिसमें शेष भूभाग की भी राशि सम्मिलत होगी। • अगर प्रभावित व्यक्ति विपन्न वर्ग का अधरात प्रभावित व्यक्ति विपन्न वर्ग का असरा प्रकार के फीस, स्टाम्प इयूटी एवं अन्य सा सभी प्रकार के फीस, स्टाम्प इयूटी एवं अन्य सा सभी प्रकार के फीस, स्टाम्प इयूटी एवं अन्य
. घरबारी भूमि की जनि (आवासीय वं व्यवसायिक मि)	क. भूस्वामि ख. परंपरागत अधिकार प्राप्त प्रभावित व्यक्ति	प्रतिस्थापन लागत पर क्षतिपूर्ति राशि	खर्च (विधिनुसार) पुर्नस्थापना एवं पुर्नवास र लगेंगे, का वहन क्रियान्वयन संस्था करेगी। अ. प्रतिस्थापन भूमि या नगद मुआवज प्रतिस्थापन मूल्यानुसार जो बिहार पुर्नस्थापना एव पुर्नवास के तहत बी.एल.ए.आर.आर.पी. 2007 प्र आधारित है। ब. सभी प्रकार के फीस, स्टाम्प ड्यूटी एवं अन्य खर्च (विधिनुसार) पुर्नस्थापना एवं पुर्नवास में लगेंगे, का बहन क्रियान्वयन संस्था करेगी।


4. किराये के आवास की हानि	Province of the A Province of the A	क. प्रतिस्थापन लागृत पर क्षतिपूर्ति राशि ख. स्थानान्तरण भत्ता क. किराया भला ख. प्रतिस्थापन लागत पर क्षतिपूर्ति राशि	अ. प्रभावित व्यक्ति को आवासीय संरचना के लिए प्रतिस्थापन मुल्य दिया जाएगा जो बेसिक शेड्यूल रेट के अनुसार बिना हास मूल्य के देय होगा। ब. रू. 10000/— स्थानान्तरण भत्ता के रूप में। स. प्रभावित व्यक्ति को ढाए गए निर्मित स्थल से मलंबे के ढेर को बिना मूल्य के ले जाने का अधिकार होंगा। द. किराया भत्ता जो प्रचलित दर के अनुसार, जो अधिकतम तीन महीने के किराये के लिए देय होगी। अ. आवासीय एवं व्यवसायिक दोनो किरायेदार को किराया भत्ता जो प्रचलित दर के अनुसार, जो अधिकतम तीन महीने के किराये के लिए देय होगी।
		ग. स्थानान्तरण भत्ता	ब. किरायेदार द्वारा अतिरिक्त संरचना निर्माण की स्थिति में किरायेदार को क्षतिपूर्ति देय होग जो कि भूस्वामी के कुल मुआवजा राशि से काट कर दी जाएगी। स. नए स्थान में स्थानान्तरित होने के लिए आवास एवं घरेलू सामान के अनुसार स्थानान्तरण भत्ता। द. किरायेदार द्वारा भूस्वामी को अगर अग्रिम राशि दी गई है तो सबूत जमा करने पर वह भी भूरवामी के कुल मुआवजा राशि से काट कर किरायेदार को दी जाएगी। य. किरायेदार द्वारा निर्मित स्थल से मलबे के ढेर को बिना मूल्य के ले जाने का अधिकार होगा।
	चना को हानि उपवेशियो द्वारा निर्मित संस्वना	कोई क्षतिपूर्ति नही	अ. उपवेशियों को सूचित किया जाएगा और अपनी सम्पत्ति इटाने के लिए एक माह का समय दिया जाएगा। ब. संरचना की हानि पर प्रतिस्थापन लागत पर क्षतिपूर्ति स. रु 10000/स्थानान्तरण भत्ता द. ढाए गए निर्मित स्थल से मलबे के ढेर का अधिकार बिना किसी मूल्य के।
\(\frac{1}{2}\)	अतिक्रमणकारियों द्वारा निर्मित संख्यना	े कोई क्षतिपूर्ति नही ख. केवल विपन्न	अतिक्रमण करने वालों को सूचित किया जाएगा और अपनी सम्पत्ति हटाने के लिए एक माह का समय दिया जाएगा। ब. प्रभावित संरचना पर क्षतिपूर्ति केवल विपन्न परिवार को स. ढाए गए निर्मित स्थल से मलबे के ढेर का अधिकार बिना किसी मूल्य के।

तः फसलः एवं वृक्षाः	की हाति 💎 🛒 👉		
6. वृक्ष की हानि	म मनेकार	बाजार मूल्यानुसार क्षतिपूर्ति हॉर्टिकल्चर विभाग के सहयोग से निधारित	औसत पैदावार के अनुसार हॉर्टिकल्चर विभाग व सहयोग से निधारित की जाएगी। स. इमारती लकड़ी की हानि पर वक्ष के प्रकार
7. फसल की हानि	क. भूस्वामि	बाजार मूल्यानुसार	के आधार पर प्रचलित बाजार मूल्यानुसार
ACC CONTROL OF	ख. बटाईदार ग. पहेदार	क्षतिपूर्ति कृषि विभाग के सहयोग से र्निधारित	अग्रिम सूचना दे दी जाए। व. खड़ी फसल की स्थिति में कृषि फसल के
य भूरवामी व अ- व	एवामी के बाजार क्षेत्र की र	प्रचना की हाति	्रा विश्व श्रीय श्रीय स्था होता ।
10 200 10 5 3 10 10 5 3 10	er i a sa saka	पुर्निस्थापन सहयोग	अ. प्रभावित उपक्रम को निम्नितिखत विकल्प दिए जाएंगेः स्वंय व्यवस्थित कर दुकान का पुर्निनेमाण दुकान चालकों द्वारा पूरे मुनाफे के साथ पात्रता सारणी के अनुसार ब. योजना पुर्निस्थापन सहयोग विकल्प उनलोंगों को उपलब्ध कराया जाएगा जिनका व्यवसायिक निर्माण व्यवसायिक उपक्रम के लिए आगे इस्तेमाल नहीं किया जाएगा जो योजना के प्रभाव के परिणामस्वरूप होगा। बाजार क्षेत्र में दुकानों का आवंटन प्रभावित दुकान मालिक की आर्थिक स्थिति के आधार पर होगा। स. रु.10000 / —स्थानान्तरण भत्ता द. ढाए गए निर्मित स्थल से मलबे के ढेर का अधिकार
8	अ-भूरवामी -(किरायेदार, पट्टेदार और उपवेशी) बाजार मेत्र में व्यवसायिक उपक्रम खोने चाले		अ) प्रभावित उपक्रम को निम्नलिखित विकल्प दिए जाएंगेः स्वंय व्यवस्थित कर दुकान का पुर्निर्निमाण दुकान बालकों द्वारा पूरे मुनाफें के साथ पात्रता सारणी के अनुसार अथवा ब. योजना पुर्नस्थापन सहयोग विकल्प उनलोंगों को उपलब्ध कराया जाएगा जिनका व्यवसायिक निर्माण व्यवसायिक उपक्रम के लिए आगे इस्तेमाल नहीं किया जाएगा जो योजना के प्रभाव के परिणामस्वरुप होगा। बाजार क्षेत्र में दुकानों

			का आवंटन प्रभावित दुकान मालिक की आर्थिक स्थिति के आधार पर होगा।
1 - 200			स. रु.10000 / —स्थानान्तरण भत्ता द. ढाए गए निर्मित स्थल से मलबे के ढेर का अधिकार
क जीविक्ताकार्जन	की हानि । १६ % अ		
 आय के प्राथमिक स्रोत करी हानि 	भूस्वामि के व्यवसायिक आय की हानि	पुर्नवास सहयोग	अ. भूस्वामी जिनके व्यवसाय की हानि विस्थापन के कारण हुई है उन्हें एकमुश्त रु 9000.00 ट्रांजिशनल भत्ता देय होगा।
	भूस्वामि के कृषिजनित आय की हानि	पुर्नवास सहयोग	अ. प्रशिक्षण सहयोग आय उत्पाद हेतु 4000/— प्रति प्रभावित परिवार जिनके प्राथमिक स्रोत की हानि हुई है। ब. सडक निर्माण के कार्य में रोजगार का अवसर, अगर वह चाहें।
- 100	अ—भूस्वामि,उपवेशी, विपन्न अतिक्रमणकारी जिनके आय के प्राथमिक स्रोत की हानि	पुर्नवास सहयोग	अ. प्रशिक्षण सहयोग आय उत्पाद हेतु 4000/- प्रति प्रमावित परिवार ब. सड़क निर्माण के कार्य में रोजगार का अवसर, अगर वह चाहे। स. राष्ट्रीय/राज्य स्तर पर मनरेगा जॉब कार्ड।
	दैनिक मजदूर जो व्यवसायिक संरचना के हटने से परोक्ष रुप से प्रभावित हुए हो	पुर्नवास सहयोग	अ. यह उस व्यक्ति पर लागू होगा जो व्यवसायिक संरचना के हटने से परोक्ष रूप से प्रभावित हुए है। उन्हें तीन महीन की सरकार द्वारा निर्धारित न्यूनतम मजदूरी दर के अनुसार रकम दी जाएगी। ब. सड़क निर्माण के कार्य में रोजगार का अवसर, अगर वह चाहै। स. राष्ट्रीय/राज्य स्तर पर मनरेगा जॉब कार्ड।
	कृषि मजदूर/बटाईदार	पुर्नवास सहयोग	अ. 200 दिन की सरकार द्वारा निर्धारित न्यूनतम मजदूरी दर के अनुसार रकम सहयोग राशि। ब. सड़क निर्माण के कार्य में रोजगार का अवसर, अगर वह चाहे। स. राष्ट्रीय ∕ राज्य स्तर पर मनरेगा जॉब कार्ड।
	लाइसेन्स धारी चल विकेता (मोबाइल वेन्डर)एवं गुगरी संचालक (किओस्क)	पुर्नवास सहयोग	अ. मोबाइल वेन्डर क्षतिपूर्ति एवं सहयोग के अधिकारी नहीं होंगे। ब. मोबाइल वेन्डर जिन्हें प्रभावित क्षेत्र में परिचालन के लिए स्थानीय अथारिटी का परिमट प्राप्त है वे कियोस्क ऑपरेटर की श्रेणी मे ही माने जाएगे। स. कियोस्क ऑपरेटर एवं मोबाइल वेन्डर जिन्हें प्रभावित क्षेत्र में परिचालन के लिए परिमट प्राप्त हैं वे एकमुश्त रु. 4000.00 सहयोग के पात्र होंगे।

10.आम जनता के सम्पत्ति संसाधन की हानि	प्रभावित समाज/संस्था	आर्थिक सहयोग/ पुर्नर्निमाण	सहयोग राशि प्रतिस्थापन दर पर अथवा सामाजिक भवन का पुर्निर्निमाण प्रभावित समाज के सहयोग के साथ
ह विपन्न वर्ग को स	हयोग 💮 💮		
11. विपन्न वर्ग को अतिरिक्त सहयोग	विपन्त वर्ग में सम्मिलित निवासी है : गरीबी रेखा से नीचे, महिला मुखिया परिवार अनुस्थित जाति, अनुस्थित जनजाति,, विकलांग और बृद्व	एकमुश्त विषेष सहयोग	एकमुश्त सहयोग राशि 10000/— रू० विपन्न परिवार के लिए (ये राशि अन्य सहयोग राशि के अतिरिक्त होगी) ।
12. निर्माण के दौरान अस्थायी प्रभाव जैसे:— आम यातायात में बाधा, जुडे पार्सल भूमि का नुकसान / सम्पति को हानि भारी मशीन की निर्माण स्थल पर आवाजाही के कारण	• मूस्वामी / प्रमावित प्लॉट के परमारागत अधिकारी	आय की हानि के लिए आर्थिक संविपूर्ति	अ. निर्माण कार्य के समय भारी मशीन की निर्माण स्थल पर आवाजाही के कारण भूमि और संरचना पर किसी भी प्रकार की हानि होने पर ठीकेदार उसका खर्च वहन करेगा। ब. ठीकेदार अनुमानित आर ओ. डब्लू के बाहर के भूस्विमियों के साथ भूमि के अस्थायी उपयोग के लिए आपसी सहमित से एक किराए की रकम तय करेगा। स. निर्माण स्थल के पास छावनी का निर्माण ठीकेदार पथ निर्माण विभाग के अधिकारियों से सम्पर्क करके तय करेगा।
13. कोई अन्य आकस्मिक प्रभाव	कोई भी बिना पूर्वामुमान	के होनेवाले प्रभाव जिसके	कारण लेखपत्र प्रस्तुत करना हो और परियोजना से परियोजना की गति धीमी पड़े।

ANNEXURE-2



3मान छिनाड २०/5/२०१५ की मान विक्रोनिका छोपछ मोगीया जिला मुजास्क्या में केडण मिन मिन एवं भाषितीं के संयुक्त तालाशांत में एन साम समा का आमी जा किया अमी, आप समा का प्रभा 3324 अह है कि विसार देश शेड डेबमपूरी बापी रिवान 4- 2TOH - 3724 44 - 86041-86 49- 2241- 24 41 1/41 15 815 81- 1941- 81. 281-8 49-8 GANI- 812- 8- 1840 43/5 8 MI- 14 HIN 812 18125 8 414 62 1849 1824 - 415 8 BAIL SHOT SHY 4- 9145 97- 981 8, 1 \$500, Northelf of 21 Thuil - 37 200 PS JOH19 - BUT BY SHOTE 4/32 / 174101 \$ MO 2017 41 2414) of 92 734 SH 43/2 60 - 346 22119 41 2414) of 92 734 UHIV, SH STONION OF MULTINGS 18211 MO241 - -415 25 3410) 13 731 2114 9- 461916 2373. ADID- Eg. 47896 8916 अग्न अभिद्धा किया नामार अग्न अग्नी अग्नी के निय अग्नि के कार निया को का का का निया को का निया को का निया को न स्थार ही स्थारती के राह तथा कार्य कार्य कार्य के पाय के कार्य 37401 Exall 811 GOILIL

क्रिस्ट ३ मिला है । जिल

Can intologist 2, 7 lac

ेराज उन्मर 21/0/3417 अर्थक, क्षार STIP- A CONTRACTE 274 217201 2071 किनो री राष भासभार 1327M 14 401 11 Pl) व्यक्तद्वराच्ये वार्ड आवृक्त वार्ड 140 2'4' E ला मानव्यवस्य (विका (CUTAPOTE या रेग रिमह (भाष्ट्र का का ग RIMER, RIMSC. Santash

(1) Bandyan Salui 19. 5.14 About 19. 5.14 About 19. 5.14

Anuradha Chandra Manager (Tech.)

.

उगान हिनांड उप ५ २०१५ है। श्राम महमद्रेष्ठ पायर धारण जरेन (जिला अभाकासा भे जिला हैस्ट केंद्र ALL & CONTINE 64 - -41-18501 3- 512-1 8 211- 8/12 भागावाव। भी स्थान भी तिस्था तर्वेष्ठा ति स्थित क ली - मि-2150 (STE) of GICIN- of BEN MAIRING of - WIENTI & 21 4 51- 48 JEN15 2297 Par 31517 HM37 0181-95 2410 & Mb- 3/8-014/9- 274). 310- 25- 41- 214 +4110. का क्योंकिमान कर डिमाजार, परंत्र गामिगा ने- कहा हि-481 (49) 2- 3/ 13 mm & 24 8 9 9 9 14) 3h, (भी - महमद्रपुर् हिं- द्वार शहला भारते हैं उसी प्रशह पि इस स्वान 37 - 945 (3241 WIL, 4800 - a114/5- 2)d)- (29105 & 313411(0141- 4=112 Ball 81 ANI Aldest Brills (185 ALIQ SAIL) 3) NIST (41) 24 XERTIO 3) - (46) 2000 UI - 69- \$500 2/4/2019-02- 50/21/ Part Part Part Contain 2011/2 2011/2 The St truth of Buth

- دامع الداده المد

ा ही रामचल्या

@ 122/2/18

3) Bugsigen

(रामशरण साह

5) राजिद्यश्रम

क्ष्य क्षाहि क्षाह

रीता देवी

के ब्रामिद्वी


(1) 2102 and 301-

Asin Hadel. Whendown Sinher 3/4/2014

221504065

9 Surgical Plis 1 231 200 AST 2501 किनोरी राम ्रेडल, प्रावनायी (19) Hydal Nall (1) Bambyan Salan (B) De difasing 21005 17, 6 WI H'MANAGE 19 CUTAPITE स्कित्ता हिन्दे (साम् काका) Santash

ANNEXURE-3





Bihar State Road Development Corporation Limited

(A Govt. of Bihar Undertaking)

Registered Office: Central Mechanical Workshop Campus, Near Airport, Sheikhpura, Patna-800014 Tel: 0612-2226711/2226723

Letter No. BSRDC Ltd.-694 /2011 - 26 8 2

Patna, Dated: 20/12/1

LETTER OF AWARD

From,

D.N. Prasad Chief General Manager.

To,

M/s Consultants for Rural Area Development Linked Economy H.Q.-C/258, Road No.-1C, Ashok Nagar, Ranchi,

Jharkhand-834002.

Selection of NGO Firm for Implementation of Resettlement Plan (RP) for Pc Sub: SH-86(SARAIYA-MOTIPUR ROAD) under Bihar State Highways Project-III (Now

Notification of Award: Resettlement and Rehabilitation Contract for Package-Reg: (SARAIYA-MOTIPUR ROAD).

Ref No.:RFP/NGO/BSHP-III Date 23.08.2011.

Sir,

Under reference to the above mentioned subject, you are being informed the proposal dated 19.09.2011 & opened on 19.09.2011 at 15.30 Hrs. for implement-Resettlement and Rehabilitation of SH-86 (SARAIYA-MOTIPUR ROAD)Consisting of 288 length for the Accepted Contract Amount of Rs. 15,50,000/-(Rupees Fifteen Lacks Fifty Thonly, Inclusive of all taxes are hereby accepted by Bihar State Road Development Corp

You are directed to submit negotiated Financial Document without change of ma proposed Team & RFP Conditions within 7 (Seven) days from issue of this letter. At the time, you are also directed to contact the Chief General Manager BSRDCL HQ Patna to p the formalities of entering into an agreement as per R.F.P. document, other related docum other terms and conditions. A copy of this letter is being sent to you through Fax/E-mail or

You are also advised to submit acceptance letter to this work order immediately entering into the agreement.

Thanking you,

Yours since

Memo No. BSRDC Ltd.-694/2011 - 2682_

(D. N. Pra Copy to: Deputy General Manager (Tech.) PIU-Hajipur for information and necessary action-

Manager (Tech.) evelopment Linter of months

CONTRACT 46, REE



Bihar State Road Development Corporation Limited

(A Govt of Bihar Undertaking)

Registered Office: Central Mechanical Workshop Campus, Near Airport, Sheikhpura, Patna 800014.

Tel: 0612-2226711/2226723

Letter No. BSRDCLtd-694/2011

Patna, Dated:

From,

Suryamani Singh

Deputy General Manager (Tech)

M/ Consultants for Rural Area Development Linked Economy,

C/258, Road No. 1C, Ashok Nagar,

Ranchi, Jharkhand

Pin-834002

Sub:

Selection of NGO firm for Implementation of Resettlement Plan (RP) for Package-II, SH-86 (Saraiya-Motipur) Road under BSHP-II-AF.

Ref:

- 1. This office letter no. BSRDCL-694/2011/2682 dated: 22.12.2011
- 2. Your letter no. CR/R&R/SH-86/161/11-12 dated: 28.12.2011

Sir,

Under reference to the above mentioned subject, we are hereby enclosing you Photo copy of Agreement for Implementation of Resettlement Plan (RP) of Package-II, SH-86 (Saraiya-Motipur) Road under BSHP-II-AF. Your Agreement No. is 02/QCBS/2012-13, Patna, dated 20.01.2012. As per the agreement the date of Commencement of Services is 25.01,2012 and date of Completion of the work is 36 (Thirty Six) months from the Date of Commencement of Services. You are directed to consult DGM (Tech), Plu-Hajipur for Implementation of this work. This work will be performed under his supervision. You are also directed to complete the work timely as per your work programme given in the Agreement. Thanking you,

Encl: As above.

Yours faithfully

301

(Suryamani Singh)

Memo No.- BSRDCL-694/2011/ 232(104)

Patna, dated: 30/01/2012

Copy to:- pGM (Tech.), PIU-Hajipur with enclosure of the Photo Copy of the Agreement for information and necessary action. You are also advised to follow the agreement and to complete the work timely as per the Agreement. You may take help of the Consultant (NGO) in L.A process as per their scope of

Encl: As above.

27/1/20/2_ (Suryamani Singh)





बिहार स्टेट रोड डेवलपमेंट कॉरपोरेशन लिमिटेड

(बिहार सरकार का एक उपक्रम) निबंधित कार्यालय : केन्द्रीय यात्रिक कर्मशाला, हवाई अड्डा के निकट, शेखपुरा, पटना - 800014

पत्रांक : BSRDC Ltd.-930/2012

पटना, दिनांक : 🛝

प्रेमक,

अमीर हसन, महाप्रबंधक (परियोजना)।

सेवा में.

उप महाप्रबंधक (तक0), परियोजना कार्यान्वयन इकाई. मुजफ्फरपुर।

विषयः राज्य उच्च पथ-86 (सरैया—मोतीपुर) में Implementation of Resettlement Plan for R&R Workके लिये Micro Plan for Title Holder की स्वीकृति के संबंध में।

प्रसंगः आपके कार्यालय का पत्रांक 265(we) दिनांक 01:08:2014

महाशय.

उपर्युक्त विषयक एवं प्रसंगाधीन पत्रों के संदर्भ में कहना है कि राज्य उच्च पथ-86 (सरैया-मोतीपुर) में Implementation of R&R Work के तहत आपके द्वारा अनुशंसित एवं समर्पित Microplan for Title Holder में कुल 22 गाँवों का Microplan जिसमें Shifting Assistance के लिये रू० 60,000/- (साठ हजार रूपये) मात्र, Training Assistance के लिये रू० 4,88,000/- (चार लाख अठासी हजार रूपये) मात्र, Special Assistance के लिये रू0 2,50,000/- (दो लाख पंचास हजार रूपये) मात्र यानि कुल मिलाकर रू0 7,98,000 / — (सात लाख अनठानवे हजार रूपये) मात्र के लिये सक्षम पदाधिकारी द्वारा निम्न शर्तों के साथ सैद्धान्तिक स्वीकृति प्रदान की गई है:--

Microplan के प्रत्येक PAFs की विवरणी स्वीकृत R.P.से मिलान कर ली जाय एवं अन्तर होने पर इसकी सूचना मुख्यालय को दी जाय।

Micro Plan का अंकगणितीय जाँच भुगतान क़े पूर्व PIU पुनः अपने स्तर से दुबारा कर लें।

PAPs को दी जाने वाली सहायता की राशि स्वीकृत Microplan के अनुसार लाभान्वितों के सारे कागजातों के जाँचोपरांत A/c Payee Cheque के द्वारा की जाय।

किसी प्रकार का दोहरा भुगतान नहीं हो। 4.

PAPs को विधिसम्मत Notice देकर ADB के नियमानुसार भौतिक रूप से जगह को खाली करवाया जाय।

ADB द्वारा रवीकृत R&R Policies का पूर्ण रूप से पालन हो। 6.

- Compensation, Assistance & Special Assistanceमें बिहार सरकार द्वारा स्वीकृत Entitlement 7. Matrix का शत प्रतिशत पालन हो।
- Before & After Implementation of R&R of PAFs, their Structures, Training Program इत्यादि कार्यों का Photography/Videography एवं अन्य कागजात PIU में सुरक्षित रखा जाय तथा मासिक प्रगति प्रतिवेदन के साथ Soft Copy (CD) में भेजा जाय।

विवाद उत्पन्न होने की स्थिति में उसका समाधान Grievance Redress Committee (GRC) के माध्यम से किया जाय।

R&R से संबंधित सारा भुगतान R&R के लिये अलग नया Joint Account खुलवाकर ही किया जाय तथा Account No. की जानकारी मुख्यालय को भी दी जाय।

R&R से संबंधित भुगतान Technical Sanction (T.S.) के अन्तर्गत स्वीकृत राशि से किया जाय। Manager (Tech.)



Bihar State Road Development Corporation

(A Govt. of Bihar Undertaking)

Registered Office: Central Mechanical Workshop Campus, Near Airport, Sheikhpura, Patna-800014. Tel: 0612-2226711/2226723

Letter No. BSRDC Ltd.-778 /2011 ー 172

Patna, Dated:

27/03/0012

LETTER OF AWARD

From,

D.N. Prasad

Chief General Manager.

To,

M/s Consultants for Rural Area Development Linked Economy

H.Q.-C/258, Road No. 1C,

Ashok Nagar, Ranchi,

Jharkhand-834002.

Selection of NGO Firm for Implementation of Resettlement Plan (RP) for SH-87 Sub:

(Runnisaidpur - Bhiswa Road) under Bihar State Highways Project-II-AF.

Notification of Award: Resettlement and Rehabilitation Contract for SH-87 Reg:

(Runnisaidpur - Bhiswa Road).

Ref No: RFP/NGO/BSHP-II-AF Date 30.12.2011.

Sir,

Under reference to the above mentioned subject, you are being informed that your proposal dated 20.01.2012 & opened on 20.01.2012 at 15.30 Hrs. for implementation of Resettlement and Rehabilitation of SH-87 (Runnisaidpur - Bhiswa Road) Consisting of 67.60 KM length for the Accepted Contract Amount of Rs. 30,00,000/-(Rupees Thirty Lacks) only, Inclusive of all taxes are hereby accepted by Bihar State Road Development Corporation Limited.

You are directed to submit negotiated Financial Document without change of man days, proposed Team & RFP Conditions within 7 (Seven) days from issue of this letter. At the same time, you are also directed to contact the Chief General Manager BSRDCL HQ Patna to perform the formalities of entering into an agreement as per R.F.P. document, other related documents & other terms and conditions. A copy of this letter is being sent to you through Fax/E-mail or Speed post.

You are also advised to submit acceptance letter to this work order immediately before entering into the agreement.

Thanking you,

(D. N. Prasad)

Memo No. BSRDC Ltd.-778 /2011 _ 772

Patna, Dated: 27/03/2011

Copy to:Deputy General Manager (Tech.) PIU-Hajipur for information and necessary action

Anuradha Chandra (D. N. Prasad)

Manager (Tech.)

tte For Roral Area Develops, end underd Figure ()

उप महाप्रबंधक (तकनीकी) का कार्यालय परियोजना कार्यान्वयन ईकाई-3 बिहार स्टेट रोड डेवलपमेंट कॉरपोरेशन लिमिटेड, हाजीपुर

	र्ग ऽ ७ ८७ । हाजीपुर	
पत्राकः	6 ong	

दिनांकः 3/9/1

प्रेषक:-

उप महाप्रबंधक (तकनीकी) परियोजना कार्यान्वयन ईकाई-3 बिहार स्टेट रोड डेवलपमेंट कॉरपोरेशन लिमिटेड, ए-1, गंगा ब्रीज कॉलोनी, हाजीपुर

सेवा में.

जिलाधिकारी महोदय. सीतामढ़ी।

राज्य उच्च पथ सं0–87 (रून्नीसैदपुर–भिसवा) पथ के चौड़ीकरण एवं मजबुतीकरण विषय:-हेतु शिकायत समाधान समिति (Grievance Redressel Committee) के गठन के संबंध

इस कार्यालय का पत्रांक 409 अनु० / हाजीपुर दिनांक 19.05.2012 प्रसंग:-

महाशय, उपरोक्त विषयक प्रसंगाधीन पत्र की छाया प्रति संलग्न करते हुए सूचित करना है कि राज्य उच्च पथ सं0-87 (रून्नीसैदपुर-भिसवा) पथ के चौड़ीकरण एवं मजबुतीकरण कार्य हेतु एशियन डेवलपमेण्ट बैंक के पुर्नवास एवं मुर्नस्थापन नीति के तहत परियोजना प्रभावित परिवारों के शिकायतों क समाधान हेतु शिकायत समाधान समिति का गठन अभी तक नहीं हो पाया है। प्रसंगाधीन पत्र द्वारा शिकायत समाधान समिति (Grievance Redressel Committee) के गठन हेतु अध्यक्ष के रूप में स्वंय अथवा अपने प्रतिनिधि को नामित करने हेतु अनुरोध किया गया था।

अतः अनुरोध है कि ADB के पुर्नवास एवं पुर्नस्थापन नीति के तहत प्रसंगाधीन पत्र के आलोक में शिकायत समाधान समिति (Grievance Redressel Committee) के अध्यक्ष के रूप में स्वयं अथवा अपने प्रतिनिधि को नामित करने की कृपा की जाय।

धन्यवाद!

विश्वासमाजन,

अनु0- यथोक्त।

उप महाप्रबंधक (तकं0)

ज्ञापाकः 758

हाजीपर

दिनांकः 3(911)

प्रतिलिपिः जिला भू-अर्जन पदाधिकारी, सीतामढ़ी को सूचनार्थ एवं आवश्यक कार्रवाई हेतु प्रेषित।

Manager (Tech.)

5.0 Assistance as per Micro plan

Table No. 8. Assistance as per Micro Plan

				Entitlement							
Category	Total No. of AFs	Total No. of Commercial AFs	Assistance for structure	Shifting Assistance	Special Assistance to Vulnerable	Training	Total				
Squatter Vulnerable	65	61	500603	650000	650000	244000	2044 6 0 3				
Squatter Non Vulnerable	51	49	520444	510000	NE	196000	1226444				
Encroacher Vulnerable	42	19	371506	NE	420000	76000	867506				
Encroacher Non Vulnerable	8	3	NE	NE	NE	NE	0				
Total	166	132	1392553	1160000	1070000	516000	4138 5 5 3				
		Cost of Training	as per RP page n	0. 59		300000	300000				
	Grand Total		1392553	116000	107000	816000	4438553				

Total Value of Micro Plan= 44,38,553.00 (Rs. Forty four lakh thirty eight thousand five hundred and fifty three

only)

NGO Representative/Team Leader

CRADLE

Anager (Tech.)

DGM (Tech.)

BSRDCL, PIU, Muzaffarpur



							5	ocia	Cate	ory		Ту	pe of \	/ul.		E a			9 5	G
SI. NO.	Village Name	Total AFs	Sq	Enc	V	NV	sc	st	ОВС	Gen	BPL	APL	WHH	Cast C	РНС	Compensation for structure	Shifting Assistance	Training Assistance	Special Assistance to Vulnerables	Total
1	Mohammadpur	19	18	1	17	2	3	0	16	0.	17	2	0	0	0	151751	180000	64000	170000	565751/
2	Chakia	1	1	0	1	0	0	0	1	0	1	0	0	0	0	5436	10000	4000	10000	29436 ,
3	Bisar Patti Chowk	1	1	0	1	0	0	0	1	0	1	0	0	0	0	25368	10000	0	10000	45368
4	Raghunath pur	24	7	17	16	8	8	0	12	4	16	8	0	0	0	216807	70000	28000	160000	474807
5	Nawada	5	2	3	3	2	3	0	2	0	3	2	0	0	0	61885	20000	8000	30000	119885
6	Jaitpur	53	50	3	27	26	3	0	44	6	25	26	0	1	1	545046	500000	204000	270000	1519046
7	Basra	29 /	25	4	12	17	0	0	26	3	11	17	1	0	0	151755	250000~	116000	120000 /	637755
8	Jagaria	10	2	8	7	3	0	0	8	2	7	3	0	0	0	65795	20000	28000	70000.	183795
9	Manikpur	1	1	0	1	0	0	0	1	0	1	0	0	0	0	8154	10000	4000~	10000	32154
10	Harpur	3	1	2	3	0	0	0	3	0	3	0	0	0	0	7248	10000	12000	30000	59248
11	Distoliya	5	0	5	5	0	0	0	5	0	5	0	0	0	0	64898	0	4000/	50000	118898
12	Thikahan Kothi	1	1	0	1	0	0	0	0.	1	1	0	0	0	0	6523 -	/10000/	4000	10000	30523
13	Thikahan Bazar	1	1	0	0	1	0	0	0	1	0	1	0	0	0	19464	10000	4000	0	45629
14	Jahangirpur	3	3	0	3	0	1	0	2	0	3	0	0	0	0	17123	30000	12000	30000,	89123
15	Banjaria	1	0	1	1	0	0	0	1	0	1	0	0	0	0	4077	0	4000	10000	18077
16	Sidhaila	5	3	2	5	0	1	0	4	0	5	0	0	0	0	19479/	30000	20000	50000	119479
17	Mishrolia	4	0	4	4	0	4	0	0	0	4	0	0	0	0	21744	0	0	40000	61744
		166	116	50	107	59	23	0	126	17	104	59	1	1	1	1392553	1160000	516000	1070000	4138553

Anuradha Chandra
Manager (Fech.)

33459011

5.0 Assistance as per Micro plan

Table No. 8. Assistance as per Micro Plan

		Total No. of		Entit	lement		Total	
Category	Total No. of AFs	Commercial AFs	Assistance for structure	Shifting Assistance	Special Assistance to Vulnerable	Training		
Squatter Vulnerable	110	40	8,74,074	11,00,000	11,00,000	160000	32,34,074	
Squatter Non Vulnerable	22	15	1,51,748	2,20,000	NE	60000	4,31,748	
Encroacher Vulnerable	187	31	21,74,481	NE	18,70,000	124000	41,68,481	
Encroacher Non Vulnerable	5	3	NE	NE	NE	NE	0	
Tenant Vulnerable	0	0	NE	0	0	NE	0	
Tenant Non Vulnerable	0	0 .	NE	0	NE	NE	0	
Total	324	89	32,00,303	13,20,000	29,70,000	3,44,000	78,34,303	
G	Frand Total	1	32,00,303	13,20,000	29,70,000	3,44,000	78,34,303	

Total Value of Micro Plan= 78,34,303 (Rs. Seventy Eight Lakh Thirty four Thousand Three Hundred and Three

only)/

Manager Tech) Protest symmetation Unit,

DGM (Tech.) BSRDCL, PIU, Muzaffarpur

Consultants for Rural Area Development Linked Economy (CRAPLE and Land)

Manager (Tech.)

Page 7



ABSTRACT OF MICROPLAN FOR NTH-- SH-87

									Socia	l Cateo	ry		Туре	of Vul.		e	, e	, a	to les	9
SI. NO.	Village Name	Total AFs	Sq	Enc	Tenant	V	NV	sc	ST	ОВС	Gen	BPL	APL	WHH	РНС	Compensatio n for structure	Shifting Assistance	Training Assistance	Special Assistance to Vuinerables	Total Assisstance
1	Katra More	2	2	0	0	2	0	0	0	2	0	2	0	0	0	16200	20000	8000	20000	64200
2	Mananpur	7	-6	1	0	6	1	1	0	6	0	6	1	0	0	29430	60000	8000	60000	157430
3	Baligarh	17	0	17	0	17	0	10	0	7	0	17	0	0	0	97088	0	16000	170000	283088
4	Gangwara	3	2	1	0	1	2	0	0	3	0	1	1	1	0.	35910	20000	12000	10000	77910
5	Tarma Tola	3	0	3	0	3	0	0	0	2	1	3	0	0	0	20520	0	4000	30000	54520
6	Mehsaul	7	2	5	0	5	2	0	0	7	0	3	2	2	0	116664	20000	16000	50000	202664
7	Nawadih	3	0	3	0	3	0	0	0	3	0	3	0	0	0	46998	0	0	30000	76998
8	Morahpul Batra	3	3	0	0	2	1	0	0	3	0	2	1	0	0	131652	30000	12000	20000	193652
9	Islampur chowk	5	4	1	0	4	1	0	0	4	1	5	0	0	0	15120	40000	20000	40000	115120
10	Mohni Sakrauli	- 1	0	1	0	1	0	0	0	1	0	1	0	0	0	9720	0	4000	10000	23720
11	Gauri	3	1	2	0	1	2	0	0	3	0	1	2	0	0	7128	10000	8000	10000	35128
12	Ganguli	6	3	3	0	6	0	0	0	6	0	5	0	1	0	26784	30000	4000	60000	120784
13	Sharif Pur	21	2	19	0	21	0	4	0	16	1	19	0	1	1	524033	20000	4000	210000	758033
14	Rasulgani	5	1	4	0	4	1	0	0	5	0	3	1	1	0	75828	10000	0	40000	125828
15	Nanpur	17	17	0	0	16	1	9	0	5	3	15	1	1,	0	58320	170000	0	160000	388320

CRADLE OLD Ren Nu 2011/95 New Rig New Strate Charles C

Confeation 3

Anuradha Chandra

257912013 Dy. G.H. (Tech)

	TOTAL	324	132	192	0	297	27	76	0	237	11	261	24	36	3	3200303	1320000	344000	2970000	7834303	
33	Koria Pipra	23	4	19	0	20	3	4	0	9	0	17	3	3	0	150768	40000	4000	200000	394768	
32	Sisotia	10	0	10	0	10	0	1	0	9	0	10	0	0	0	72900	0	4000	100000	176900	
31	Barahi	9	5	4	0	8	1	0	0	9	0.	8	1	0	0	94037	50000	16000	80000	240037	
30	Sursand	1	0	1	0	1	0	1	0	0	0	1	0	0	0	7290	0	0	10000	17290	
29	Virrakh	1	0	1	0	1	0	0	0	1	0	1	0	0	0	10800	0	4000	10000	24800	
28	Kwari	30	9	21	0	28	2	2	0	28	0	26	2	2	0	102060	90000	4000	270000	466060-	476060
27	Rasalpur	13	4	9	0	12	1	0	0	13	0	10	0	2	1	82890	40000	24000	120000	266890	Shak
26	Basudevpur	2	2	0	0	2	0	2	0	0	0	2	0	0	0	30240	20000	4000	20000	74240	
25	Balha Madhusuda n	42	9	33	0	37	5	4	0	35	3	33	5	4	0	583119	90000	24000	380800 370000	1 077119 106711	9 Dubot
24	Narayanpur	26	22	4	0	26	0	1 7	0	8	1	21	0	5	0	165240	220000	12000	260000	657240	
23	Hariharpur	17	15	2	0	17	0	9	0	8	0	14	0	3	0	132363	150000	32000	170000	484363	
22	Chainpura	4	0	4	0	4	0	0	0	4	0	3	0	1	0	27432	0	0	40000	67432	
21	Bedaul	7	1	6	0	6	1	0	0	7	0	5	1	1	0	116496	10000	24000	60000	210496	
20	Budhnad Chowk	3	2	1	0	3	0	1	0	2	0	3	0	0	O.	17280	20000	12000	30000	79280	
19	R.C.Pupri	8	8	0	0	7	1	0	0	8	0	6	1	0	1	59400	80000	28000	70000	237400	
18	Pupri block	3	3	0	0	2	1	0	0	2	1	1	1	1	0	12960	30000	12000	20000	74960	
17	Yadupatti	13	2	11	0	13	0	0	0	13	0	6	0	7	0	146021	20000	12000	130000	299614 308021	
16	Bahera	9	3	6	0	8	1	1	0	8	0	8	1	0	0	177614	30000	12000	80000	200044	i .

CRADLE OLD Reg. No. 201-06 New Reg. No. - 5107 Nagar.

Anuradha Chandra
Anuradha Chandra



ANNEXURE-4



BIHAR STATE ROAD DEVELOPMENT CORPORATION LIMITED BIHAR STATE HIGHWAYS PROJECT- II Implementation of Resettlement Rehabilitation Plan – BSHP-II - AF SARAIYA – MOTIPUR ROAD (SH-86)

ENTITLEMENT OF NON TITLE HOLDER - IDENTITY CARD

VILLAGE - Jaitpur		BLOCK- Sariaya	DISTRIC	T - Muzaffarpur
Name -	Raj Kishore Sh	aah	No. of Persons in Family-	7
Father's/Husband's Name-	Sri Doman shal	n III	Type of Loss-	Com
PAFs Identity No -	8.500/L/sq/com/T	7/NV/84	Type of	Т
Occupation -	Bike repairing		Structure	
Caste -	OBC		Vulnerable-	NV
A: ENTITLEMENT				
1	Compensation/	Replacement Cost for Str	ucture	9966
2	Shifting Assista	ance Rs.10,000/-		10000
3	Training Assist Payable)	ance for Vulnerable HH R	s.4,000/- (Not	4000
4	Special Assista	.10,000/-	NA	
*	Total Amount o		23966	
	In words: Rs. To and sixty six or	wenty three thousand nine	e hundred	
3: Payment				
Installments	Date	Cheque/Draft No.	Amount (in Rs.)
İst				
2nd				
SIGNATURE		215142 8. Rd. No		-
SIGNATURE	ITATIVE	Di Reg No. 201/96	SIGNATURE OF R.O.	Tech I
Encl :- 1.		liments of Assistance amount	Pole: 'गया ily signed by EP ^{nuaif fo}	CONTINUE PRINCIPLE CONTENTS.

I cord on P5 x h x xx 10 / 6211 - 21 1 (an 2112 2-18

Difference

परियाजना प्रभावत पारवाव

पुनवांक चोजना क्रियान्वयन, एकोज 2, इस 85 (सर्था-मोतीपुर) बिहार स्टेट रोड डेवलपनन्ट कॉरफोरेशन लिभिटेड परियोजना क्रियान्वयन इकाई, हाजीपुर 3, बिहार

4.	परियोजना प्रभावित परिवार की पहचानः (Identification of PAF) A. नामः B. पिता/पति का नामः C. पताः परिवार की पहचानः संरचना विवरणीः सङ्क के मध्य से चूरी कुल क्षेत्रफल प्रभावित क्षेत्रफल प्रभावित क्षेत्रफल
2.	परिवार प्रश्नावली : 3% ल. 2 चौ. 5.5 कुल
	परिवार का प्रकार 1. संयुक्त [🗸 2. एकल [🔀] 3. विस्तृत [🛁 धार्मिक समूह
	 1. हिन्दू [
3.	प्रभाव का प्रकारः (a) अतिकमणकारी (Encroacher) \(\sumseteq \) (b) उपवेशी (Squatter) (c) किराएदार (Tenant) \(\sumseteq \) (d) वेजलेकर (Wage Labor) (e) भूरवामी (Title Holders) \(\sumseteq \) (f) अन्य (Other)
4.	नुकसान का प्रकारः (i) आवासीय (ii) व्यवसायिक
5.	(iii) आवासीय और व्यवसायिक (iv) भूमि (v) भूमि (v) भूमि (v) परका (v) अन्य कि (v) अन्य कि
6.	सामान्य पहचान (General Identification): A: चेनेज / पहचान न0 = 500 59 COUNTY
	B- (i) ग्रामः
	C- स्थिति (i) ग्रामीण 💢 (ii) अर्ध शहरी 🕡 (iii) शहरी
13	Consultants For Rural Area Development Washard Tech

7	यदि विपन्त है तो दमः आमार है -	
	 बीपीएल कार्ड विकटांन लधु/सीनांत दृष्य प्रमान एक अन्य (लिखिए) 	
8.	प्रमाण-पत्री का सत्यापन -	
	1. खसरा / खतौनी	[] 6. राशन कार्ड (लाल, पीला, सफेट)
	2. किसान बही	7. बिजली का बिल
	 रजिस्ट्री / वैनामा प्रपत्र 	[火] 8. पगड़ी / अग्रिम धनराशि देने के प्रमाण
	4. इकरारनामा / नोटरी	ি 9. चुनाव पहचान पत्र
	5. पंचायत	[🛪] 10. अन्य
(L.	परिवार का विवरण (Household Par	ticulars)
	परिवार के कुल सदस्य : महिला	अपुरुष
	परिवार में शिक्षित संदस्यः महिला	ि पश्च - प्रि
		मिडिल 🖳 मैट्रिक 📗
10.	रनातक केवल भूरवामियों के लिएः (Only f	तकनीकी or Title Holdres)
	(i) खसरा नं	Ť
44.	कि राएतार :	त्य सम्पत्ति
	रहने की अवधि	लम्बाई चौड़ाई कुल
	किराया प्रतिभाह रू०	प्रमावित क्षेत्रफल (sq.)
	प्रतिमाह आय रू०	आश्रित परिवार की संख्या
12.	यदि आप विस्थापित होते हैं तो आप कहां	बसना चाहेंगे? (स्थल का विवरण दे)
	उत्तरदाता का नाम : ४७५ डिडोर्	७/६ दिनांक: 29/2/2C/2
	पर्यवेक्षक का नाम :	Amadha Chand Examer:
	BSRCD के प्रतिनिधि का नाम :	Example:
30	Ciones !	Manage

EMPT IN CHES. MISSEN

Consultants For Rural Area Development Linked Economy



KBW1171842





Sex / लिंग

: Male / पुरुष Age 35 Years as on 1.1.2002 आयु : ३५ वर्ष १.१.२००२ को



Address : 38, Village-Purakhauli, Thana No,

Nachhari, Town/Vill - Purakhauli, Anchal - Lalaganj, Distt - Valshali

पता

: ३८,गांव-पुरखीली,याना नं, डछन्र, शहर/गाँव - पुरखोली, अंचल - लालगंज, जिला - वैशाली

Facsimile Signature of Electoral Registration Officer 51, LALGANJ Constituency ५१, लालगंज निर्वाचन क्षेत्र के निर्वाचक रजिस्हीकरण अधिकारी

कं हस्ताक्षर की अनुकृति Place : Hajipur

Date : 05/03/2003

विमान :04/03/२००३

स्थान : हाजीपुर This Card may be used as an Identity Card under different Government Schemes. इस पत्र का विभिन्न सरकारी योजनाओं के अन्तर्गत पहचान पन्न के रूप में प्रयोग किया जा सकता है।

शामिशार खाइ

KBW1171842



केन्या बेंक

Bangalore - 560 002

शाखा का नाम और पता Name and Address of the Branch

: PAT1252@OARBAHBOTQ3IN

FURKHAULI

LALGANT, VAISHALI 844121

देतीफोन सं. / Telephone N**प्**3227 Jel No.

)06224-237231

फैक्स/ ई-मेल/ Fax/ E-mail:

23/08/2006il-Id : PAT1252@CANBANK.CO.IN

RAJ KISHORE SAH SANGITA DEVI

खाता सं / Account No. 106042 1253121 4121 4121

नाम / Name/s

Agriculturist S/O DOMAN SAH

PURKHAULI

व्यवसाय / Occupation

LALGANJ, VAISHALI-844121 23227

पता / Address

23/08/2006

गांहक आई डी / Customer ID.:

खाता खोलने की तिथी/ A/c Opened on

नामांकिती का नाम/

Name of Nominee

नामांकन की पंजीकरण संख्या/

Nomination Reg. No.

जन्म तिथि Date of Birth

अधिकारी/प्रबंधक/OFFICER /MANAGER

210192112 2718

BIHAR STATE ROAD DEVELOPMENT CORPORATION LIMITED BIHAR STATE HIGHWAYS PROJECT- II- AF Implementation of Resettlement Rehabilitation Plan Runnisaidpur to Bhiswa Road (SH-87)

ENTITLEMENT OF NON TITLE HOLDER, IDENTITY CARD

VILLAGE -Sharif Pu	f'	BLOCK- Nanpur DISTRICT - Si		RICT - Sitamarh	
Name -	Israt Parveer		No. of Persor	15	
ather's/Husband's Jame-	Md Camina Angeri		Type of Loss	6 Res	
AFs Identity No -	15.450/L/EN/RES	6/T/V/63			
Occupation -	Agri Labour		Type of Stru	1 T	
Category -	OBC	N) Marine C	Vulnerable-	V	
: ENTITLEMENT		N I I I I I I I I I I I I I I I I I I I		V	
1 Compensation		n/Replacement Cost for Structure		8640	
2	Shifting Assistance Rs.10,000/-			0	
		sistance for Vulnerable HH Rs.4,000/- (Not		0	
4	Special Assistance for Vulnerable HH Rs.10,000/-			10000	
	Total Amount of Allowance (in Rs.)			18640	
	In words: Rupe	n words: Rupees Eighteen Thousand Six Hundred Forty Only			
Payment				··· ,	
Installments	Date	Cheque/Draft No.	Amount (in Rs.)		
lst		1,000,000,000	Amount	in Rs.)	
2nd			100		
SIGNATURE	OF PAP	R.T. I of Israf parveen			
SIGNATURE OF NGO REPRESENTATIVE		RADLE OLO Resi No. 2016/16	SIGNATURE OF R.O.	Con/150/10/13	
CI :- 1. R	Receipts of all instal	Iments of Assistance amount	Peginia was	engentation Unit.	
4. 1	notocopy of Chequ	Ilments of Assistance amount res/Drafts of all installments dul	y signed by EP	7	

पहचान प्रपन्न

परियोजना प्रभावित परिवार

पुनर्वास योजना क्रियान्वयन SH -87 (रुनीसायदपुर—भिसवा) बिहार स्टेट रोड डेवलपमेन्ट कॉरपोरेशन लिमिटेड, परियोजना क्रियान्वयन इकाई, हाजीपुर 3, बिहार

1.	परियोजना प्रभावित परिवार की पहचानः र	संरचना विवरणीः
		सड़क के मध्य से दूरी
	A. नामः	कुल क्षेत्रफल :
		ल॰ चौ॰ कुल
	C. पताः	प्रभावित क्षेत्रफल
	3	ल. चौ. कुल
2.	परिवार प्रश्नावली :	
	परिवार का प्रकार	३. विस्तृत []
	1. संयुक्त [] 2. एकल [] धा र्मिक समूह	३. विस्तृत ।
	1. हिन्दू [] 2. मुस्लिम []	3. ईसाई [] 4. अन्य
	सामाजिक स्तर	
	3 6	ाति [] 3. पिछड़ी जाति []
	4. सामान्य जाति [] प्रेवार की आयः प्रतिमाह	पेशा : अन्तर्वरी
3.	प्रभाव का प्रकारः	
J.	(a) अतिकमणकारी (Encroacher)	(b) उपवेशी (Squatter)
	(c) किराएदार (Tenant)	(d) वेजलेवर (Wage Labor) (f) अन्य (Other)
191	(e) भूस्वामी (Title Holders)	(i) Gra (other)
4.	नुकसान का प्रकारः	
	(i) आवासीय (ii) व्यवसानि	यक
	(iii) आवासीय और व्यवसायिक (iv) भूमि	
5.	संरचना के प्रकारः (i) पक्का (ii) अर्धपक्का (iii) कच्चा	(iv) अन्य
	(i) पक्का (ii) अर्धपक्का (iii) कच्चा	(IV) s. samman
6.	सामान्य पहचान (General Identification):	
	A. चेनेज/पहचान न0 —	
	B- (i) ग्रामः (ii) डाकखाना	(iii)अंचल
	(iv) ब्लाकः(v) जिलाः	
25	C- स्थिति (i) ग्रामीण (ii) अर्ध शहरी	(iii) शहरी
		1 me
	CHARLE S	A That Charling
	Consultants For Rural Area Developmen	nt Linked Economy Manager (Tech.)
	15 Yes, water Contes	

ਰਿਧਾਰ (vorterable) ਕਰਿ ਰਿਧਾਰ है तो क्या आधार ह
1 बीपीएल कार्ड 3 विकलांग 5 तथु सामात कृषक प्रमाण पत्र । 6. किस्रयेदार प्रमाण पत्र 7 अन्य (लिखिए)
 प्रमाण-पत्रों का सत्यापन - खरारा / खतौनी किसान बही रिजिस्ट्री / बैनामा प्रपत्र इकरारनामा / नोटरी पंचायत परिवार का विकास (पान्य पर्यापन कार्ड (लाल, पीला, सफेद) [] राष्ट्री / बिजली का बिल [] श. पगड़ी / अग्रिम धनराशि देने के प्रमाण [] चुनाव पहचान पत्र [] अन्य
9. परिवार का विवरण (Household Particulars) परिवार के कुल सदस्य : महिला पुरुष बच्चे परिवार में शिक्षित सदस्य: महिला पुरुष बच्चे शिक्षा का स्तर : प्राइमरी मिडिल मैट्रिक स्नातक तकनीकी 10. केवल भूस्वामियों के लिए: (Only for Title Holdres)
(i) खसरा नं. (ii) खाता नं. (iii) खाता नं. (iii) कृषक की भूमि का कुल क्षेत्रफल (iv) मुआवजा प्राप्त हुआ हाँ / नहीं (v) कुल मुआवजे की राशि : भूमि मकान
रहने की अवधि प्रभावित क्षेत्रफल (sq.) प्रभावित क्षेत्रफल (sq.) आश्रित परिवार की संख्या प्रतिमाह आय रूठ आश्रित परिवार की संख्या प्रतिमाह आय रूठ यदि आप विस्थापित होते हैं तो आप कहां बसना चाहेंगे? (स्थल का विवरण दें)
उत्तरदाता का नाम : पर्यवेक्षक का नाम : BSRCD के प्रतिनिधि का नाम : Eस्ताक्षर : Eस्ताक्षर : Consultants For Rural Area Development Linked Economy Manager (Tech.)



BR/11/064/465097



Elector's Name : Ishrat Parbin निर्वाचक का नाम : इशरत परबीन Husband's Name: Mo. Samim Ansari

पति का नाम Sex / लिंग

:मो. समीम अंसारी :Female / महिला

Age

: 32 Years as on 1.1.2003

आयु

वर्ष १.१.२००३ को

Address : 36,,

Town/Vill - Sharifpur, Anchal - Runnnisaidapur,

Distt - Sitamarhi

पता

: ३६,, शहर/गाँव - शरीफपुर, अंचल - रुन्त्रीसैदपुर,

जिला = सातामही

Facsimile Standard of **Electoral Registration Officer**

for 64-RUNI SAIADPUR Constituency

६४-रुनी सैदपुर निर्वाचन क्षेत्र के निर्वाचक राजस्थीकरण अधिकारी के हस्ताक्षर की अनुकृति

Place : Sitamarhi

स्थान : सीतामढी

Late: 18.03.2004

BR/11/064/465097

नाक : १८.०३.२००४ This Card may be used as an Identity Card under different Government Schemes

इस पत्र का विभिन्न सरकारी गोजनाओं के अन्तर्गत वह चान पत्र के हप में प्रयोग किया।





बी. पी एल. याजना

कुपन क्रं 0032002 जिला की नाम सीतामढी जिला काड - 33 पाइका राज् - मई 13

खाद्यान्य की मात्रा - 15 कि. ग्रा. चावल

जन वितरण प्रणाली विक्रेता का नाम एवं अनुज्ञप्ति संख्या सहित मुहर

हस्ताक्षर/अंगूठां निशान


हस्तान्तर ज.वि.प्र.विकेत

विक्रय पूल्य रु. 6-78 ! तिकिला

Photograph wellow of the Depositor(s) i ame (viandatory For SCSS 2004Cheque A/c (Y/N)(for SCSS - 2004 only) रजिस्ट्री की तारीख नामांद्र न के हस्ताक्षर की सन्या Signature of Date of Nomination Postmuster. Number Registration : लेनदेन का विवरण तारीख Date Particulars of Transaction विकासी बकाया **ਬ.**ह. जमा Irritial Balance Withdrawal Deposit-100 Anuradha Chandra Manager (Tech.) (2)



Bank or India बक आफ डाड्या MAGRICULTURE AND ALLIED AO Occupation : S/O DEO HARAYAN SAMANI VILL BIPARA Br. | Name : SAHASRAM Address II PIPARA ANCHAL PARIMAR DIST SITAMER ATERO BARAHL DT STAMARHI. Br. Address : BIHAR. SITA MAU (MJP). (84333) 8(333) STIAKARHI IBIHAR) INDIA R9208 BIHAR Br. Tel. :: Sahsaram Muzaffarour@bankofindia.co.lin Quarational Inst: SEUF Br. | Email :: BX100004435 RECD. Nomination : IFSC Code : 26-07-2013 1843013504 A/C Open Dt.: MICR Code : 134306399 Customer 1d : W43510110010285 Account No. : D. JAGDESH SAHANEY NAME !! CHief Grievance Redress Officer:022-66684464 Total free number of our call center: 1800220229 This pass hook is system denurated and does not require any imitials.



BSRDCL, PIU, MUZAFFARPUR

CRADLE

NTH ASSISTANCE DISBURSEMENT LEDGER

				R	UNNISAL	DPUR-	BISHWA R	OAD, PACKA	GE-II, SH-87			
34 1/4 1/10 2	- Mayor	stentitracios vo	Name of PAP	эшех вивимину запіса	Forgi Compensation & Assistance Excluding Commes	Installment	असत	sorphiss, orchard i	Упронас	AP Signane	MGGSignature	VRO Signature
53	Gauri	14.550/R/EN/ COM/K/V/53	Md. Sattar Kuraisi	Lt. Indal Kureshi	14,698	1st	25.2.14	492346	7349:		Delbus 1	1131
						2nd	6214	1533 LY	13 (3)		Riley	12
54	Gauri	14.550/L/SQ/C OM/T/NV/54	Motiour Rahman		12,430	151		492347	6215.00		Plabout 3:11	117
					1	2n	d Esch	2, 2, 2, 2, 2, 2, 2, 2, 2, 2, 2, 2, 2, 2	25		July 1	B

26

1+IIIIexure-b

NTH ASSISTANCE DISBURSEMENT LEDGER SARAIYA - MOTIPUR ROAD, PÁCKAGE-II, SH- 86

Village.	Неприсанов №а	Varie of PAD	English and the Sunnit	Total Compensation excluding Training	installment	Pare	ારલામાં જ સામેડા) manny		lineka, i	
Mohamm adpur	0.050/L/Sq/ Com/V/9	Bhola Paswan	Lt.Munnilal Paswan	25436	1ST	18-2-2914	429969	12,718:20		Shipiy	
	-				2ND	22 ·12·1 Y	234333	12718:20		Therpier	G15
Mohamm adpur	0.050/L/Sq/ Com/V/10	Md.Тауа ў	Lt.Bulla Miyan	25662	1ST	18-2-2014	429970	12,831:00	FG JACY	Makey.	
	3				2ND	22.12.19 Anurad	234334 he Chandr	128312~	A. インベ U	LJ Chillery	Aland



Annexure-7

बिहार स्टेट रोड डेवलपमेन्ट कॉरपोरेशन लिए, जरेयोजना कार्यान्वयन इकाई, मुजफ्रसपुर SH-87 (कन्नीसैदपुर-भिसवा) पथ हेतु पुर्नवास एवं पुर्नस्थापना कार्य hladi salgay Eughan प्राप्ति रसीढ पिता/पति का नाम 🔑 ५५० में अंदे ए आई०डी० नं० १ क्या है कि संव क्या कि संव क्या कि संव क्या कि संव कि संव कि संव कि संव कि संव कि संव कि संव कि संव गवाह अरेट के लिए प्राप्तकर्ता का हस्ताक्षर बिहार स्टेट रोड डेवलपमेन्ट कॉरपोरेशन लि0, परियोजना कार्यान्वयन इकाई, मुजफ्फरपुर SH-87 (रून्नीसैदपुर-भिसवा) पथ हेतु पुर्नवास एवं पुर्नस्थापना कार्य प्राप्ति रसीद नाम हर्ग भेडल पिता / पित का नाम सोगार्थ मंडल आई०डी० नं० १००० | 159 | Сот Т/V/2 तारीख 10 4 14 चेक सं० 753502 के द्वारा 13240 - ०० एपये 1118 किस्त के रूप में प्राप्त किया। गवाह क्रा १३ के कि प्राप्तकर्ता का हस्ताक्षर बिहार स्टेट रोड डेवलपमेन्ट कॉरपोरेशन लि0, परियोजना कार्यान्वयन इकाई, मुजफ्फरपुर SH-87 (रून्नीसैदपुर-भिसवा) पथ हेतु पुर्नवास एवं पुर्नस्थापना कार्य शिवादिनी पिता/पित का नाम रेंभार्ज मिलिंड आई०डी० नं० ०.५०० ८ १९८ । १९८ । १४ विक सं० .. 7535०३

गवाह कि हिंद रिए


के द्वारा किस्त के रूप में प्राप्त किया। Manager (Tech.)

प्राप्तकर्त्ता का हस्ताक्षर

	se sign above
The state of the second seco	se sign abovs
()	se sign abova
(日本) 10: 1811/01年17月7年 238 202年19月8日 (日本) 1日 1日 1日 1日 1日 1日 1日 1日 1日 1日 1日 1日 1日	se sign abovs

पुष्तप्तरपुर, युज्जपत्तयुर जिला - 842 001 Muzzafarpur, Muzzafarpur Dist - 842 001 ;=8 CCD± : `	A IA Y Y Y Y
) 903	
) POLITICAL STATE OF THE STATE	0.2/-
) The Month of the	THE LOCAL COLUMN
HMDCU TRAY BUE TRAIN U. Our Bray Of ES いっぽ 原本さ CBS CODE: 00668 Plea	ase sign above
भू जाकरपुर, मुजाकरपुर जिला - 842 001	ORTHREE 40 0 % 3 0 ** O 1 2 O 1 5
	<u>। १९५५ को ८६ ८६ ५६ ५६ ५६ ५६ ५६ ५६ ५६ ५६ ५६ ५६ ५६ ५६ ५६</u>
) RUPEES THE SOLE ON 14	/718/=
) highten only	
) 15 1 1 7 7 9 3 7 1 G 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	LTO, MOZAFFASPUR
HAICGU HAICGU TO YN, DIN ARLY DUR BRAYC, EST, CLEAR YOU CAS CODE: 00668	LTO MUZAFFARRUR Den Mausger (1806.) Den skrigt abovo
HAICEU BY AND TO TO TO THE PURITY CONTROL OF	Gen Navager (1866.)

₹1.₹ _ --/c. i.'o. for his of the constant correction, which is the Dy. Gen. Manager (Tech) .. AY NELE AT PIRE WELL OUR DRUCK WELL THE WARRY OF SIGNORS. Please sign above #181901# 842019002# 25 मुजाफरपुर, मुजाफरपुर जिला - 842 001 VALID FOR THREE MONTHS ON Muzzafarpur, Muzzafarpur Dist. - 842 001 IFS CODE: IDIB000M056 re या वारक को OR BEARER खा. सं. For PI'J BILLE STATE BOAD DEVP. CORP. LTD., MUZAFFARPUK A/c No. Manager (Tech.) Dy. Gen. Manager (Tech.) HMCGU MABLE AT PAR AT ALL OUR BRANCHES IN CLEARING" CBS CODE: 00668 Please sign above #181405# 845014005# 29 मुज्जफरपुर, मुज्जफरपुर जिला – 842 001 Muzzafarpur, Muzzafarpur Dist. - 842 001 2 0 IFS CODE: IDIB000M056 या धारक को OR BEARER अला करें खा. सं. 9 3 For PI'U BIHAR STATE ROAD DEVP. CORP. LTD., MUZAFFARPUR Q A/c. No. Manager (Tech.) Dy. Gen. Manager (Tech.) HMCGU DE: 00668 Chandra
Chandra
Chandra
Tech.) BLE AT PAR AT ALL OUR BRANCHES IN CLEARING" CBS CODE: 00668 Please sign above 12 18 1903 11 50



#754332# 842035002G

Nine Thousand Three

#754313# 842015002#

मुजफरपुर - 842001 Muzaffarpu.: - 842001 2013 MCHAX

(85C : CMR&0000257	578-121 (0 D vs m
- 17 J	÷ = =	18035/-
ę (Ci)	March .	DOG CORE NO., Which I have been by Gen. Manager (Ex. Please sinn above
518	29	
Yalid Tc./	আ আ ∠েম [ally from the disteroil instrument. O S O S 2 O U
	ndred at	9320/
. Ca	elhar state road D garda Ar ger (Tech.)	CVP. CORP. LTD., MUZAFARRON Artirot Dy. Gen. Manager (18.4) Pleasa sign abovs
] 20%	2 - 9	
Valid for	चा खा CA [nly from the date of instruction O 8 O 8 2 O 1 4 D D M M Y Y Y
7200 Aums	ati ₹	या भारक को 0: 3 sursi
. 6	OU BIKAR STATE ROA Infrakcion . nager (Tech.)	D DEVP. CORP. LTD., MUZZETAE A. J. J. Dy. Gen. Manager (Tecn.) Plasse sign above

a) artis at par at all our Branchas in India"

"Pity : de stips: et all our Branches in India"

10751,331,110 BL, 201 Amerika Chandre (Tech.)


29

The The same

युजफ्फरपुर - 842 001 Muzaffarpur - 842 001 2012 MCRAQ IFSC CNRB0000258

The same	-		a = 1 2 1 1 7 7 1 1 = 57
1999年7年 375年2年19 . 27	Same Signal Holder Library	अदा करें।	16,404
Eight will		AND THE PARTY OF T	
画点 10256101056	5/55		/
		Confloration	
Valid for three months only from the date	of instrument	Co.	Please sign above
10 1 C 5 3	29# &4 20 1500 E:#	រ ំ	
n. acra		4	
le intrese any BEDE	मुजफ्फरपुर - 842 001 Muzaffarpur - 842 001 2012 MCRAQ IFSC CNRB0000258	चा खा СА	10012015 DDMMYYYY
10,444 co			या शारका को Or Bearer
ay Nagenara fas.	134 D	who at	
upess सबसे हुँ (६० ६८) य	Bossand SIX AUX	अहा क्षे	15,649
enty enty			
eft. 전 Ste. No.			1.
		Cont Sa	Marin Marine
Valid for three manths only from the date	of instrument		Please sign above
	28# 875072005#	1 1 13 (2)	
- John	मुजफ्फरपुर - 842 001 Muzaffarpur - 842 06 ी 2012 MCRAQ IFSC CNRB0000258	चा खा │ €A	1 0 0 1 2 0 1 5 D D M M Y Y Y Y
savel Mahin-			एक शास्त्रहरू क्यो ं 🗓 र 🗷 🛎 🖦
= 25/37 TT	Salsond Test Mi	uncersus	The second second second
		_ কেন্ত্ৰিক	6,5,46,7
	16.5	r	
	0	handis	
SP 20 P - + 4 P	Anu	radha Chandra anager (Tech.)	(Face to 177
. p. m. Ti	more at an anamara	allage	

- (B5329# 7620)5008%



Annexure-8

विहार स्टेट रोड डेक्लपबेन्ट कॉरपोरेशन लिए, परियोजना कार्यान्त्यन इकाई, एका हे पूर SH-87 (कन्नीसैदपुर मिसवा) पथ हेतु पुर्नवास एवं पुर्नस्थापना कार्य

V Detton	P.	प्राप्ति रसीद		
	भे भडल	पिता/पतिका न	[H 2044]	7214
		i de la companya de la companya de la companya de la companya de la companya de la companya de la companya de		
के द्वा	T 14860=	रूपये [[5].	/ किस्त कें	रूप में प्राप्त किया।
			1	7
गवाह	3103000			सतीव मेंड
1110			प्राप्तकर्त्ती का ह	हस्ताक्षर

बिहार स्टेट रोड डेवलपमेन्ट कॉरपोरेशन लि0, परियोजना कार्यान्वयन इकाई, मुजफ्फरपुर

SH-87 (रून्नीसैदपुर-भिसवा) पथ हेतु पुर्नवास एवं पुर्नस्थापना कार्य प्राप्ति रसीद

नाम हिता / पति का नाम स्रोग्नार्थ मंड ५ आई०डी० नं० १ २०० ८ ८०० ८०० ८०० ८०० तारीख 10 स्व 14 चेक सं० .. 753502 के द्वारा ... 13 2 40 - 🕫 🐪 ... रूपये .🏗 🕍 ... किस्त के रूप में प्राप्त किया।

गवाह अपेश किए दि

प्राप्तकर्ता का हस्ताक्षर

बिहार स्टेट रोड डेवलपमेन्ट कॉरपोरेशन लि0, परियोजना कार्यान्वयन इकाई, मुजफ्फरपुर


SH-87 (रून्नीसैदपुर-भिसवा) पथ हेतु पुर्नवास एवं पुर्नस्थापना कार्य

नाम सी वरित पिता / पिता / पिता नाम रें भाग भिरिपेक आई०डी० नं० ०.५०० ८ ५० | १९८ ७ / ४ | उतारीख 10 मु- १५ चेक सं० ... में इंड ५० ३ के द्वारा 12,430 = ल्वं रूपये [18] किस्त के रूप में प्राप्त किया।

गवाह की हिंद हिं।



प्राप्तकर्त्ता का हस्ताक्षर





Asian Development Bank

India Resident Mission

19 May 2014

Mr. Pratyaya Amrit, Managing Director, BSRDC/ Secretary, RCD Government of Bihar Patna

Dear Mr. Amrit,

Re: Loan 2663-IND: Bihar State Highway II Project Loan 2894-IND: Bihar State Highway II Project-Additional Financing TA 8170-IND: Road Master Plan for Bihar's State Highway Development -Special Project Administration Mission during 7-9 May 2014

We would like to thank BSRDC for the cooperation and assistance extended to the Mission. Attached is the Aide Memoire of the Mission for the captioned Projects. We would like to request BSRDC for the close monitoring and implementation of the action plan for the achievement of overall disbursement of \$100 million for CY2014.

Yours sincerely,

M. Teresa Kho

Country Director & MS

Attachment:

Mr. Nilaya Mitash, Joint Secretary (MI), DEA

ASIAN DEVELOPMENT BANK

(i) Loan 2663-IND: Bihar State Highway II Project (ii) Loan 2894-IND: Bihar State Highway II Project-Additional Financing; and (iii) TA 8170-IND: Road Master Plan for Bihar's State Highway Development

Special Project Administration Mission – 7-9 May 2014

AIDE MEMOIRE

A. Introduction

1. An Asian Development Bank (ADB) Special Project Administration Mission¹ (the Mission) was conducted for Loans 2663-IND and 2894-IND and Technical Assistance (TA) 8170-IND from 7-9 May 2014. The Mission focused on the achievement of the disbursement targets during CY2014 and reviewed the progress and status of each civil works contracts and the status of TA implementation with the officials of Bihar State Road Development Corporation Ltd. (BSRDC)—the executing agency (EA); supervision consultants, the contractors and the TA consultants. The Mission together with BSRDC officials made a field visit to an ongoing contract package (SH-83) under Loan 2894-IND. The Mission had a wrap-up meeting with the Managing Director, BSRDC/Secretary, Road Construction Department (RCD). The Aide-Memoire summarizes the findings, discussions, and understandings reached during the Mission. A list of persons met by the Mission is at Attachment 1. The findings and recommendations of the Mission are subject to confirmation by higher authorities of ADB, Government of India, Government of Bihar (GoB) and BSRDC.

B. Background

- 2. Loan 2663-IND in an amount of \$300 million was approved on 16 September 2010. The loan and project agreements were signed on 22 December 2010 and made effective on 2 March 2011. On Borrower's request, the original loan closing date of 30 June 2015 has been extended by one year to 30 June 2016 to accommodate the delay in the completion of works. An amount of \$25.36 million was assessed as loan surplus and cancelled effective 21 November 2013 and the net loan amount is \$274.64 million. The Project constitutes (i) construction and upgradation of about 389 km state highways identified under the Bihar State Highway Development Program; (ii) capacity enhancement in road asset management and road maintenance.
- 3. Loan 2894-IND in an amount of \$300 million was approved on 20 September 2012. The loan and project agreements were signed on 12 August 2013 and made effective on 8 November 2013. The loan closing date is 31 March 2018. The Project constitutes rehabilitation and upgradation of 254 km state highways identified under the Bihar State Highway Development Program. A piggyback TA (TA 8170) in an amount of \$1 million on a grant basis was also approved together with the loan. The TA will support the state government's initiatives, especially for preparing a 20-year strategic master plan for developing Bihar's state highways, including long term vision and goals, an action program, a financing plan, and a monitoring and evaluation system with performance indicators and target.

¹ The Mission comprised Anil Motwani, Team Leader, Transport, India Resident Mission (INRM) and Prabhasha Sahu, Associate Project Officer, INRM.

C. Project Status, Mission Findings and Action Plan

- 4. At the outset, the Mission informed BSRDC that the achievement of disbursement targets for 2014 is placed very high on the priorities for ADB as well as the Government of India and the progress on the disbursements is being monitored very closely. The 2 loans for Bihar State Highways with a cumulative loan amount of \$574.64 million (net amount after cancellation) is one of the largest portfolios for any executing agency for ADB-funded projects in India. It constitutes 5.3% of ADB's overall portfolio and 15.2% of ADB's transport sector portfolio in India. During the Inception Mission for Loan 2894 conducted during 26 February-3 March 2014, it was discussed that in view of the size of the portfolio, a combined disbursement of \$100 million for both loans should be achieved by BSRDC during CY2014. Although, a combined disbursement target of \$80 million for CY2014 has been agreed during the TPRM, a disbursement of \$100 million should still be targeted in view of the portfolio size.
- 5. The Mission was informed that contractor's poor performance on Loan 2663 continues to cripple the progress and a notice for termination has been issued for 2 out of 5 contracts. This would seriously affect the achievement of the targeted disbursement of \$50 million for the loan. Under these circumstances, the progress and disbursement performance on Loan 2894 will have to be scaled up to meet the overall target of \$100 million. The Mission held detailed discussions with BSRDC officials, supervision consultants and the contractors on the constraints and factors impeding the progress of works and agreed on measures to resolve these issues. In order to achieve a disbursement of \$100 million, a monthly target for each of the contract was agreed upon² (Attachment 2).
- 6. The status of project implementation and the mission findings are summarized as below.

a. Loan 2663-IND: Bihar State Highway II Project

7. **Civil works contracts:** The civil works for construction and upgradation of about 356 km state highways were awarded under 4 contract packages during 2010-11. During implementation, an additional subproject (Siwan-Siswan road on SH 89 of 33 km) was approved utilizing the loan savings and the civil works contract was awarded in July 2013. The works are being executed under 4 PIUs and supervised by 2 supervision consultants. The particulars and the current physical progress for 5 contracts are summarized below.

Contract Pkg (State Highway)	Length (km)	Contractor	Contract Amount (Rs. million)	Contract Award Date	Original Completion Date	Progress (April 14)
1 (SH 78)	100.40	Ramky Infrastructure	3,918	Apr-10	May-13	37.6%
2 (SH 81)	86.80	Patel Engineering	2,340	Aug-11	Oct-14	16.58%
3 (SH 90)	64.71	Sadbhav-GKC (JV)	2,018	Sep-11	Apr-14	27.67%
4 (SH 91)	101.70	Gammon India	3,289	Sep-11	Oct-14	29.76%
5 (SH 89)	33.07	BSC-C&C JV	1,499	Jul-13	Aug-15	7.41%

*As reported during the review mission

² It was clarified during the Mission that the agreed milestones for the completion of the activities and contract are not related to the extension of time under the contract, which are to be considered and granted by BSRDC in consultation with the supervision consultants on account of reasons not attributable to the contractor. The contractor would be liable for the contractual liquidated damages beyond the extended date of completion approved by BSRDC in consultation with the supervision consultants.

Absorbed to the same of the sa

d. Action Plan

24. The action plan finalized during the Mission is as below.

General

An engineering solution such as provision of RE wall/toe wall will be considered and adopted to minimize the land acquisition.

If land acquisition within a reasonable time is not considered feasible, works will be undertaken within the existing ROW.

The Project Director in the field PIUs will be delegated adequate authority to ensure smooth implementation of the project.

iv. A fortnightly review meeting Chaired by MD, BSRDC/Secretary, RCD will be held to monitor the progress of all the contracts

v. ADB will monitor the progress of works for all the contracts through the monthly progress reports and will undertake a review mission every two months

Loan 2663

i. BSRDC will consider splitting the remaining works under the terminated contracts for SH 78 and SH 90 in 2 packages each. BSRDC will also prepare a profile of contractors in Bihar to assess their capacity and formulate qualification criteria that would attract more number of capable contractors.

ii. BSRDC will send the bid documents for ADB clearance within 15 days.

BSRDC will consider undertaking the construction of 3 ROBs on SH 78 through IRCON and will seek prior approval from ADB, if the construction can be undertaken within the timeframe and mutually acceptable terms and conditions.

iv. BSRDC will expedite the completion of remaining land acquisition and resettlement activities for SH 78 and SH 81 by 31 October 2014 so that work for the completion of balance works can be undertaken expeditiously.

The financial progress by the contractors during the period May-November 2014 will be as under

a. Contract package SH 81:

Rs. 360 million

b. Contract package SH 89:

Rs. 617 million

c. Contract package SH 91:

Rs.600 million

The monthly breakup of the financial progress is at Attachment 2.

- vi. The contractors will submit a resource based work program for the completion of works and the same will be finalized upon review by supervision consultants and BSRDC.
- vii. The contractors will prepare interim milestones for physical progress for monitoring by BSRDC and the supervision consultants.

Loan 2894

i. BSRDC will expedite the completion of remaining land acquisition and resettlement activities for SH 88 by 31 October 2014 so that work for the completion of balance works can be undertaken expeditiously.



ii. The financial progress by the contractors during the period May-November 2014 will be as under

a.	Contract package SH 83:	Rs. 462 million
	Contract package SH 86:	Rs. 616 million
C.	Contract package SH 87:	Rs.1059 million
d.	Contract package SH 88:	Rs.1501 million

The monthly breakup of the financial progress is at Attachment 2.

- iii. The contractors will submit a resource based work program for the completion of works and the same will be finalized upon review by supervision consultants and BSRDC.
- The contractors will prepare interim milestones for physical progress for monitoring by BSRDC and the supervision consultants.

E. Acknowledgement

25. The Mission greatly acknowledges the cooperation and assistance provided by BSRDC.

Anil Motwani

Team Leader, Transport /Mission Leader India Resident Mission Asian Development Bank



समाहरणालय, सीतामढ़ी

(जिला भू-अर्जन प्रशाखा)

दिनांक-16.05.2013 की बैठक की कार्यवाही

अपर समाहर्त्ता, सीतामढ़ी–सह–अध्यक्ष, शिकायत समाधान सिमिति, SH-87 की अध्यक्षता में हुए बैठक में ग्राम–िपपरा कोईरिया, अंचल–परिहार, थाना नं0–126, जिला–सीतामढ़ी के परियोजना प्रभावित रैयत, BSRDCL के प्रतिनिधि तथा CRADLE के प्रतिनिधि सम्मलित हुए।

परियोजना प्रभावित रैयत श्री शशि भूषण कुमार, मकेश्वर पासवान इत्यादि द्वारा प्रतिनिधित्व करते हुए, यह शिकायत की गई की Proposed Alignment में काफी घर पड़ रहे हैं, जिसके कारण वे बेघर हो रहे हैं। उनके द्वारा Alignment में Change करने हेतु अनुरोध किया गया।

बैठक में यह निर्णय लिया गया कि स्थल का भौतिक निरीक्षण तथा प्रभावित मृगि को चिहिन्त कर सीमांकन किया जाए। इस कार्य में संबंधित रैयत, भू—अर्जन, सीतागढ़ी के अमीन, BSRDCL के अमीन तथा CRADLE के प्रतिनिधि भी उपस्थित रहेंगे। स्थल निरीक्षण तथा प्रभावित भूमि को चिन्हित करने हेतु दिनांक— 27.05.2013 को रैयतो की सहमति से तिथि निर्धारित की गई, तथा उन्हें उक्त तिथि पर उपस्थित रहने का निर्देश दिया गया। कार्यवाही की प्रति संबंधित रैयतों को भी अनिवार्य रूप से उपलब्ध कराने हेत् निर्णय लिया गया।

धन्यवाद ज्ञापन के साथ बैठक की कार्यवाही समाप्त की गई।

E01 —

अपर समाहर्त्ता, सीतामढ़ी-सह-अध्यक्ष,

शिकायत समाधान समिति, SH-87

ज्ञापांक- 363

31344cm 4V

दिनांक- 1610 S/15.

प्रतिलिपि := परियोजना प्रभावित रैयत, ग्राम-पिपरा कोईरिया / उप-महाप्रबंधक (तक0), BSRDCL/CRADLE, Ranchi को सूचनार्थ एवं आवश्यक कार्यवाही हेतु प्रेषित।

7 20 11 20 1160 B.S. A.C.D.

Awadha Chamatan समाधान समिति, SH-87

Recived Recived

Zugehriende Sheet

ace = 16.05-2013 Pace = अपर समाहभि कार कामिनाम काही, समाध्यामणम, सीनामही

Dibject: (ATAINET / LITHER TO (CAMPILES A INTAINE) 21021 3 EZ, TET 40 -87 de MERCHOT

VA 11 UNE ARRIVOT COM MINIS & 1212-1214 (121121) FIRME COM OF 6/605
SH COMMON COM MINIS - 336/100340, Projen - 26.4.13

SI.No. Designation Signature לנת נגרו לה בוחוץ יצוצר 29 2151 pour iArgi 212. north. Co. L.C. Contraccas 1, 13 Marry or (Tess) - Cum अमि प्रकाश Winder on son 7017 an 415 लंदना ग्रमार, सिंह, T. L. 95-507' aksmard Egl नेग कमार Proj Mag CRADINE 30 WT . D. S. A. D. C. -4329L 4/69 -10/ रव्र 4/दम अमी D.S.R.D.C 21/=1 20V137115 YMIAN MI Shershi 482013 HBZAK 410 11 -4-47 B411 21-37 3h1(-, , 122/4/41919 6.1.7. 24101124 4/3/1(n 4/60/0-L.T-9 (717 410 1923 41691n-17 NO1/10 18nd 416917 E) c/an 4/6/011 12/17/04/10 Anuradha Chandra
