



Social Monitoring Report

Project Number: 48023-003
December 2022

Period: October 2021 to December 2022

People's Republic of China: Ningxia Liupanshan Poverty Reduction Rural Road Development Project

No. 8

Prepared by Ningxia Project Management Office and Hangzhou Darren Engineer Project Management Co. Ltd. for the Asian Development Bank

This social monitoring report is a document of the borrower. The views expressed herein do not necessarily represent those of ADB's Board of Directors, Management, or staff, and may be preliminary in nature.

In preparing any country program or strategy, financing any project, or by making any designation of or reference to a particular territory or geographic area in this document, the Asian Development Bank does not intend to make any judgments as to the legal or other status of any territory or area.

Asian Development Bank

**Loan 3444-PRC: ADB Funded Ningxia Liupanshan
Poverty Reduction Rural Road Development Project**

**External Resettlement Monitoring and
Evaluation Report**

No.8

(As of December 2022)

Hangzhou Darren Engineer Project Management Co. Ltd.

Resettlement External M&E Specialist

January 2023

ABBREVIATIONS

AAOV	–	Average Annual Output Value
ADB	–	Asian Development Bank
AHs	–	Affected Households
APs	–	Affected Persons
AV	–	Administrative Village
CRO	–	County Resettlement Office
DI	–	Design Institute
DMS	–	Detailed Measurement Survey
CRO	–	County Resettlement Office
FS	–	Feasibility Study
HD	–	House Demolition
LA	–	Land Acquisition
LAB	–	Land and Resources Bureau
LAR	–	Land Acquisition and Resettlement
LEF	–	Land-Expropriated Farmer
L&RO	–	Land & Resources Office
M&E	–	Monitoring and Evaluation
MOU	–	Memorandum of Understanding
NDRC	–	National Development and Reform Commission
PADO	–	Poverty Alleviation and Development office
NDRC	–	Ningxia Development and Reform Commission
PPTA	–	Project Preparatory Technical Assistance
PRA	–	Participatory Rural Appraisal
PRO	–	Project Resettlement Office
RIB	–	Resettlement Information Booklet
RP	–	Resettlement Plan
SES	–	Socioeconomic Survey
SPS	–	Safeguard Policy Statement of ADB
NHAR TD	–	Ningxia Hui Autonomous Region Transport Department
TRO	–	Town/township Resettlement Office

WEIGHTS AND MEASURES

km	–	kilometer
m ²	–	square meter
mu	–	666.7 m ²

Table of Contents

1	<i>Brief Introduction of the Project and Resettlement External M&E</i>	1
1.1	Project background	1
1.2	Construction Contents and Scales	2
1.3	External Resettlement Monitoring and Evaluation	5
1.3.1	EMA	5
1.3.2	M&E Scope	5
1.3.3	M&E Contents	5
2	<i>Monitoring and Evaluation of Resettlement Implementation</i>	6
2.1	Summary of Resettlement Impacts and RPs Updating	6
2.2	Resettlement M&E of Subproject in Tongxin County, Wuzhong Municipality	6
2.2.1	Planned and Actual Resettlement Impacts	6
2.2.2	Compensation Rates and Resettlement Measures	7
2.2.3	Progress of Project and Resettlement Implementation	9
2.2.4	Main Findings during External M&E	9
2.3	Resettlement M&E of Subproject in Yuanzhou District, Guyuan Municipality	9
2.3.1	Planned and Actual Resettlement Impacts	9
2.3.2	Compensation Rates and Resettlement Measures	11
2.3.3	Progress of Project and Resettlement Implementation	12
2.3.4	Main Findings during External M&E	13
2.4	Resettlement M&E of Subproject in Xiji County, Guyuan Municipality	13
2.4.1	Planned and Actual Resettlement Impacts	13
2.4.2	Compensation Rates and Resettlement Measures	14
2.4.3	Progress of Project and Resettlement Implementation	15
2.4.4	Main Findings during External M&E	16
2.5	Resettlement M&E of Subproject in Pengyang County, Guyuan Municipality	16
2.5.1	Planned and Actual Resettlement Impacts	16
2.5.2	Compensation Rates and Resettlement Measures	17
2.5.3	Progress of Project and Resettlement Implementation	18
2.5.4	Main Findings during External M&E	19
2.6	Resettlement M&E of Subproject in Jingyuan County, Guyuan Municipality	19
2.6.1	Planned and Actual Resettlement Impacts	19

2.6.2	Compensation Rates and Resettlement Measures	20
2.6.3	Progress of Project and Resettlement Implementation	21
2.6.4	Main Findings during External M&E	22
3	<i>M&E of Resettlement Funds Disbursement</i>	23
3.1	Resettlement Budget and Resources.....	23
3.1.1	Tongxin County, Wuzhong Municipality (Updated RP).....	23
3.1.2	Yuanzhou District, Guyuan Municipality (Updated RP)	23
3.1.3	Xiji County, Guyuan Municipality (Updated RP)	23
3.1.4	Pengyang County, Guyuan Municipality (Updated RP)	23
3.1.5	Jingyuan County, Guyuan Municipality (Updated RP)	24
3.2	Disbursement Status of Resettlement Funds	24
4	<i>M&E of Capacity Building of Implementing Agencies and Staff</i>	26
4.1	Establishment of Implementing Agencies	26
4.2	Staffing.....	26
4.3	Evaluation of Implementing Agencies' Capacity	28
5	<i>Information Disclosure, Public Participation and GRM</i>	29
5.1	Information Disclosure, Public Consultation and Participation	29
5.2	Status of GRM	35
6	<i>Main Findings and Recommendations and Next Plan</i>	37
6.1	Main Findings	37
6.2	Main Recommendations	37
6.3	Next Steps.....	37
	<i>Appendix 1: New Land Compensation Policy document of Subprojects</i>	
	38
	<i>Appendix 2: LA and HD Agreements and Payment Records of</i>	
	<i>subprojects.....</i>	41
	<i>Appendix 3: Resettlement Status of AHs in Yuanzhou District.....</i>	51

1 Brief Introduction of the Project and Resettlement External M&E

1.1 Project background

1. The Ningxia Liupanshan Poverty Reduction Rural Road Development Project (hereafter refer as "the Project") focus on rural road development in the Liupanshan area of Ningxia Hui Autonomous Region (NHAR) under the nationwide initiative of Outline of Poverty Alleviation and Development Strategy in Rural Areas of China (2011–2020). The Project's impact will be increased rural incomes and reduction in the incidence of poverty in the Liupanshan area. The Project's outcome will be improved rural transport network in Liupanshan, particularly in poor areas.

2. The Project mainly aims at: 1) improving the technical grade for road network, increasing network capacity, and perfecting regional road network; 2) enhancing the connection between the project area and surrounding area, improving regional traffic condition, and promoting the economic development of the project area and region; 3) constructing 7 trunk roads and 21 feeder roads in Xiji County, Pengyang County, Jingyuan County, and Yuanzhou District in Guyuan City, Hai County in Zhongwei City, and Tongxin County in Wuzhong City. As required by ADB, resettlement plans (RPs) have been prepared for 7 trunk roads and 2 feeder roads.

Table 1-1: Basic Information of the Project

#	Item	Details
1	Country	People's Republic of China (PRC)
2	Loan No.	Loan 3444-PRC
3	Project	Ningxia Liupanshan Poverty Reduction Rural Road Development Project
4	Borrower	Ministry of Finance (MOF) of the PRC
5	Executing Agency	Ningxia Hui Autonomous Region Government (NHARG)
6	Implementing Agency	Transport bureaus of Yuanzhou, Xiji, Tongxin, Pengyang, Haiyuan, Jingyuan, and Longde counties
7	Total Estimated Cost	265.54 US\$ million
8	ADB Loan	100 US\$ million
9	IR category	B
10	IP category	B
11	Approval date	21 Oct 2016
12	Signing Date	10 Apr 2017
13	Effectivity Date	14 Jul 2017
14	Original closing date	30 Jun 2022
15	Extended closing date	30 June 2023

Source: ADB website.

3. See the Sketch Map of Project Distribution in Figure 1-1.

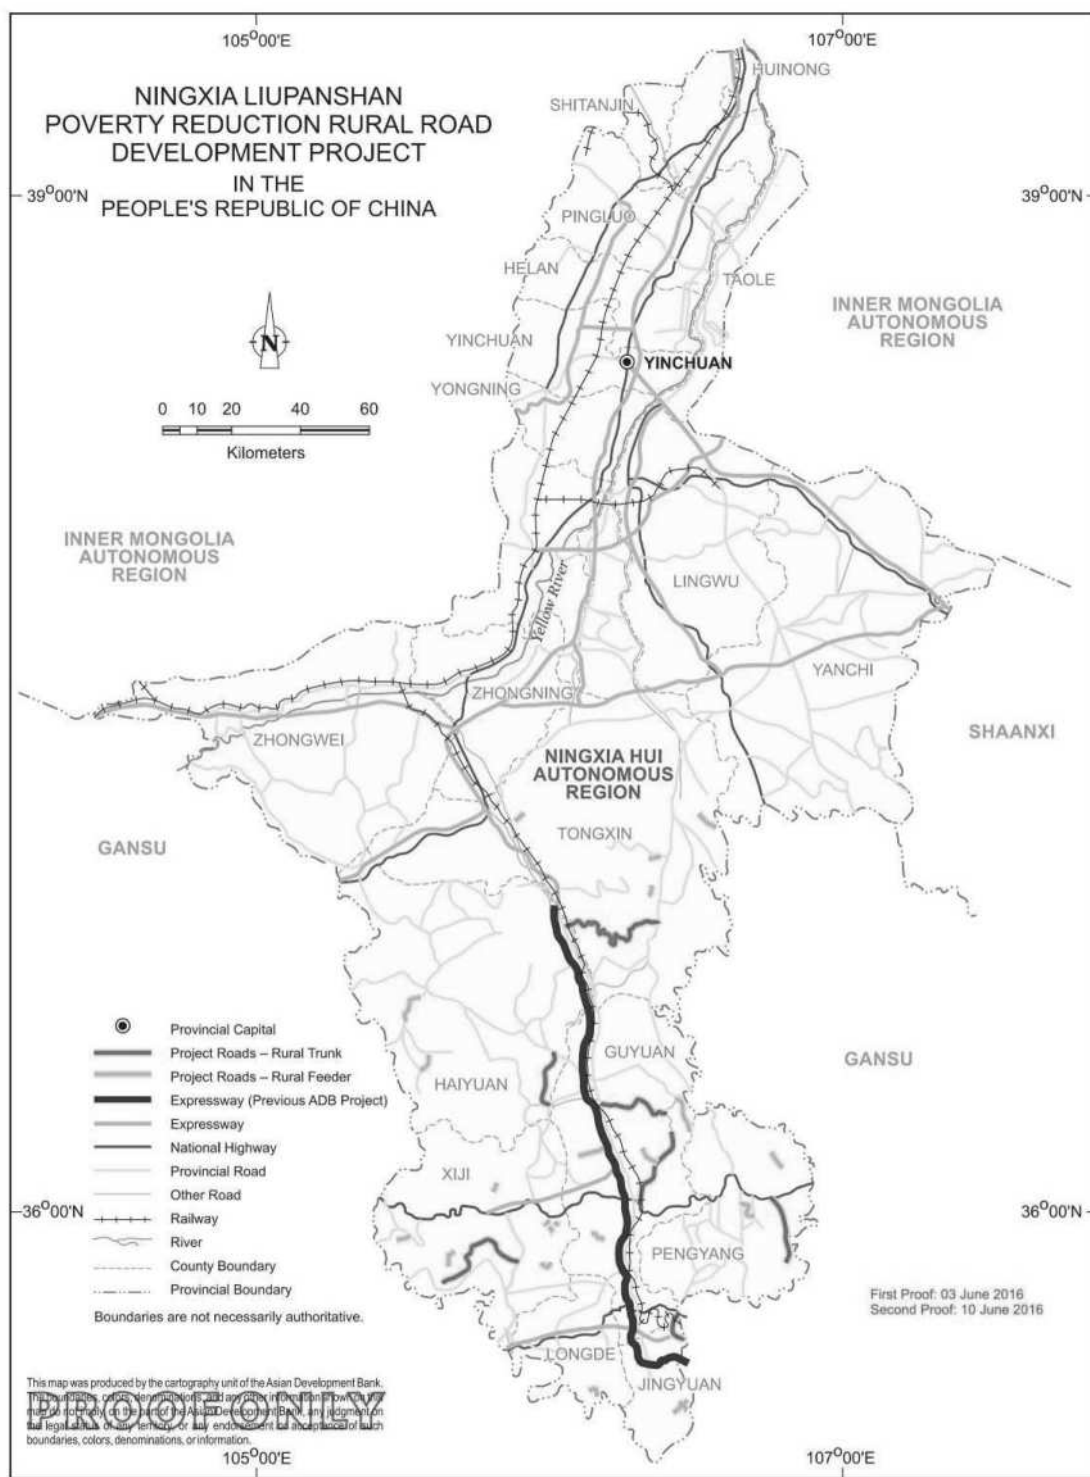


Figure 1-1: Sketch Map of Project Distribution

1.2 Construction Contents and Scales

- See the construction activities and scales in table 1-2 below.

Table 1-2: Summary of Construction Contents in Project Counties

No.	Project County/District	Construction activities and scales
1	Tongxin County, Wuzhong Municipality	<p>①Road Construction: The subproject starts from K236+199 (Xiangshui Bridge) of Line G344 (the former Line S101) at Wangtuan Town which is in the north of Tongxin County and 15km away from the county and ends at K61+510 which joins Line S202 (the former K337+800 of Line S203). The total length is 61.51 km and estimated total money is CNY 387,521,607.</p> <p>②LA impacts: A total of 1,942.77 mu of land will be acquired, including 403.3 mu of farmland (20.76%), 14.11 mu of residential land (0.73%), 11.35 mu of forest land (0.58%) , and 1514.01 mu of unused land (77.93%).</p> <p>③HD impacts: The subproject will involve 3,888 m2 of house demolition, among which, rural residents' houses in brick-timber structure (3,685 m2, accounting for 94.78% of the total area of demolition) and earth-wood structure (203 m2, accounting for 5.22% of the total area of demolition), and involves 25 households with 108 persons.</p> <p>④Affected Persons: The subproject will affect 149 households with 616 persons, all of which will be affected by LA, and only 25 households with 108 persons will be affected by HD. No enterprises or shops are involved in the acquisition and demolition. In addition, scattered trees, poles, wires, tombs, enclosures, water wells and other ground ancillary facilities will be affected.</p>
2	Haiyuan County, Zhongwei Municipality	<p>①Road Construction: The subproject starts from K0+000 of Line G341 being designed at the north of Zhaike Town, passes through Zhengqi village, Satai village, Sabu village, Zhongping village, Matao village, and Yuantao village, and ends at Line S311, with subgrade/pavement width of 7.5m/ 6.5m. It is constructed based on the standard of tertiary road, with total length of 28.4km and estimated total money of CNY 115.3063 million. The total construction period is 24 months.</p> <p>②LA impacts: A total of 485mu of land will be acquired, including 209.24mu of farmland (43.17%), 1.6mu of residential land (0.33%), 18.45mu of forest land (3.81%), and 255.74mu of unused land (52.7%), which will affect 108 households with 507 persons.</p> <p>③HD impacts: The project will involve 240 m² of house demolition. The houses by demolition are all earth-wood structure, which involves 2 households with 12 persons.</p> <p>④Affected Persons: The subproject will affect 108 households with 507 persons. At this stage, no temporary land occupation is planned. No enterprises or shops are involved in the acquisition and demolition. In addition, scattered trees, poles, wires, tombs, enclosures, water wells and other ground ancillary facilities will be affected.</p>
3	Yuanzhou District, Guyuan Municipality	<p>①Road Construction (A): Guanting-Guyuan Section of Guyuan-Xiji Road. The road starting point (K0+000) is at the boundary of Yunwu Mountain Nature Reserve on the north of Guanting Village, and the ending point (K26+330) connects with the Eastern Ring Road in Guyuan City, with the total length of 26.33km. The total investment is estimated to be CNY 229,310,500.</p> <p>②Road Construction (B): Wanzhang-Sanying Road. The road starts from the intersection of Wanzhang Village in Zhaike Town at the western foot of Yunwu Mountain and Pingle Village of Touying Town in Guyuan City, and ends at K31+700 of Road G344 (K301+900 of former Road S101), with the total length of about 31.7km. (The total amount is estimated to be CNY 168,420,200).</p> <p>③LA impacts: A total of 1,218.2mu of land will be acquired, including 453mu of dry farmland, 2.5mu of residential land, 738.9mu of unused land, and 23.8mu of forest land.</p> <p>④HD impacts: The 650m2 of brick-wood residential houses are involved in the house demolition (HD).</p> <p>⑤Affected Persons: The total number of affected residents is 1,130 of 269 households.</p> <p>⑥No enterprises, shops, mosques, schools, hospitals, or other sensitive facilities are involved in the acquisition and demolition. In addition, scattered trees, enclosures, electricity and telecommunication facilities will be affected.</p>
4	Xiji County, Guyuan Municipality	<p>①Road Construction: Jiangtai-Xitan-Pingfeng Road totally adopt the former road at section K0+000-K0+685.438; reconstruct the former road at section K0+685.438~K5+800; adopt the former road in part and reconstruct the former road in part at section K5+800-K29+080 and K33+340~K73+000; build new road at section K29+080.784~K32+400. Total length is 73km, with the subgrade width of 7.5m and pavement width of 7m. (The total amount is estimated to be CNY 405,165,141).</p> <p>②LA impacts: A total of 1,898.6 mu of rural collective land will be acquired permanently, including 1,387.4 mu of farmland (73.07%), 2.7 mu of residential land (0.14%), and 3.1 mu of unused land (0.16%).</p> <p>③HD impacts: Houses of 500m2 which are all in earth-wood structure will be demolished..</p>

		<p>④Affected Persons: 1,188 households with 5,281 people will be affected by LA and 4 households with 35 people will be affected by HD, totaling 1,188 households with 5,281 people affected.</p> <p>⑤the project does not involve in temporary land occupation according to the feasibility study report. And no enterprise or shop will be affected by LA and HD. In addition, scattered trees, poles, wires, tombs, enclosures, water wells and other ground ancillary facilities will be affected.</p>
5	Pengyang County, Guyuan Municipality	<p>①Road Construction: Chunshucha (Mengyuan) -Yangping (Chengyang) Road starts at K1784+100 of Line G309 from north to south, passing by Mengyuan Town, Wugou Town, and Chengyang Town, and ends at Yangping Village of Chengyang Town. The ending point (K30+727.08) is at K19+136 of Pengyang-Zhenyuan Road. The project is 30.75km long in total, with the subgrade width of 7.5m and pavement width of 6.5m. The total investment is estimated to be CNY 91.006202 million.</p> <p>②LA impacts: A total of 506.51 mu of land will be acquired, including 201.06 mu farmland, 2 mu residential land, and 296.15 mu unused land.</p> <p>③HD impacts: The project will involve 1,253.8 m² building demolition (369.6 m² brick-wood buildings and 884.2 m² earth-wood buildings).</p> <p>④Affected Persons: 205 households with 814 persons will be affected by land acquisition, and ten households with 45 persons will be affected both by house demolition and land acquisition. In total 205 households with 814 persons will be affected by LAR. .</p> <p>⑤No enterprises or shops are involved in the acquisition and demolition. In addition, scattered trees, poles, wires, water wells and other ground ancillary facilities will be affected.</p> <p>⑥Temporary Land Occupation: So far as designed, 161.9 mu of land will be temporarily occupied, which is all unused land.</p>
6	Jingyuan County, Guyuan Municipality	<p>①Road Construction: (i) Shatang (Huanghua Town)-Gaodian Road is the rural trunk road and includes main section and branch section. The main section starts from Shatang Village of Huanghua Town in Jingyuan County, intersects road S313 that is newly planned (formal Jingyuanping Road), and ends at Haodian Village in Liupanshan Town, intersects road G312 at the section of K1835+318, with the whole length of 13.443 km, with the designed speed of 30 km/h, width of subgrade of 7.5 m, and width of pavement of 6.5 m. The branch section starts from Tuyao Village, intersects the main section at K3+023.63, and ends at Tuyao Village, intersects the section of K0+856, with the whole length of 1.782 km, with the designed speed of 20 km/h, width of subgrade of 6.5 m, and width of pavement of 6.0 m. The total investment for this trunk road is estimated to be CNY 46,591,274. (ii) Dongxia-Digou road project is the feeder road project, including one main road and three branches. The main road starts from road S101 in Dongxia Town, goes southeastward and then northeastward via Pangdong Village along the old road, and ends at Digou Forest Protection Station of Longtan Forest Farm via the west part of Dongxia Village and Shidi Village, with the stake number of K8+200 (ending point). Branch A starts from Pangdong Village, connects stake K1+242.1 of main road, and ends at the unsurfaced road at the east end of Pangdong Village via Group 3 of Pangdong Village along the old road, with stake number of AK0+661 (ending point); Branch B starts from the intersection of the west part of Dongxia Village and main road K4+354.79, goes southward via Dongxia Village, and then southward at K0+725, and stops at the end of Shangxia Village along the old road, with stake number of BK2+162 (ending point); Branch C starts from Shidi Village, and intersects main road K5+123.81, goes westward along the old road, and ends at the unsurfaced road of the west end of the village. The total distance of construction is 11.717 km and the total investment is estimated to be RMB 24,542,200 Yuan.</p> <p>②LA impacts: A total of 394.52mu of land will be acquired, including 160.01 mu of Farmland (40.6%), 24.31 mu of Residential land (6.2%), and 210.2 mu of Forest land (53.3%).</p> <p>③HD impacts: The residential houses involved in the house demolition (HD) are rural houses of 2,169 m², are brick-wood houses of 624 m² and earth-wood houses of 1,545 m².</p> <p>④Affected Persons: 112 households with 432 persons will be affected by LA, of which both LA and HD will affect 38 households with 134 persons.</p> <p>⑤No enterprises or shops are involved in the acquisition and demolition. In addition, scattered trees, poles, wires, tombs, enclosures, water wells and other ground ancillary facilities will be affected.</p> <p>⑥Temporary Land Occupation: The project will acquire 17 mu of temporary land that is unutilized land.</p>

Note: One feeder road (Zhangtian-Jinglin-Yangchuan Road) in Longde County, which only involved relocation of some ground attachments, was completed in 2017. See details in the 2nd external resettlement monitoring report.

Table 1-3: Summary of Rural Roads and Civil works Implementation Progresses (up to 31 Dec 2022)

#	Category	Road Name	County/district	Categories of LAR impacts	Civil works implementation progress	LAR implementation progress
1	Trunk	Wangtuan-Yuwan Road	Tongxin	LA, HD	Completed	LAR activities completed already
2	Trunk	Zhengqi-Jiucui-Sikouzi Road	Haiyuan	LA, HD	Completed	LAR activities completed already
3	Trunk	Shatang (Huanghua Town)-Gaodian Road	Jingyuan	LA	Completed	LAR activities completed already
4	Trunk	Chunshucha (Mengyuan) -Yangping (Chengyang) Road	Pengyang	LA, HD	Completed	LAR activities completed already
5	Trunk	Jiangtai-Xitan-Pingfeng Road	Xiji	LA, HD	Completed	LAR activities completed already
6	Trunk	Guanting-Guyuan Road	Yuanzhou	LA, HD	Completed	LAR activities completed already
7	Trunk	Wanzhang-Sanying Road	Yuanzhou	LA, HD	Completed	LAR activities completed already

Note: The LAR activities of Haiyuan Subproject was completed in 2019, see details in the 4th external resettlement monitoring report. After the design changes of Dongxia-Digou feeder road in Jingyuan County, it does not involve LAR impacts, as it has been upgraded and completed on the original road with domestic funds in 2019.

1.3 External Resettlement Monitoring and Evaluation

5. In line with the requirements in PRs on external resettlement M&E, the EMA prepared this M&E report on basis of the actual progress of the Project. The period covered by this E&M report is from October 2021 to 31 December 2022.

1.3.1 EMA

6. Recruited by PMOs, the resettlement specialist of Hangzhou Darren Engineer Project Management Co, Ltd., is responsible for the external resettlement M&E of the Project.

1.3.2 M&E Scope

7. External M&E covers all the 7 rural trunk roads in 6 project counties which all involve LAR impacts and external resettlement M&E requirements. Meanwhile, the other 19 rural feeder roads have completed their land compensation activities which were presented in a separate Resettlement Due Diligence Report, which had been submitted to ADB in May 2018. In addition, Haiyuan Subproject was completed in 2019, see details in the 4th external resettlement monitoring report, and Tongxin Subproject was completed in 2021, see details in the 6th external resettlement monitoring report.

1.3.3 M&E Contents

8. The external M&E reports will monitor and evaluate the progress and implementation status of RPs in 6 project counties/district, including changes of LAR impacts, resettlement implementing progress, compliance with compensation policies for land, houses and other assets, implementation status of livelihood restoration and resettlement, the satisfaction levels of affected population, capacity buildings of relevant organizations, GRM, etc. See details in Table 1-4.

Table 1-4: Main Contents of External Resettlement M&E

No.	Project Counties	Contents of M&E
1	Tongxin County, Wuzhong Municipality	LAR impacts and implementation status
2	Haiyuan County, Zhongwei Municipality	LAR impacts and implementation status
3	Yuanzhou District, Guyuan Municipality	LAR impacts and implementation status
4	Xiji County, Guyuan Municipality	LAR impacts and implementation status
5	Pengyang County, Guyuan Municipality	LAR impacts and implementation status
6	Jingyuan County, Guyuan Municipality	LAR impacts and implementation status

2 Monitoring and Evaluation of Resettlement Implementation

2.1 Summary of Resettlement Impacts and RPs Updating

9. See details in Table 2-1.

Table 2-1: LAR Impacts in Original RPs and RPs Preparation/Updating

No.	Project county/district	LAR impacts in draft RPs	Draft RP prepared	RP Updating
1	Tongxin County, Wuzhong Municipality	It plans to reconstruct the Wangtuan-Yuwan Road. 1942.77 mu of land will be acquired, and 3888m2 of rural residential houses will be demolished. Totally 149 HHs with 616 persons will be affected by LAR, in which 25 HHs with 108 persons will be affected by HD. No enterprises or shops are involved in the acquisition and demolition.	Draft standalone RP Prepared	RP updated and approved in June 2019
2	Haiyuan County, Zhongwei Municipality	It plans to construct the Zhengqi-Jiucui-Sikouzi Road. 485 mu of land will be acquired, affecting 108 HHs with 507 persons. The project will involve 240 m ² of house demolition with earth-wood structure, affecting 1 HH with 12 persons, who will be also affected by LA. No enterprises or shops are involved in the land acquisition and house demolition.	Draft standalone RP Prepared	RP updated and approved in April 2019
3	Yuanzhou District, Guyuan Municipality	It plans to construct the Guanting-Guyuan Section of Guyuan-Xiji Road and Wanzhang-Sanying Road. 1218.2mu of land will be acquired, and 650 m2 of residential houses in brick-wood structure will be demolished. In total, 269 HHs with 1130 persons will be affected by the subproject. No enterprises or shops are involved in the acquisition and demolition.	Draft standalone RP Prepared	RP updated in Feb 2020 for Guyuan-Xiji Road (Guanting-Yuanzhou Section), and RP updated in Aug 2020 for Wanzhang-Sanying Road
4	Xiji County, Guyuan Municipality	It plans to construct the Jiangtai-Xitan-Pingfeng Road. 1898.6mu of land will be acquired, and 500 m2 of residential houses in earth-wood structure will be demolished. In total, 1188 HHs with 5281 persons will be affected by the subproject, including 4 HHs with 35 persons affected by HD. No enterprises or shops are involved in the acquisition and demolition.	Draft standalone RP Prepared	RP updated and approved in March 2020
5	Pengyang County, Guyuan Municipality	It plans to construct Chunshucha (Mengyuan) - Yangping (Chengyang) Road. 506.51mu of land will be acquired, and 1253.8 m2 of residential houses will be demolished. In total, 205 HHs with 814 persons will be affected by the subproject, including 10 HHs with 45 persons affected by HD. No enterprises or shops are involved in the acquisition and demolition.	Draft standalone RP Prepared	RP updated in October 2020
6	Jingyuan County, Guyuan Municipality	It plans to construct Shatang (Huanghua Town)-Gaodian Road and Dongxia-Digou road. 394.52 mu of land will be acquired, and 2169 m2 of residential houses will be demolished. In total, 112 HHs with 432 persons will be affected by the subproject, including 38 HHs with 134 persons affected by HD. No enterprises or shops are involved in the acquisition and demolition.	Draft standalone RP Prepared	RP updated in May 2020.

2.2 Resettlement M&E of Subproject in Tongxin County, Wuzhong Municipality

2.2.1 Planned and Actual Resettlement Impacts

(i) Land Acquisition (LA)

10. See details of the LA impacts in Table 2-2.

Table 2-2: Permanent Collective Land Acquisition Impacts of Tongxin Subproject

Road	Indicators		Original RP	Updated RP	Actual impacts during implementation
Wangtuan - Yuwang Road	LA Area (mu)		1942.77	2057.42	841.25
	In which (mu)	Farmland	403.3	339.1 ^①	693.99 ^②
		Residential land	14.11	8.59	0
		Unused land	1514.01	1458.55	0
		Forest land	11.35	251.18	147.26
	AHs		149	188	344
	APs		616	817	897
	Affected towns		2	2	2
	Affected villages		9	9	9

Source: local sub-PMO.

(ii) House Demolition (HD)

11. See details of HD impacts in Table 2-3.

Table 2-3: Rural Residential House Demolition Impacts of Tongxin Subproject

Road	Indicators		Original RP	Updated RP	Actual impacts during implementation
Wangtuan - Yuwang Road	HD Area (m2)		3888	1759.3	1189.18
	In which (m2)	Timber-brick	3685	721	624.29
		Earth-wood	203	1038.3	564.89
	AHs		25	20	12
	APs		108	101	53
	Affected towns		2	2	2
	Affected villages		3	4	2

Source: local sub-PMO.

(iii) Affected Persons (APs)

12. See details of APs in Table 2-4.

Table 2-4: Affected Population of Tongxin Subproject

Type	Phases	Wangtuan		Yuwang		Subtotal	
		Number of households	Number of people	Number of households	Number of people	Number of households	Number of people
LA impact	Original RP	95	391	54	225	149	616
	Updated RP	78	339	110	478	188	817
	Actual Impacts during RP implementation	158	417	186	480	344	897
HD impact	Original RP	22	95	3	13	25	108
	Updated RP	16	80	4	21	20	101
	Actual Impacts during RP implementation	10	41	2	12	12	53
Total	Original RP	95	391	54	225	149	616
	Updated RP	78	339	110	478	188	817
	Actual Impacts during RP implementation	168	461	188	492	356	950

Source: local sub-PMO.

2.2.2 Compensation Rates and Resettlement Measures

^① Including 14.92mu Irrigated land and 324.18 mu farmland.^② Including 53.67mu Irrigated land and 640.32 mu farmland

(i) Compensation rates of LA and HD

13. See details of LA and compensation rates in Table 2-5.

Table 2-5: LA and HD Compensation Standards of Tongxin Subproject

LA	Acrid land/Residential land		Unused land		Forest land	Young crops
Original RP	6,400 yuan/mu		1,280 yuan/mu		N/A	600 yuan/mu
Updated RP	24,840 yuan/mu for irrigated land and 6,400 yuan/mu for dryland and residential land		1,280 yuan/mu		Trees: 4,480 yuan / mu; Shrubs: 3,840 yuan / mu	600 yuan/mu
Actually implemented	24,840 yuan/mu for irrigated land and 6,400 yuan/mu for dryland and residential land		N/A		Shrubs: 3,840 yuan/mu	Huangqi, Chaihu 2,000 yuan / mu; Corn 2,400 yuan / mu; Wheat 300 yuan / mu
HD	Brick-concrete	Brick-timber	Earth-wood	Makeshift house	relocation subsidy (One time)	Subsidy for temporal resettlement (6 months)
Original RP	600 yuan/M ²	410 yuan/M ²	310 yuan/M ²	100 yuan/M ²	1,000yuan	300 yuan/month per HH
Updated RP	600 yuan/M ²	410 yuan/M ²	310 yuan/M ²	100 yuan/M ²	1,000yuan	300 yuan/month per HH
Actually implemented	Based on market valuation price, the actual rates are higher than these in URP.					

Source: local sub-PMO.

(ii) Compensation rates for Temporary Land Occupation

14. See details in Table 2-6.

Table 2-6: Temporary Land Occupation Compensation Standards of Tongxin Subproject

Phases	Type	Area (mu)	Compensation standard
Original RP	Unused land	1651.06	600 yuan/mu
Updated RP	Unused land	170	600 yuan/mu
Actually implemented	Water irrigated land	1.28	2,400 yuan/mu

Source: local sub-PMO.

(iii) Planned Livelihood Restoration and Resettlement Measures

15. To minimize the resettlement impacts to APs and restore their living standards, rehabilitation measures have been developed and included in this RP. The comprehensive compensation and livelihood restoration packages, including expanding cash crop plantation, improving existing low yield farmland, etc., will help offset the losses from land acquisition. Since this Subproject is in a linear impact scope, the land and income loss of AHs are very slight. After cash compensation, their income is relatively easy to recover, and they directly benefit from the convenient transportation brought by road construction.

16. For households affected by HD (all affected partly), two options are available for them to choose at their own wills. In both cases, cash compensation for residential land, house structures and attachments as well as transfer allowances will be provided to AHs. The major options include:

1) Providing housing land with cash compensation for houses: The villagers committees select and allocate appropriate housing land to the affected households around their former residential land, and the new housing land area shall not be less than the former area. And the village committees have promised that they will provide housing land within their village to relocate the AHs and the resettlement place will be determined before civil works.

2) Full cash compensation and reconstruction on existing housing land: As there are more than 2 mu housing land per household affected by the project, the AHs can rebuild new houses within the scope of their existing housing land after HD. The compensation will be paid for affected housing land and houses.

According to M&E, all 12 AHs had chosen cash compensation and self-resettlement. So far, house compensation and housing resettlement had been properly solved.

2.2.3 Progress of Project and Resettlement Implementation

(i) Subproject implementation progress

17. As of 31 December 2022, Wangtuan-Yuwang road in Tongxin County had completed all civil works.

18. In addition, the Subproject obtained the pre-examination approval of construction land from the Department of Natural Resources of the Autonomous Region in 2017. However, due to the Subproject involved the occupation of some basic farmland, according to the current national construction land approval policy, the construction land approval has not been obtained.

(ii) Resettlement Implementation Progress

19. Tongxin subproject had signed all the LA and HD agreements and paid the LAR compensation fees, with a total 841.25 mu of LA and 1189.18 m² of HD, affected 356 AHs, with a total of 7.9595 million yuan paid.

20. See details in Table 2-7.

Table 2-7: Summary payment of LAR funds (actually completed) in Tongxin Subproject

No.	Category	Resettlement funds (Yuan)	Percentage of payment
1	Permanent LA	5,996,689.2	100%
2	Temporary land	3,072	100%
3	HD	1,397,270	100%
4	young crops	32,110	100%
5	Ground attachments	530,339.8	100%
6	Total	7,959,481	100%

Source: local sub-PMO.

2.2.4 Main Findings during External M&E

21. (i) Tongxin subproject has completed the civil works in November 2020.

22. (ii) Tongxin Subproject has completed the signing of LA and HD agreements and all payment of resettlement funds.

23. (iii) Remaining issues/tasks: Tongxin sub-PMO should: i) proceed the approval of construction land as soon as possible with coordination with relevant local government departments; ii) continuously provide support on livelihood restoration for AHs; and iii) get ready to carry out resettlement completion review.

2.3 Resettlement M&E of Subproject in Yuanzhou District, Guyuan Municipality

2.3.1 Planned and Actual Resettlement Impacts

(i) Land Acquisition

24. Details are shown in Table 2-8.

Table 2-8: Permanent Acquisition of Collective Land of Yuanzhou Subproject

Road	Indicators		Original RP	Updated RP	Actually implemented
Guyuan-Xiji Road (Guanting-Yuanzhou section)	Permanent land (mu)		527.9	649.35	702.04
	Land type (mu)	Farmland	202.4	334.01	229.02
		Residential land	1.7	2.06	61.52
		Unused land	323.8	313.28	165.91
		Forest land ^①	0	0	235.78
		Grass land	0	0	9.81
	Number of affected households		94	126	332
	Affected population		395	562	1,292
	Town/township		1	1	1
	Villagers committee		4	4	6
Wanzhang-Sanying Road	Permanent land (mu)		690.3	613.72	647.01
	Land type (mu)	Plough	250.6	458.32	481.91
		Residential land	0.8	1.25	0
		Unused land	415.1	0	0
		Forest land	23.8	154.55	113.13
		Grass land	0	0	51.97
	Number of affected households		175	282	301
	Affected population		735	1117	1169
	Town/township		3	3	3
	Villagers committee		6	6	8
Total	Total permanent land(mu)		1,218.2	1,263.07	1,349.05
	Number of affected households		269	408	633
	Affected population		1,130	1,679	2,461

Source: local sub-PMO.

(ii) House Demolition (HD)

25. See details in Table 2-9.

Table 2-9: Impacts of Rural Residential House demolition of Yuanzhou Subproject

Road	Indicators		Original RP	Updated RP	Actually implemented
Guyuan-Xiji Road (Guanting-Yuanzhou section)	HD Area (m2)		350	380	2,653.83
	In which (m2)	Brick	350	270	1,028.24
		Earth-wood	0	110	437.66
		Simple	0	0	1,187.93
	AHs		3	4	27
	APs		15	20	109
	Affected towns		1	1	1
	Affected villages		2	3	5
Wanzhang-Sanying Road	HD Area (m2)		300	610	700.22
	In which (m2)	Brick	300	450	455.83
		Earth-wood (Non-residential)	0	100	244.39
		Non-residential brick	/	60	0
	AHs		3	4	7
	APs		15	21	29
	Affected towns		1	2	2
	Affected villages		1	2	2

^① Return dry land to forest land.

Total	Total HD Area (m2)	650	990	3,354.05
	AHs	6	8	34
	APs	30	41	138

Source: local sub-PMO. n/a= not available so far.

(iii) Affected Persons (APs)

26. See details in Table 2-10.

Table 2-10: Affected Population of Yuanzhou Subproject

Type	Phases	Guanting		Touying		Sanying		Zhaike		Subtotal	
		AHs	APs	AHs	APs	AHs	APs	AHs	APs	AHs	APs
LA impact	Original RP	94	395	23	97	112	470	40	168	269	1130
	Updated RP	126	562	71	302	185	702	26	113	408	1679
	Actually implemented	332	1,292	32	124	226	875	43	170	633	2,461
HD impact	Original RP	3	15	0	0	3	15	0	0	6	30
	Updated RP	4	20	1	5	3	16	0	0	8	41
	Actually implemented	27	109	0	0	6	25	1	4	34	138
Total	Original RP	94	395	23	97	112	470	40	168	269	1130
	Updated RP	126	562	71	302	185	702	26	113	408	1679
	Actually implemented	359	1401	32	124	232	900	44	174	667	2,599

Source: local sub-PMO. n/a= not available so far.

2.3.2 Compensation Rates and Resettlement Measures

(i) Compensation Rate for Permanent Land Acquisition and House Demolition

27. See details in Table 2-11.

Table 2-11: LA and HD Compensation Standards of Yuanzhou Subproject

LA	Acrid land/Residential land		Unused land		Young crops
Original RP	6,400 yuan/mu		1,280 yuan/mu		700 yuan/mu
Updated RP	8,500 yuan/mu		1,700 yuan/mu		1,000 yuan/mu
Actually implemented	26,000 yuan/mu		3,000 yuan/mu		1,000 yuan/mu
HD	Brick-concrete	Simple (non-residential)	Earth-wood	Temporary house	transition subsidy (6 months)
Original RP	600 yuan/M ²	N/A	310 yuan/M ²	100 yuan/M ²	300 yuan/month. HH
Updated RP	600 yuan/M ²	280 yuan/M ²	310 yuan/M ²	100 yuan/M ²	300 yuan/month. HH
Actually implemented	1,200 yuan/M ²	300 yuan/M ²	680 yuan/M ²	300 yuan/M ²	All AHs have other housing without transitional resettlement

Source: local sub-PMO. N/A= not applicable.

(ii) Compensation Rate for Temporary Land Occupation

28. In Guyuan-Xiji Road (Guanting-Yuanzhou section), the impacts of temporary land use occupation are avoided. In Wanzhang-Sanying Road, the compensation standard for temporary land use is 1,000 yuan/mu.

(iii) Resettlement and livelihood rehabilitation

29. To minimize the resettlement impacts to APs and restore their living standards, rehabilitation measures have been developed and included in this RP. The comprehensive compensation and livelihood restoration packages, including expanding cash crop plantation, improving existing low yield farmland, etc., will help offset the losses from land acquisition.

Since this Subproject is in a linear scope, the land and income loss of AHs are very slight. After cash compensation, their income is relatively easy to recover, and they directly benefit from the convenient transportation brought by road construction.

30. For households affected by HD (all affected partly), two options are available for them to choose at their own wills. In both cases, cash compensation for residential land, house structures and attachments as well as transfer allowances will be provided to AHs. The major options include:

i) Providing housing land with cash compensation for houses: The villagers committees select and allocate appropriate housing land to the affected households around their former residential land, and the new housing land area shall not be less than the former area. And the village committees have promised that they will provide housing land within their village to relocate the AHs and the resettlement place will be determined before civil works.

31. ii) Full cash compensation and reconstruction on existing housing land: As there are more than 2 mu housing land per household affected by the project, the AHs can rebuild new houses within the scope of their existing housing land after HD. The compensation will be paid for affected housing land and houses.

32. According to M&E, all AHs had chosen cash compensation and self-resettlement and moved to other existing houses.

2.3.3 Progress of Project and Resettlement Implementation

(i) Subproject implementation progress

33. 1) **Guyuan-Xiji Road (Guanting-Yuanzhou section):** The FSR was approved in July 2016. The original land use pre-examination was obtained in 2017. The preliminary design was approved in January 2018, and the construction drawing was approved in March 2018. The contract was awarded on August 10, 2020. The new land use pre-examination has been obtained in September 2020. Due to the ecological red line, it is necessary to obtain the approval of occupying the red line of ecological protection, which has been submitted to the Ministry of Natural Resources in April 2020. The local government issued a land acquisition announcement for the subproject in July 2020 and has started civil works in August 2020. The LAR compensation announcement was issued on 20 October 2020. At of 31 December 2022, civil works of the Subproject have been completed.



Figure 2-1: Sites of Guyuan-Xiji Road

34. 2) **Wanzhang-Sanying Road:** The FSR was approved in July 2016. The land use pre-examination was obtained in August 2017. The construction drawing was approved in April

2019. The Subproject issued a land acquisition notice in July 2020. The civil work contract was awarded on 15 October 2020. This road has started civil works from November 5, 2020. The LAR compensation announcement was issued on 20 October 2020. The Ningxia Autonomous Region Government announced a new land acquisition compensation policy on December 19, 2020. So, the Yuanzhou District Government had updated the land compensation rates in accordance with the new policy on April 30, 2021. At of 31 December 2022, civil works of the Subproject have been completed.

(ii) Resettlement Implementation Progress

35. Guyuan-Xiji Road (Guanting-Yuanzhou section) Subproject had signed all the LA and HD agreements and paid the LAR compensation fees, with a total 702.04 mu of LA and 2653.83 m² of HD, affected 359 AHs, with a total of 22.0343 million yuan paid.

36. Wanzhang-Sanying Road Subproject had signed all the LA and HD agreements and paid the LAR compensation fees, with a total 647.01 mu of LA and 700.22 m² of HD, affected 308 AHs, with a total of 11.4467 million yuan paid.

37. See details in Table 2-12.

Table 2-12: Summary payment of LAR funds (actually completed) in Yuanzhou Subproject

No.	Category	Resettlement funds (10,000 Yuan)			Percentage of payment
		Guyuan-Xiji Road (Guanting-Yuanzhou section)	Wanzhang-Sanying Road	Total	
1	Permanent LA	1,718.56	294.55	2,013.11	100%
2	HD	461.34	60.74	522.08	100%
3	Young crops and ground attachments	23.53	789.38	812.91	100%
4	Total	2,203.43	1,144.67	3,348.1	100%

Source: local sub-PMO.

2.3.4 Main Findings during External M&E

38. (i) The Guyuan-Xiji Road (Guanting-Yuanzhou Section) and Wanzhang-Sanying Road in Yuanzhou District have completed all civil works.

39. (ii) The Guyuan-Xiji Road (Guanting-Yuanzhou Section) and Wanzhang-Sanying Road in Yuanzhou District have completed the signing of LA and HD agreements and payment of all resettlement funds.

40. (iii) Remaining issues/tasks: i) The Guyuan-Xiji Road (Guanting-Yuanzhou section) and Wanzhang-Sanying Road Subprojects should proceed the approval of construction land as soon as possible with coordination of relevant local government departments; ii) continuously provide support on livelihood restoration for AHs; and iii) get ready to carry out resettlement completion review.

2.4 Resettlement M&E of Subproject in Xiji County, Guyuan Municipality

2.4.1 Planned and Actual Resettlement Impacts

(i) Land Acquisition

41. See details in Table 2-13.

Table 2-13: Permanent Acquisition of Collective Land of Xiji Subproject

Road	Indicators		Original RP	Updated RP	Actually implemented
Jiangtai-Xitan-Pingfeng Road	Permanent land (mu)		1,898.6	1,815.9	1,314.22
	Land type (mu)	Farmland	1,387.4	1,356.4	1,015
		Residential land	2.7	2.9	0
		Unused land	3.1	0	0
		Forest land	505.4	456.6	299.15
	AHs		1,188	1,171	1,715
	APs		5,281	5,132	7,621
	Town/township		5	4	5
	Villagers committee		20	19	22

Source: local sub-PMO.

(ii) House Demolition (HD)

42. See details in Table 2-14.

Table 2-14: Impacts of Rural Residential House Demolition of Xiji Subproject

Road	Indicators		Original RP	Updated RP	Actually implemented
Jiangtai-Xitan-Pingfeng Road	HD Area (m ²)		574	1343	11,145.65
	In which (m ²)	Brick-wood	424	832	941.03
		brick-concrete	/	/	1,412.26
		Earth-wood	150	511	275.68
		Simple	/	/	4,551.53
	AHs		8	10	88
	APs		35	43	355
	Affected towns		3	3	4
	Affected villages		4	3	9

Source: local sub-PMO.

(iii) Affected Persons (APs)

43. See details in Table 2-15.

Table 2-15: Affected Population of Xiji Subproject

Type	Phases	Subtotal	
		AHs	APs
LA impact	Original RP	1,188	5,281
	Updated RP	1,171	5,132
	Actually implemented	1,715	7,621
HD impact	Original RP	8	35
	Updated RP	10	43
	Actually implemented	88	355
Total	Original RP	1,188	5,281
	Updated RP	1,171	5,132
	Actually implemented	1,803	7,976

Source: local sub-PMO.

2.4.2 Compensation Rates and Resettlement Measures

(i) Compensation rates of LA and HD

44. See details in Table 2-16.

Table 2-16: LA and HD Compensation Standards of Xiji Subproject

LA	Acrid land/Residential land	Forest land (arbor)	Forest land (bush)	Forest land (return acrid land)	Young crops
Original RP	13,472 yuan/mu	9,430 yuan/mu	8,083 yuan/mu	/	850 yuan/mu

Updated RP	13,472 yuan/mu	9,430 yuan/mu	8,083 yuan/mu	/	850 yuan/mu
Actually implemented	14,520 yuan/mu(III area) 15,480 yuan/mu(II area)	N/A	N/A	14,520 yuan/mu	850 yuan/mu(acrid) 1,000 yuan/mu(irrigated) 1,200 yuan/mu(alfalfa)
HD	Brick-timber	Earth-wood	Moving Subsidy (one-off)		Transition subsidy (6 months)
Original RP	600 yuan/M2	310 yuan/M2	1,000 yuan		300yuan/month. HH
Updated RP	600 yuan/M2	310 yuan/M2	N/A		N/A
Actually implemented	Based on market evaluation value and higher than these in URP.				

Source: local sub-PMO.

(ii) Temporary Land Occupation

45. Xiji Subproject temporarily occupied 73.39 mu of farmland. The compensation standard for temporary occupation of cultivated land is 850 yuan/mu.

(iii) Resettlement and livelihood rehabilitation

46. To minimize the resettlement impacts to APs and restore their living standards, a rehabilitation plan has been developed and included in this RP. The comprehensive compensation package that will be used by the affected households, which includes expanding cash crop plantation, improving existing low yield cash crops and land rental to expand agricultural plantation, can offset the losses incurred due to the land acquisition impacts. Additionally, arranged jobs, waged non-farming jobs, off-farming business, and special measures for vulnerable groups have been put in place. Since this Subproject is in a linear scope, the land and income loss of AHs are very slight. After cash compensation, their income is relatively easy to recover, and they directly benefit from the convenient transportation brought by road construction.

47. For physically displaced households (i.e., house demolition), two options are available for them to choose according to their own desire in order to restore their living condition. In both cases, cash compensation for Residential land, house structures and attachments based on replacement costs as well as transfer allowances will be provided. The major options include:

- i) Cash compensation and self-resettlement. The compensation standard will be determined in accordance with replacement cost proposed in the resettlement plan.
- ii) Housing land and subsidy provided by local government: The villagers committees select and allocate appropriate housing land to the affected households, and the allocated area shall be not less than the former area. And the village committees have promised that they will arrange housing land within their village to relocate the APs and the resettlement place will be determined before the project is constructed.

48. According to M&E, all AHs had chosen cash compensation and self-resettlement, as they had remaining houses or surplus homestead for building new houses. So far, HD compensation and housing resettlement had been properly solved.

2.4.3 Progress of Project and Resettlement Implementation

(i) Subproject implementation progress

49. Jiangtai-Xitan-Pingfeng Road: this subproject has started civil works in July 2020.

50. Due to the occupation of the basic farmland and ecological red line, it needed to carry on the land use pre-examination again and obtain the approval of construction land from Nature and Resources Ministry. On January 26, 2021, the Xiji Subproject received and use pre-examination opinion from the Ministry of Natural Resources. So far, the construction land application document had not been formally approved. The subproject issued a tender

advertisement on 30 September 2019 and opened the tender in the end of October 2019. The notice of housing demolition and the pre-announcement of land acquisition were disclosed in March 2020.

51. All four civil work package contracts were signed in the first half of 2020. As of 31 Dec 2022, three civil works contracts had been completed and the main part of the remaining one civil work had been completed.



Figure 2-2: Jiangtai-Xitan-Pingfeng Road

(ii) Resettlement Implementation Progress

52. As of 31 Dec 2022, Xiji County had signed all the LA and HD agreements and paid the LAR compensation fees, with a total 1314.22 mu of LA and 11145.65 m² of HD, affected 1,803 AHs, with a total of 33.5691 million yuan paid. See details in Table 2-17.

Table 2-17: Summary payment of LAR funds (actually completed) in Xiji Subproject

No.	Category	Resettlement funds (Yuan)	Percentage of payment
1	HD	12,778,161	100%
2	Permanent LA	19,042,297.21	100%
3	Ground attachments	1,748,677.6	100%
4	Total	33,569,135.81	100%

Source: local sub-PMO.

2.4.4 Main Findings during External M&E

53. (i) Xiji subproject had signed all LA and HD agreements and paid the LAR compensation fees.

54. (ii) Remaining issues/tasks: i) proceed the approval of construction land as soon as possible through coordination with relevant local government departments; ii) continuously provide support on livelihood restoration for AHs; and iii) get ready to carry out resettlement completion review.

2.5 Resettlement M&E of Subproject in Pengyang County, Guyuan Municipality

2.5.1 Planned and Actual Resettlement Impacts

(i) Land Acquisition

55. See details in Table 2-18.

Table 2-18: Permanent Acquisition of Collective Land of Pengyang County

Road	Indicators	Original RP	Updated RP	Actually implemented
Chunshucha (Mengyuan) -Yangping (Chengyang) Road	Permanent land (mu)	506.51	399.92	353.99
	Land type (mu)	Farmland	201.06	237.42
		Residential land	9.3	1.89
		Unused land	296.15	36.09
		Forest land	/	124.52
	AHs	205	179	426
	APs	814	758	1,317
	Town/township	3	2	2
	Villagers committee	9	8	8

Source: local sub-PMO.

(ii) House Demolition (HD)

56. See details in Table 2-19.

Table 2-19: Impacts of Residential House Demolition of Pengyang Subproject

Road	Indicators	Original RP	Updated RP	Actually implemented
Chunshucha (Mengyuan) -Yangping (Chengyang) Road	HD Area (m2)	1253.8	925	827.6
	In which (m2)	Brick-wood	369.6	300
		Earth-wood	884.2	625
		Simple	/	/
	AHs	10	6	13
	APs	45	26	51
	Affected towns	2	1	1
	Affected villages	2	1	1

Source: local sub-PMO.

(iii) Affected Persons (APs)

57. See details in Table 2-20.

Table 2-20: Affected Population of Pengyang Subproject

Type	Phases	Subtotal	
		AHs	APs
LA impact	Original RP	205	814
	Updated RP	179	758
	Actually implemented	426	1,317
HD impact	Original RP	10	45
	Updated RP	6	26
	Actually implemented	13	51
Total	Original RP	205	814
	Updated RP	179	758
	Actually implemented	439	1,368

Source: local sub-PMO.

2.5.2 Compensation Rates and Resettlement Measures

(i) Compensation rates of LA and HD

Table 2-21: LA and HD Compensation Standards of Pengyang Subproject

LA	Farmland/ Residential land	Unused land	Young crops
Original RP	11,200 yuan/mu	2,240 yuan/mu	600 yuan/mu
Updated RP	11,200 yuan/mu	2,240 yuan/mu	600 yuan/mu

Actually implemented	23,400 yuan/mu(I area) 24,800 yuan/mu(II area)		/		Included in the comprehensive land compensation rates	
HD	Brick-concrete	Brick-timber	Earth-wood	Makeshift house	relocation subsidy (one time)	transition subsidy (6 months)
Original RP	600 Yuan/M ²	410 yuan/M ²	310 yuan/M ²	100 yuan/M ²	1,000 yuan/HH	300 yuan/month. HH
Updated RP	/	670 yuan/M ²	320 yuan/M ²	/	1,000 yuan/HH	300 yuan/month. HH
Actually implemented	740	670	320	100-200	/	400 (18 months)

Source: local sub-PMO.

(ii) Compensation rate for temporary land occupation

58. Pengyang Subproject temporarily occupied 113.83 mu of farmland. The compensation standard is determined as CNY 600 per mu for temporary land occupation.

(iii) Resettlement and livelihood rehabilitation

59. To minimize the resettlement impacts to APs and restore their living standards, rehabilitation measures have been developed and included in this RP. The comprehensive compensation and livelihood restoration packages, including expanding cash crop plantation, improving existing low yield farmland, etc., will help offset the losses from land acquisition. Since this Subproject is in a linear scope, the land and income loss of AHs are very slight. After cash compensation, their income is relatively easy to recover, and they directly benefit from the convenient transportation brought by road construction.

60. For households affected by HD (all affected partly), two options are available for them to choose at their own wills. In both cases, cash compensation for residential land, house structures and attachments as well as transfer allowances will be provided to AHs. The major options include:

i) Providing housing land with cash compensation for houses: The villagers committees select and allocate appropriate housing land to the affected households around their former residential land, and the new housing land area shall not be less than the former area. And the village committees have promised that they will provide housing land within their village to relocate the AHs and the resettlement place will be determined before civil works.

ii) Full cash compensation and reconstruction on existing housing land: As there are more than 2 mu housing land per household affected by the project, the AHs can rebuild new houses within the scope of their existing housing land after HD. The compensation will be paid for affected housing land and houses.

61. According to M&E, all 9 AHs had chosen cash compensation and self-resettlement. They had purchased new houses in a centralized resettlement site with the cash compensation and enjoyed partial price concessions.

2.5.3 Progress of Project and Resettlement Implementation

(i) Subproject implementation progress

62. Chunshucha (Mengyuan) -Yangping (Chengyang) Road: The final design was approved on 30 March 2018. The subproject obtained its land use pre-examination approval in August 2019 and the permit to occupy woodland in September 2019.

63. After the completion of the final design, due to occupation of basic farmland and ecological red line, the Chunshucha (Mengyuan) -Yangping (Chengyang) Road needed to carry on the land use pre-examination again and obtain the approval of construction land. The Department of Natural Resources of Ningxia Autonomous Region has submitted the construction land application of Pengyang subproject to the Ministry of Natural Resources in June 2020. The construction land application was officially approved by the Ministry of Natural Resources on 13 September 2020. On December 1, 2020, it obtained the approval for construction land utilization from the Ningxia Autonomous Region Government.

64. The subproject had issued a tender advertisement on 16 March 2020 and opened in April 2020. Two civil works contracts had been awarded in November and December 2020, respectively. The land acquisition announcement was issued in February 2021. The civil works had begun in March 2021. As of 31 Dec 2022, civil works of the Subproject had been completed.



Figure 2-3: Sites of Chunshucha (Mengyuan) -Yangping (Chengyang) Road

(ii) Resettlement Implementation Progress

65. As of 31 Dec 2022, Pengyang County had signed all the LA and HD agreements and paid the LAR compensation fees, with a total 353.99 mu of LA and 827.6 m² of HD, affected 439 AHs, with a total of 12.547 million yuan paid. See details in Table 2-22.

Table 2-22: Summary payment of LAR funds (actually completed) in Pengyang Subproject

No.	Category	Resettlement funds (10,000 Yuan)	Percentage of payment
1	Permanent LA	812.3	100%
2	HD	193.06	100%
3	Young crops and ground attachments	249.34	100%
4	Total	1254.7	100%

Source: local sub-PMO.

2.5.4 Main Findings during External M&E

66. (i) Pengyang subproject had signed all LA and HD agreements and paid the LAR compensation fees.

67. (ii) Remaining issues/tasks: i) continuously provide support on livelihood restoration situation AHs; and ii) get ready to carry out resettlement completion review.

2.6 Resettlement M&E of Subproject in Jingyuan County, Guyuan Municipality

2.6.1 Planned and Actual Resettlement Impacts

(i) Land Acquisition

68. See details in Table 2-23.

Table 2-23: Permanent Acquisition of Collective Land of Jingyuan Subproject

Road	Indicators		Original RP	Updated RP	Actually implemented
Shatang (Huanghua Town)-Gaodian Trunk Road	Permanent land (mu)		180.17	179.65	30.17
	Land type (mu)	Plough	12.97	12.97	30.17
		Residential land	1	0.48	0
		Forest land	166.2	166.2	0
	Number of affected households		13	76	42
	Affected population		47	274	274
	Town/township		2	2	1
	Villagers committee		3	3	1

Source: local sub-PMO.

Note: Jingyuan Subproject includes Shatang (Huanghua Town)-Gaodian Trunk Road and Dongxia-Digou Road. Dongxia-Digou Road, including 1 trunk road and 3 feeder roads. According to the final design, the 3 feeder roads were dropped out, and the trunk road was reduced from 11.717 km to 6.16 km. And from May to October 2019, the road upgrading was completed with domestic counterpart funds, without any LAR impacts.

(ii) House Demolition (HD)

69. See details in Table 2-24.

Table 2-24: Impacts of Rural Residential House Demolition of Jingyuan Subproject

Road	Indicators		Original RP	Updated RP	Actually implemented	Remarks
Shatang (Huanghua Town)-Gaodian Road	HD Area (m2)		144	42	0	No HD impacts during implementation
	In which (m2)	Brick	144	0	0	
		Earth-wood	0	42	0	
	AHs		2	2	0	
	APs		9	9	0	
	Affected towns		1	1	0	
	Affected villages		1	1	0	

Source: local sub-PMO.

(iv) Affected Persons (APs)

70. See details in Table 2-25.

Table 2-25: Affected Population of Jingyuan Subproject

Type	Phases	Subtotal	
		AHs	APs
LA impact	Original RP	74	298
	Updated RP	74	265
	Actually implemented	42	274
HD impact	Original RP	38	134
	Updated RP	2	9
	Actually implemented	0	0
Total	Original RP	112	432
	Updated RP	76	274
	Actually implemented	42	274

Source: local sub-PMO.

2.6.2 Compensation Rates and Resettlement Measures

(i) Compensation rates of LA and HD

71. See details in Table 2-26.

Table 2-26: LA and HD Compensation Standards of Jingyuan Subproject

LA	mountainous dryland / Residential land			Forest land		Young crops	
Original RP	5,670 Yuan/mu			3,969 Yuan/mu		600 Yuan/mu	
Updated RP	5,670 Yuan/mu			3,969 Yuan/mu		600 Yuan/mu	
Actually implemented	16,500 Yuan/mu			N/A		based on value appraisal	
HD	brick-concrete	Brick-timber	Brick and earth-timber	Earth-timber	Makeshift house	relocation subsidy (one time)	transition subsidy (6 months)
Original RP	1,000 yuan/M ²	600 Yuan/M ²	410 yuan/M ²	310 yuan/M ²	100 yuan/M ²	1,000 yuan/HH	300 yuan/month. HH
Updated RP	N/A	N/A	N/A	N/A	70 yuan/M ²	N/A	N/A
Actually implemented	No HD impacts during implementation						

Source: local sub-PMO. N/A=not applicable.

(ii) Compensation for Temporary Land Occupation

72. No temporary land occupation impacts occur during implementation.

(iii) Resettlement and livelihood rehabilitation

73. To minimize the resettlement impacts to APs and restore their living standards, rehabilitation measures have been developed and included in this RP. The comprehensive compensation and livelihood restoration packages, including expanding cash crop plantation, improving existing low yield farmland, etc., will help offset the losses from land acquisition. Since this Subproject is in a linear scope, the land and income loss of AHs are very slight. After cash compensation, their income is relatively easy to recover, and they directly benefit from the convenient transportation brought by road construction.

74. After the adjustment of the subproject, there is no longer any HD impact during implementation.

2.6.3 Progress of Project and Resettlement Implementation

(i) Subproject implementation progress

75. Shatang (Huanghua Town)–Gaodian Road: this subproject has started civil works in July 2020.

76. The preliminary design of the road in Jingyuan County was approved on 27 December 2017; and the construction drawing was approved on 10 July 2018. Because of the difficulty of forest land approval processing, Jingyuan County negotiated with the design institute to adjust the route partially, after which the subproject does not involve any forest land, basic farmland and ecological red line. The project obtained land pre-examination opinion in August 2017. The subproject had issued a tender advertisement on 10 February 2020; the tender was opened in April 2020. Civil construction contract was awarded, and construction started in July 2020. As of 31 Dec 2022, civil works of Subproject have been completed.

77. After the design changes, the Dongxia-Digou Road in Jingyuan County no longer involves any LAR impacts and had been upgraded and completed on the original road with domestic counterpart funds in 2019.

(ii) Resettlement Implementation Progress

78. As of 31 Dec 2022, Jingyuan County had signed all the LA agreements and paid the LAR compensation fees, with a total 30.17 mu of LA, affected 42 AHs, with a total of 1.429 million yuan

paid.

79. There is no HD impact during implementation.

Table 2-27: Summary payment of LAR funds (actually completed) in Jingyuan Subproject

No.	Category	Resettlement funds (Yuan)	Percentage of payment
1	Permanent LA	497,805	100%
2	Young crops	931,290	100%
3	Total	1,429,095	100%

Source: local sub-PMO.

2.6.4 Main Findings during External M&E

80. (i) Jingyuan Subproject had completed the signing of LA agreements and the payment of all LA compensation fees.

81. (ii) Remaining issues/tasks: Jingyuan sub-PMO should: i) sort out and provide complete and detailed data/information on LAR activities for resettlement completion review; and ii) continuously provide support on livelihood restoration for AHs.

3 M&E of Resettlement Funds Disbursement

3.1 Resettlement Budget and Resources

3.1.1 Tongxin County, Wuzhong Municipality (Updated RP)

82. Based on the price in 2018, the resettlement costs covered by the updated RP were CNY 13.7650 million, including basic costs of CNY 7.3668 million. Seeing from the influence category, permanent collective land acquisition costs are CNY 5.6917 million, housing demolition costs are CNY 0.8105 million, compensation fees for ground attachments and special facilities are CNY 0.7626 million, and compensation fees for temporal land occupation are CNY 0.1020 million.

83. Other fees include RP formulating fee and monitoring fee of CNY 150,000, supporting fund for vulnerable groups of CNY 69,000, land acquisition fee of CNY 4.7979 million, technical training fee of CNY 130,000, and contingencies of CNY 1.2514 million.

3.1.2 Yuanzhou District, Guyuan Municipality (Updated RP)

84. The fees incurred during the land acquisition and relocation and resettlement shall be listed in the total budget of the project.

85. ①Guyuan-Xiji Road (Guanting-Yuanzhou section) : Based on the price in 2018, the total relocation and resettlement costs were CNY 10,480,097, including basic costs of CNY 4,494,401. Seeing from the influence category, permanent collective land acquisition costs are CNY 3,723,181, housing demolition costs are CNY 207,300, compensation fees for ground attachments are CNY 313,920, special facilities are CNY 250,000.

86. ②Wanzhang–Sanying Road: Based on the price in 2019, the total relocation and resettlement costs were CNY 15,718,801, including basic costs of CNY 6,579,890. Seeing from the influence category, permanent collective land acquisition costs are CNY 5,678,340, housing demolition costs are CNY 441,400, compensation fees for ground attachments are CNY 160,150, special facilities are CNY 250,000.

87. Other fees include RP formulating fee, implementation & management fee, land acquisition fee, technical training fee, external monitoring evaluation fee and contingencies. See details in the table below.

3.1.3 Xiji County, Guyuan Municipality (Updated RP)

88. Based on the prices in 2018, the estimated resettlement costs covered by this RP are CNY 46.068 million, including basic costs of CNY 24.418 million. Seen from the category, permanent collective land acquisition costs are CNY 23.771 million, housing demolition and relocation costs are CNY 0.658million, compensation fees for ground attachments are CNY 1.203million, and compensation fees for special facilities are CNY 150000.

89. Other fees include RP formulating fee, implementation & management fee, land acquisition fee, technical training fee, external monitoring evaluation fee and contingencies.

3.1.4 Pengyang County, Guyuan Municipality (Updated RP)

90. Based on the price in 2018, the estimated resettlement costs covered by this RP are CNY 9.555 million, including basic costs of CNY 5.752 million. Seeing from the influence category, permanent collective land acquisition costs are CNY 3.813 million, housing demolition costs are CNY 417,800, compensation fees for ground attachments are CNY 1203,000, and compensation fees for special facilities are CNY 300,000.

91. Other fees include RP formulating fee, implementation & management fee, land acquisition fee, technical training fee, external monitoring evaluation fee and contingencies.

3.1.5 Jingyuan County, Guyuan Municipality (Updated RP)

92. Based on the prices in 2019, the estimated resettlement costs covered by this RP are CNY 2,175,444, including basic costs of CNY 1,008,581. Seeing from the category, permanent collective land acquisition costs are CNY 743,691, housing demolition and relocation costs are CNY 2,940, compensation fees for ground attachments are CNY 131,750, and compensation fees for special facilities are CNY 120,000.

93. Other fees include RP formulating fee, implementation & management fee, land acquisition fee, technical training fee, external monitoring evaluation fee and contingencies.

3.2 Disbursement Status of Resettlement Funds

94. Tongxin County, Yuanzhou District Xiji County, Pengyang and Jingyuan County had completed the payment of all resettlement funds. See details in Table3-1 to Table3-6.

Table 3-1: Disbursement status of resettlement Funds of Tongxin Subproject

No.	Items	Budget (10,000 Yuan)	Disbursement Status (10,000 Yuan)	Percentage of payment (%)
1	Permanent LA	569.17	599.67	100%
2	Temporary land	10.2	0.31	100%
3	HD	81.05	139.73	100%
4	young crops	0	3.2	100%
5	Ground Ancillary	76.26	53.03	100%
6	Total	736.68	795.95	100%

Source: local sub-PMO.

Table 3-2: Disbursement status of resettlement Funds of Yuanzhou Subproject

No.	Items	Budget (10,000 Yuan)			Disbursement Status (10,000 Yuan)			Percentage of payment (%)
		Guyuan-Xiji Road (Guanting-Yuanzhou section)	Wanzhang-Sanying Road	Total	Guyuan-Xiji Road (Guanting-Yuanzhou section)	Wanzhang-Sanying Road	Total	
1	Permanent LA	372.32	567.83	940.15	1,718.56	294.55	2,013.11	100%
2	HD	20.73	44.14	64.87	461.34	60.74	522.08	100%
3	Young crops and ground attachments	56.39	46.02	102.41	23.53	789.38	812.91	100%
4	Total	449.44	657.99	1,107.43	2,203.43	1,144.67	3,348.1	100%

Source: local sub-PMO.

Table 3-3: Disbursement status of resettlement Funds of Xiji Subproject

No.	Items	Budget (10,000 Yuan)	Disbursement Status (10,000 Yuan)	Percentage of payment (%)
1	Permanent LA	2,377.1	1,904.23	100%
2	HD	65.8	1,277.82	100%
3	Ground Ancillary	120.3	174.87	100%
4	Total	2,441.8	3,356.92	100%

Source: local sub-PMO.

Table 3-4: Disbursement status of resettlement Funds of Pengyang Subproject

No.	Items	Budget (10,000 Yuan)	Disbursement Status (10,000 Yuan)	Percentage of payment (%)
1	Permanent LA	381.3	812.3	100%

2	HD	41.78	193.06	100%
3	Young crops and ground Ancillary	150.3	249.34	100%
4	Total	575.2	1254.7	100%

Source: local sub-PMO.

Table 3-5: Disbursement status of resettlement Funds of Jingyuan Subproject

No.	Items	Budget (10,000 Yuan)	Disbursement Status (10,000 Yuan)	Percentage of payment (%)
1	Permanent LA	74.37	49.78	100%
2	HD	0.3	0	100%
3	young crops	0	93.13	100%
4	Ground Ancillary	13.18	0	100%
5	Total	100.86	142.91	100%

Source: local sub-PMO.

Table 3-6: Summary of disbursement status of resettlement Funds for subprojects

No.	Subproject	Budget (10,000 Yuan)	Disbursement Status (as of 31 Dec 2022) (10,000 Yuan)	Payment completion (Yes or No)
1	Tongxin	736.68	795.95	Y
2	Yuanzhou	1107.43	3,348.1	Y
3	Xiji	2441.8	3,356.92	Y
4	Pengyang	575.2	1,254.7	Y
5	Jingyuan	100.86	142.91	Y

Source: sub-PMOs/IAs.

4 M&E of Capacity Building of Implementing Agencies and Staff

4.1 Establishment of Implementing Agencies

95. In order to organize and lead the project preparation and construction, the Transportation Department of Ningxia Hui Autonomous Region approved the establishment leadership Group and the Project Management Office of the Ningxia Autonomous region Project on October 16, 2017, which is set as the decision-making and administrative organ of the project. The project leadership group, led by the Deputy Director of the Transportation Department of Ningxia Autonomous region, is the decision-making institution of the project who is responsible for the overall deployment of the project and solving major problems, in which there are divisions of Comprehensive Planning and the division of Road Management. The ADB Project Management Office, as the daily and coordinating office of the Project leadership Group, is responsible for applying for the ADB loan and coordinating the preparation and implementation of RPs, and supervising and evaluating the implementation of RPs, including the disbursement of land acquisition compensation and resettlement funds.

96. The county-level transportation bureaus of project counties have also set up leading groups and project management offices to manage, coordinate, supervise, make decisions, ensure project quality, prepare annual plans, supervise the implementation of subprojects in the later stages, and report regularly to the PMO of Transportation Department of Ningxia Autonomous region. Each county PMO is responsible for coordinating the project resettlement works in its administration region, including organizing the daily resettlement works, formulating local policies for resettlement activities, and coordinating with resettlement implementing agencies at all levels. During project preparation and implementation, county PMOs will coordinate with relevant local government departments, and conduct consultations and make decisions on main issues in the process of construction and resettlement implementation. The local township governments shall be responsible for the implementation of the specific resettlement tasks in its administration scope. The agencies involved in land acquisition and resettlement of the project also include the local land bureaus at municipal, district/county levels, land and resources offices and finance and economics offices of local towns/townships, and so on. At the same time, the villages affected by the project are staffed with 1-2 key leaders to assist with resettlement implementation.

4.2 Staffing

97. The organization and coordination of the project leading groups which composed of leaders at all levels is the guarantee of the smooth implementation of resettlement. A strong organization structure ensures the smooth implementation of the specific works of RP implementation. According to the intensity of land acquisition and resettlement activities, resettlement implementing agencies at all levels are adequately staffed, as detailed in Table 4-1. Meanwhile, each resettlement implementing agency has a fixed office space and relevant office equipment.

98. Relevant staff and focal persons of Ningxia PMO and local PMOs/IAs participated in the training on safeguards and gender policies organized by ADB's Beijing Office in August and September 2021, as shown in Figure 4-1.



Figure 4-1: Project staff participated in ADB safeguards and gender policies training organized by ADB' Beijing Office

Table 4-1: Staff of Project and Resettlement Management and Implementing Agencies

No.	Project Sites	Name of Agencies	Staff	Contact Number
1	Transportation Department of Ningxia Hui Autonomous Region	Foreign Loan Office of the Department of Finance	Mr. Wang Hui	0951-5069402
		PMO	Mr. Shi Yuan	0951-6076753
			Ms. Zhong Xiaochun	0951-6076583
2	Tendering Agent	CICC bidding agency company	Mr. Ma Di	13995280730
3	Yuanzhou District	Transportation Bureau	Mr. Guo	13995049435
		Finance Bureau	Mr. Wang Tao	13995049866
4	Xiji County	Transportation Bureau	Mr. Sun Xin	15909543456
		Finance Bureau	Mr. Xue Dinglin	18995433758
5	Tongxin County	Transportation Bureau	Mr. Luo Zhongming	13995130019
		Finance Bureau	Mr. Yang Ning	15509635999
6	Haiyuan County	Transportation Bureau	Mr. Tian Yanhu	18909550977
		Finance Bureau	Mr. Tian Fengbao	15729552348
7	Pengyang County	Transportation Bureau	Mr. Cao Wenyuan	18195401966
		Finance Bureau	Mr. Ren Wannian	13995047926
8	Jingyuan County	Transportation Bureau	Mr. Wu Xiaoping	13995345808
		Finance Bureau	Mr. Yu Jiandong	13709549845
9	Longde County	Finance Bureau	Mr. Zhang Jun	18995446299
		Guanting – Yuanzhou Road	Ms. Yu Xin	13995484535
10	Design Institutes	Wanzhang-Sanying Road	Mr. Lin Haicheng	13995370998
		Jiangtai-Xitan-Pingfeng Road	Mr. Deng Shuliang	13909508208
		Wangtuan – Yuwang Road	Mr. Liu Xing	13519595663
		Zhengqi-Jiucui-Sikouzi Road	Mr. Si Xu	15909505531
		Mengyuan Chunshucha-Yangcheng Yangping Road	Mr. Gen Enchao	18609588688
		Shatfang, Huanghua –Gaodian Road	Mr. Li Weiqun	13995078255

4.3 Evaluation of Implementing Agencies' Capacity

99. The capacity evaluations of the resettlement management and implementing agencies are summarized as follows:

- (i) The project management and resettlement implementing agencies have been designated as relevant local relevant government departments; their responsibilities and tasks of institutions at all levels have been basically clarified, and relevant staff have been trained in the project preparation and implementation phases.
- (ii) From project preparation to implementation, project management and resettlement implementing agencies have gradually learned about and become familiar with the ADB's involuntary resettlement policies and procedures.
- (iii) The project management and resettlement implementing agencies have rich domestic capacity and experience in the implementation of land acquisition and resettlement affairs. However, it is necessary for them to be familiar with the relevant requirements of ADB project's resettlement implementation and management through training, investigation and study, experience exchanges and so on.
- (iv) The project implementation consulting firm and its resettlement specialist has been mobilized to provide technical guidance and assistance on RP updating and implementation.
- (v) Staff of project management and resettlement implementing agencies also need to further enhance the sharing and exchange of information and data related to projects and resettlement, and do a better job on documentation, data sharing and archiving.
- (vi) PMOs should keep the stability of resettlement implementing personnel, if personnel change, the transfer of documents and materials must be done with a timely and proper manner and training on ADB's policies should be provided.

5 Information Disclosure, Public Participation and GRM

5.1 Information Disclosure, Public Consultation and Participation

100. On 16 October 2017, the ADB Financed Ningxia Liupanshan Poverty Reduction Rural Road Development Project has held a signing ceremony of lending agreement, marking the start of the project. The Transportation Department of Ningxia Hui Autonomous Region released the notice of project kick-off on 20 October 2017 and then continuously disclosed information related to the project. In addition, the PMO of the Transportation Department of the Ningxia Hui Autonomous Region has led the planning and design institutes for many times to carry out field investigations in the project areas, publicize the basic information of the project, and to investigate and verify the indicators of the project's resettlement impacts, learn the social and economic situation of the affected population, and collect information on the attitudes and needs of the affected population, etc.



Figure 5-1: Project Commencement announcement released by the Transportation and Finance Departments of Ningxia Hui Autonomous Region

101. In addition, the State Commission for Ethnic Affairs also posted the project information on its official website and stated that it would strongly support this project. Sina News, NetEase News, Ningxia Daily and other major mainstream media portals have carried out special reports on the project, which has received sustained attention and strong support from residents in the affected areas.



Figure 5-2: Special report on the project on the official website of the State Commission for Ethnic Affairs



Figure 5-3: Special reports on the project by Ningxia Daily, Sina News and NetEase News

102. At the same time, the resettlement information of the Project has been disclosed during project preparation and implementation phases. The draft RPs had been disclosed to affected communities and peoples after they were approved by ADB. Local PMOs at all levels have disclosed and distributed of RPs and RIBs to APs; the ADB approved updated RPs also have been disclosed to affected communities and APs. According to the field investigation, before LA and HD, the PMOs and IA at all levels have carried out or will conduct a large number of public participation activities, such as land acquisition and HD mobilization meeting, issuing land acquisition and HD announcement, house value appraisal, inventory of loss survey, publicity of compensation rates and resettlement measures, etc.

103. Along with project design and implementation, further public participation has been carried out in each subproject by local PMOs and/or IAs, mainly including: publicity of compensation standards for LA and HD, introduction of resettlement measures; skills training for the affected people; surveying opinions and expectations of the affected people during the implementation, etc.



Figure 5-4: Socioeconomic Survey and Public Consultation on sites During RP Updating



Figure 5-5: Public Consultation on sites During External Monitoring



Figure 5-6: RIB Disclosed in Yuanzhou District



Figure 5-7: RIB Disclosed in Jiangtai Town, Xiji County



Figure 5-8: RIB Disclosed in Pingfeng Town, Xiji County



Figure 5-9: RIB Disclosed in Xitan Town, Xiji County



Figure 5-10: RIB Disclosed in Xingping Town, Xiji County



Figure 5-11: RIB Disclosed in Jingyuan County



Figure 5-12: Land and House Measurement in Xiji County



Figure 5-13: Land acquisition announcement in Xiji County



Figure 5-14: Land acquisition consultation meeting in Xiji County



Figure 5-15: Land measurement in Yuan District



Figure 5-12: Land acquisition announcement of Guyuan-Xiji Road in Yuan District



Figure 5-14: Land acquisition announcement of Wanzhang-Sanying Road in Yuan District



Figure 5-18: Land acquisition consultation meeting in Yuan District



Figure 5-19: Land acquisition announcement in Pengyang County

5.2 Status of GRM

104. To ensure rehabilitation and improvement of the affected persons' production, livelihood and living conditions, the provincial and county PMO closely consulted with the affected persons to reduce complaints. A mechanism was set up to provide APs with opportunities to complain and to solve problems during implementation.

105. There are clear guidelines in the appeals process, the principles of appeals, the contents and manners to response potential complaints, etc., in order to ensure the GRM operate smoothly.

106. During implementation of the RPs, the resettlement implementation units shall properly address, and record complaints and appeals received and report them to the Ningxia PMO in written form timely.

107. As the publicity and mobilization works of the subprojects have been conducted in project cycle, the government's land acquisition and demolition compensation policies have been well understood and supported by APs, no complaints and appeals have been received from affected persons so far.

6 Main Findings and Recommendations and Next Plan

6.1 Main Findings

108. (i) **Resettlement implementation progress** as of 31 December 2022, sub-PMOs and IAs had signed all the LA and HD agreements and paid all the resettlement funds.

109. (ii) **Project implementing institutions and capacity-building:** the responsibilities and tasks of relevant institutions at all levels are clear, and participated in relevant training organized by ADB, and staff need to continue to increase their inputs and strengthen the management and reporting system for resettlement implementation.

110. (iii) **Grievance Redress Mechanism:** the channels for complaints and appeals are open and smooth, and no complaints have been received to date.

6.2 Main Recommendations

111. (i) Tongxin County, Yuanzhou District, Xiji County and Hanyuan County Sub-PMOs and IAs should proceed the approval of construction land as soon as possible through coordination with relevant local government departments;

112. (ii) All the district/county sub-PMOs and IAs need to continuously provide support on livelihood restoration for AHs; and

113. (iii) All the district/county sub-PMOs and IAs need to get ready for carry out resettlement completion review. continuously strengthen the institutional and personnel capacity for project and resettlement implementation, and improve sorting and archiving of relevant data/information, internal monitoring and reporting system.

6.3 Next Steps

114. Tongxin County, Yuanzhou District, Xiji County and Hanyuan County Sub-PMOs and IAs should proceed the approval of construction land as soon as possible through coordinatiton with relevant local government departments;

115. The resettlement external M&E specialist will coordinate with Sub-PMOs and IAs to continuously collect and sort out detailed data/information on completed LAR activities for resettlement completion review, organize the income follow-up survey and assessment of AHs, and prepare and submit resettlement completion report as scheduled.

Appendix 1: New Land Compensation Policy document of Subprojects

<p style="text-align: center;">固 原 市</p> <p style="text-align: center;">原州区人民政府文件</p> <p style="text-align: center;">原政规发〔2021〕4号</p> <p style="text-align: center;">原州区人民政府关于进一步规范农用地征收工作的通知</p> <p>各乡镇人民政府、街道办事处，区直各有关部门（单位）：</p> <p>为加强集体土地管理，依法保障被征地农民合法权益，根据《中华人民共和国土地管理法》、自治区人民政府《关于公布自治区征收农用地片区综合地价的通知》（宁政规发〔2020〕8号）和自治区自然资源厅《关于进一步加强和规范集体土地征收工作的通知》（宁自然资规发〔2019〕3号）精神，经区政府2021年第8次常务会议研究同意，现就做好我区农用地征收工作通知如下：</p> <p>一、征收流程</p> <p>（一）制定征地工作方案</p> <p style="text-align: right;">— 1 —</p>	<p>偿安置协议，通过“社保卡”及时足额支付土地补偿费、安置补助费以及农村村民住宅、其他地上附着物和青苗等的补偿费用，并落实被征地农民养老保险等社会保障待遇。</p> <p>（十五）土地交付</p> <p>补偿到位后，被征地的农村集体经济组织应及时交付被征土地，被征收土地所有权人、使用权人对土地征收不服，在法定期限内未申请行政复议或者未提起行政诉讼，但在土地征收公告规定的期限内又不腾退土地和房屋的，由区自然资源部门依法申请人民法院强制执行。</p> <p>二、征收农用地补偿标准</p> <p>（一）征收永久基本农田</p> <p>第Ⅰ片区每亩补偿30800元，第Ⅱ片区每亩补偿28600元。</p> <p>（二）征收一般耕地（包括新开水浇地）</p> <p>第Ⅰ片区每亩补偿28000元，第Ⅱ片区每亩补偿26000元。</p> <p>（三）征收园地</p> <p>第Ⅰ片区每亩补偿28000元，第Ⅱ片区每亩补偿26000元。</p> <p>（四）征收退耕还林地</p> <p>第Ⅰ片区每亩补偿28000元，第Ⅱ片区每亩补偿26000元。</p> <p>荒山造林地：乔木林地每亩补偿20000元，灌木林地和其他林地每亩补偿3000元。</p> <p>（五）征收苗圃地</p> <p>第Ⅰ片区每亩补偿28000元，第Ⅱ片区每亩补偿26000元。</p> <p style="text-align: right;">— 6 —</p>
<p>（六）征收人工草地</p> <p>第Ⅰ片区每亩补偿28000元，第Ⅱ片区每亩补偿26000元；征收天然牧草地：每亩补偿3000元。</p> <p>（七）征收鱼塘</p> <p>第Ⅰ片区每亩补偿9000元，第Ⅱ片区每亩补偿8000元。</p> <p>（八）征收未利用地</p> <p>每亩补偿3000元。</p> <p>（九）征收集体建设用地（集体经营性建设用地除外）</p> <p>第Ⅰ片区每亩按28000元补偿，第Ⅱ片区每亩按26000元补偿。</p> <p>三、几点要求</p> <p>（一）完善征地工作的协调机制</p> <p>各乡镇（街道）、要高度重视，加强组织领导，完善工作机制，强化政策落实。各相关部门要各司其职，各负其责，共同做好征收土地方案报批和土地征收实施工作。乡镇人民政府（街道办事处）、村两级组织要按照区人民政府的统一安排，认真做好有关征地组织、政策宣传、群众疏导、纠纷化解等工作，确保征地工作依法有序开展。</p> <p>（二）保障被征地群众的知情权和参与权</p> <p>各乡镇（街道）征收土地时，要组织被征地农村集体经济组织和群众参与土地调查确认、听证和签订征地协议等过程，充分听取被征地群众的意见，确保被征地群众的知情权、参与</p> <p style="text-align: right;">— 7 —</p>	<p>权、申诉权和监督权，对群众提出的合理要求，必须妥善予以解决，不得强行实施征地。要及时足额支付征地补偿费，特别是不得从中安排征地工作经费。</p> <p>（三）加强征收土地监管</p> <p>被征收土地未批准之前，应保持地块现状，不得影响耕种，不得动工建设。被征收土地经依法批准后，要按规定程序实施土地征收工作。区自然资源局要建立征收集体土地监督制度，不定期开展征收土地检查工作，确保按批准要求实施征收。对征地程序不到位、补偿安置不落实的，要及时督促整改，维护被征地群众的合法权益。</p> <p>四、本通知自2021年5月1日起实施，有效期3年。适用于2020年1月份以来新增建设项目征收集体土地。涉及城市规划区内的征收工作由原州区房屋征收办公室会同相关乡镇（街道）负责征收管理工作。</p> <p style="text-align: right;">固原市原州区人民政府 2021年4月30日</p> <p style="text-align: center;">（此件公开发布）</p> <p style="text-align: right;">固原市原州区人民政府办公室 2021年4月30日印发</p> <p style="text-align: right;">— 8 —</p>

New Land Compensation Policy Document of Yuanzhou District

西吉县人民政府文件

西政发〔2021〕24号

西吉县人民政府
关于印发西吉县征收农用地片区
综合地价的通知

各乡镇人民政府，县直各部门（单位）：
《西吉县征收农用地片区综合地价》已经县人民政府第95次常务会议研究通过，现予以印发，请认真遵照执行。

西吉县人民政府
2021年5月19日

（此件公开发布）

西吉县征收农用地片区综合地价

实施征收农用地片区综合地价，是依法保障被征地农民合法权益，促进全县经济社会高质量发展的重要举措。根据《中华人民共和国土地管理法》《宁夏回族自治区土地管理条例》和《自治区人民政府关于公布自治区征收农用地片区综合地价的通知》（宁政规发〔2020〕8号），现将有关事项通知如下：

一、认真做好片区综合地价实施工作

征收农用地片区综合地价由土地补偿费和安置补助费组成，为充分保障被征地农民权益，综合征地实际情况，构成比例1:9，不包括法律规定用于社会保险缴费补贴的被征地农民社会保障费用、征收农用地涉及的地上附着物和青苗等补偿费用。

征收水浇地按所在片区综合地价1.1倍标准执行，征收园地按所在片区综合地价标准执行，征收乔木林地按所在片区综合地价0.7倍标准执行，征收旱地按所在片区综合地价0.6倍标准执行，征收人工牧草地按所在片区综合地价0.5倍标准执行，征收天然牧草地、灌木林地按所在片区综合地价0.1倍标准执行，征收退耕还林地按所在片区综合地价0.6倍标准执行（扣除原享受退耕还林补贴，扣除的资金用于异地安排退耕还林农民补贴），征收鱼塘按所在片区综合地价0.3倍标准执行；征收集体建设用地（集体经营性建设用地除外）参照所在片区综合地价标准执行，征收未利用地按所在片区综合地价0.1倍标准执行；因建设需要

附件 1


西吉县片区划定及征地补偿费用标准

单位：元/亩

征地补偿费用标准	标准	每亩（个）补偿标准			片区范围
		第 I 片区 （综合地价： 27700 元）	第 II 片区 （综合地价： 25800 元）	第 III 片区 （综合地价： 24200 元）	
水浇地	1.1 倍	30470	28380	26620	I 类： 吉强镇：大滩村、短岔村、河滩村、郭咀村、沙湾滩村、上堡村、永泉村、团结村、万庄村、夏寨村、格河村、董河村。 II 类： 吉强镇：大坪村、大雪村、南河村、南家新庄村、龙王坝村、芦子沟村、马营村、炭儿湾村、北岔村、板桥沟村、董子湾村、王昭村、夏家大路村、羊路村、杨坊村。 将台堡镇：包庄村、老寨沟村、保林村、东滩村、刘家沟村、大寨集村、明梁村、明台村、董家村、西坪村。 马莲乡：巴都沟村、北山村、马莲村、南台村、张堡滩村、什字乡：保卫村、什字村、黄沟村、马家沟村、南台村、山庄村、谢寨村、新店村、杨家庄村、余家堡子村、王丰村。 纳河乡：隆堡村、马营村、纳河村、新店村。 新营乡：羊路湾村、陈阳川村、二府营村、黑城河村、新营村。 兴隆镇：陈田玉村、川口村、大雪村、黑北村、董家村、范沟村、黄岔村、罗庄村、马嘴村、唐岔村、团庄村、王沟村。
园地	1.0 倍	27700	25800	24200	
乔木林地	0.7 倍	19390	18060	16940	

旱地	0.6 倍	16620	15480	14520	王河村、下堡子村、下瓦村、兴隆村、杨茂村、杨和村、王桥村、张台子村、张庄村。
人工牧草地	0.5 倍	13850	12900	12100	III 类： 董湖乡：西坪乡、西滩乡、王民乡、田坪乡、沙湾乡、平峰镇、偏城乡、马建乡、红耀乡、白崖乡、火石寨乡。 将台堡镇：董中村、甘岔村、韩堡村、李家嘴头村、明星村、深岔村。 马莲乡：八岔沟村、董子山村、北滩村、东滩村、唐庄村、陈家沟村、罗堡沟村、董子湾村、马莲沟村、郭堡村。 什字乡：北台村、李湾村、李庄村、董庄村、董寨村。 纳河乡：范湾村、杨湾村、南堡村、南庄村、红寨村、郭岔村、民联村、苏沟村。 新营乡：白城子村、大沙河村、大寨滩村、董子沟村、甘河村、甘井村、董子湾村、董儿岔村、上岔村、郭子子村、苏达川村、小寨滩村、腰巴庄村、王家沟村、长义山村、红庄村。 兴隆镇：义院村、董源村、沙寨村、董大庄村、郭玉村、马堡村、上村、西沟村、小段村、郭庄村、董寨村。
天然牧草地、灌木林地	0.1 倍	2770	2580	2420	
退耕还林地	0.6 倍	16620	15480	14520	
鱼塘用地	0.3 倍	8310	7740	7260	
未利用地	0.1 倍	2770	2580	2420	

New Land Compensation Policy Document of Xiji County

<div><div><div>彭阳县</div><div>人民政府文件</div><div>彭政规发〔2021〕2号</div></div><div><div>彭阳县人民政府关于公布</div><div>彭阳县征收农用地区片综合地价的通知</div></div><div><p>各乡（镇）人民政府，各部门，单位：</p><p>根据《中华人民共和国土地管理法》和自治区人民政府《关于公布自治区征收农用地区片综合地价》的通知（宁政规发〔2020〕8号），经县人民政府2021年第2次常务会议研究决定公布彭阳县征收农用地区片综合地价（以下简称区片综合地价），现将有关事项通知如下：</p><p>一、区片综合地价执行标准</p><p>按照自治区人民政府《关于公布自治区征收农用地区片综合地价》的通知（宁政规发〔2020〕8号）有关规定要求，全县征收农用地区片综合地价分两个区片地价标准执行，分别为：</p><p>I区片：白阳镇、古城镇、新集乡、红河镇、城阳乡，区片综合地价27600元/亩。</p><p style="text-align: right;">— 1 —</p></div></div>	<div><p>II区片：王洼镇、草庙乡、交岔乡、小营乡、冯庄乡、孟塬乡、罗洼乡，区片综合地价26000元/亩。</p><p>征收农用地区片综合地价由土地补偿费和安置补助费组成，构成比例1:9；土地补偿费归村集体所有，安置补助费归被征地农民所有，不包括法律规定用于社会保险缴费补贴的被征地农民社会保障费用；征地农民涉及的地上附着物和青苗补偿费用。</p><p>征收永久性基本农田按所在区片综合地价1.1倍执行；征收旱地、园地、人工牧草地、乔木林地、灌木林地、天然牧草地、国有（林、牧）场土地、未利用地、集体建设用地（集体经营性建设用地除外）参照所在区片综合地价标准执行；集体林地、草地不予补偿。大中型水利、水电工程建设征收土地的补偿标准，按国务院有关规定执行。</p><p>二、新旧征地补偿标准衔接</p><p>本次确定的综合地价标准自2020年1月1日起执行，2019年12月31日前（含12月31日），已获得有批准权限的人民政府批准的土地征收，其征地补偿及征地程序按照已批准的征收土地方案实施；2020年1月1日至本次区片综合地价公布期间批准征收的土地，按照本次区片综合地价补齐差价。青苗补偿费新标准未出台前，按照原补偿标准执行。针对区片综合地价实施后可能发生的问题，各项目单位要研究制定工作预案，建立纠纷处理协调机制，妥善解决实施过程中的有关问题。</p><p>三、区片综合地价执行情况监督</p><p>各乡（镇）、部门要加强监督，财政、人力资源社会保障、</p><p style="text-align: right;">— 2 —</p></div>
<div><p>自然资源、农业农村、审计等部门要各司其职，加强监督检查，防止弄虚作假和侵害农民合法权益等问题发生，切实保障被征地农民知情权和参与权。对实施过程中出现的重大问题，及时向县人民政府报告。</p><p>本通知自公布之日起施行，有效期至2025年12月22日；《彭阳县人民政府关于印发<彭阳县集体土地征收补偿标准>的通知》（彭政发〔2012〕4号）同时废止。</p><div><p>2021年2月3日</p></div><p>（此件公开发布）</p></div>	
New Land Compensation Policy Document of Pengyang County	

Appendix 2: LA and HD Agreements and Payment Records of subprojects

房屋征收补偿安置协议

协议编号: 026

征收部门: 固原市原州区官方镇人民政府 (简称甲方)

被征收人: 汪学军 160000900002553 (简称乙方)

汪江至原州区官庄路建设项目为提升公路通行能力,

改善当地居民出行条件, 自治区发改委核准该项目建设, 依据《中华人民共和国土地管理法》法律法规规定, 《自治区人民政府关于公布宁夏回族自治区征地补偿标准的通知》(宁政发[2013]101号), 《固原市人民政府关于印发<固原市城市规划区内国有土地上房屋征收与补偿办法(试行)>的通知》(固政发[2015]67号), 《固原市人民政府关于印发<固原市城市规划区内集体土地上房屋征收与补偿办法(试行)>的通知》(固政发[2015]68号), 《固原市人民政府<关于印发<关于公布固原市市辖区征地补偿标准的通知>的通知》(固政发[2016]77号)等文件精神, 制定本征收补偿安置方案。通过房地产评估机构的评估, 甲乙双方在平等、自愿、协商一致的基础上, 就被征收房屋的征收补偿安置情况达成协议如下:

一、征收补偿费

1、被征收人选择货币补偿方式安置的, 按以下各项补偿:

甲方征收乙方房屋 104.14 m², 评估价值 122481 元;
一次搬迁费 1000 元; 征收土地补偿 () 平方米, 折合 () 元; 奖励 10000 元; 附属物及其他 19500 元。
元。补偿费共计 122900 元。
元 (大写: 贰拾贰万玖仟零元整)。

无入。协议签订后按约定执行。

二、付款时间点

被征收人及乙方签订的征收补偿安置协议约定, 一次性付清征收补偿费。

三、约定的事项

1. 协议签订后 30 日内, 被征收人搬迁, 腾空房屋并将钥匙交付征收组。

2. 对补偿后的建筑物、构筑物及地上附着物等的拆除, 由房屋征收部门统一组织拆除。

四、协议经甲乙双方签字盖章后生效。

五、协议一式四份, 征收人、被征收人各一份, 财务支付部门一份, 其余存档备案。

甲方 (盖章)

乙方 (签字)

负责人:

经办人:

单位电话: 0950-3968506 联系电话: 18995402644

签订日期: 2021 年 6 月 29 日

固原市官方庄路项目征收房屋补偿安置协议表

序号: 026 2021.6.29

被征收房屋: 第 01 号 5 层 主房面积: 104.14 m²

房屋用途: 住宅

房屋结构: 砖混

房屋层数: 5 层

房屋坐落: 固原市官庄路

房屋现状: 完好

房屋补偿: 货币补偿

房屋补偿金额: 122481 元

房屋补偿面积: 104.14 m²

房屋补偿单价: 1175.5 元/m²

房屋补偿总价: 122481 元

房屋补偿面积: 104.14 m²

房屋补偿单价: 1175.5 元/m²

房屋补偿总价: 122481 元

房屋补偿面积: 104.14 m²

房屋补偿单价: 1175.5 元/m²

房屋补偿总价: 122481 元

房屋补偿安置协议表

房屋坐落: 固原市官庄路

房屋用途: 住宅

房屋结构: 砖混

房屋层数: 5 层

房屋现状: 完好

房屋补偿: 货币补偿

房屋补偿金额: 122481 元

房屋补偿面积: 104.14 m²

房屋补偿单价: 1175.5 元/m²

房屋补偿总价: 122481 元

房屋补偿面积: 104.14 m²

房屋补偿单价: 1175.5 元/m²

房屋补偿总价: 122481 元

房屋补偿面积: 104.14 m²

房屋补偿单价: 1175.5 元/m²

房屋补偿总价: 122481 元

房屋状况及补偿金额表

序号	房屋坐落	房屋用途	房屋结构	房屋层数	房屋现状	房屋补偿	房屋补偿面积	房屋补偿单价	房屋补偿总价
1	固原市官庄路	住宅	砖混	5	完好	货币补偿	104.14	1175.5	122481
2	固原市官庄路	住宅	砖混	5	完好	货币补偿	104.14	1175.5	122481
3	固原市官庄路	住宅	砖混	5	完好	货币补偿	104.14	1175.5	122481
4	固原市官庄路	住宅	砖混	5	完好	货币补偿	104.14	1175.5	122481
5	固原市官庄路	住宅	砖混	5	完好	货币补偿	104.14	1175.5	122481
6	固原市官庄路	住宅	砖混	5	完好	货币补偿	104.14	1175.5	122481
7	固原市官庄路	住宅	砖混	5	完好	货币补偿	104.14	1175.5	122481
8	固原市官庄路	住宅	砖混	5	完好	货币补偿	104.14	1175.5	122481
9	固原市官庄路	住宅	砖混	5	完好	货币补偿	104.14	1175.5	122481
10	固原市官庄路	住宅	砖混	5	完好	货币补偿	104.14	1175.5	122481
11	固原市官庄路	住宅	砖混	5	完好	货币补偿	104.14	1175.5	122481
12	固原市官庄路	住宅	砖混	5	完好	货币补偿	104.14	1175.5	122481
13	固原市官庄路	住宅	砖混	5	完好	货币补偿	104.14	1175.5	122481
14	固原市官庄路	住宅	砖混	5	完好	货币补偿	104.14	1175.5	122481
15	固原市官庄路	住宅	砖混	5	完好	货币补偿	104.14	1175.5	122481
16	固原市官庄路	住宅	砖混	5	完好	货币补偿	104.14	1175.5	122481
17	固原市官庄路	住宅	砖混	5	完好	货币补偿	104.14	1175.5	122481
18	固原市官庄路	住宅	砖混	5	完好	货币补偿	104.14	1175.5	122481
19	固原市官庄路	住宅	砖混	5	完好	货币补偿	104.14	1175.5	122481
20	固原市官庄路	住宅	砖混	5	完好	货币补偿	104.14	1175.5	122481
21	固原市官庄路	住宅	砖混	5	完好	货币补偿	104.14	1175.5</	

征收土地协议书

征地方：原州区官厅镇（以下简称甲方） 111-1
被征地方：官厅镇沙湾村二组（以下简称乙方）
根据官厅镇至原州区公路建设项目建设的需要，经原州区人民政府研究决定，征收乙方位于官厅镇沙湾村二组范围内的集体土地。依照《中华人民共和国土地管理法》《宁夏回族自治区土地管理条例》等规定，经甲、乙双方协商，现就土地征收有关事宜达成协议如下：

一、征收土地范围
甲方征收乙方土地位于官厅镇沙湾村二组范围内的集体土地，东至范围：刘玉成以南，刘玉成以北，刘玉成以东，刘玉成以西。

二、征收土地面积、青苗和地上附着物数量、征地补偿标准和补偿金额
被征收土地的权属、地类、面积及青苗、地上附着物等已经双方确认。

（一）征地补偿
按《自治区人民政府关于公布自治区征收农用地区片综合地价的通知》（宁政发〔2020〕8号）和《原州区人民政府关于进一步规范农用地征收工作的通知》（固政发〔2021〕4号）规定的标准执行。具体补偿情况如下：

名称	数量	补偿标准	补偿金额	备注
基本农田	亩	20100 (28600-8500) 元/亩		补偿金额
建设用地	亩	17500 (26000-8500) 元/亩		补偿金额
一般耕地	1.16 亩	17500 (26000-8500) 元/亩	20300	补偿金额
灌木林地	亩	1300 (3000-1700) 元/亩		补偿金额
合计	1.16 亩		20300	

（二）青苗、地上附着物补偿
按照固原市人民政府关于印发《固原市规划区内集体土地上房屋征收与补偿指导价》（固政发〔2015〕68号）和《固原市人民政府关于公布固原市市辖区征地补偿标准的通知》（固政发〔2016〕77号）规定的标准执行。

征收土地协议书

征地方：原州区官厅镇（以下简称甲方） 111-2
被征地方：官厅镇沙湾村二组（以下简称乙方）
根据官厅镇至原州区公路建设项目建设的需要，经原州区人民政府研究决定，征收乙方位于官厅镇沙湾村二组范围内的集体土地。依照《中华人民共和国土地管理法》《宁夏回族自治区土地管理条例》等规定，经甲、乙双方协商，现就土地征收有关事宜达成协议如下：

一、征收土地范围
甲方征收乙方土地位于官厅镇沙湾村二组范围内的集体土地，东至范围：刘玉成以南，刘玉成以北，刘玉成以东，刘玉成以西。

二、征收土地面积、青苗和地上附着物数量、征地补偿标准和补偿金额
被征收土地的权属、地类、面积及青苗、地上附着物等已经双方确认。

（一）征地补偿
按《自治区人民政府关于公布自治区征收农用地区片综合地价的通知》（宁政发〔2020〕8号）和《原州区人民政府关于进一步规范农用地征收工作的通知》（固政发〔2021〕4号）规定的标准执行。具体补偿情况如下：

名称	数量	补偿标准	补偿金额	备注
基本农田	亩	20100 (28600-8500) 元/亩		补偿金额
建设用地	亩	17500 (26000-8500) 元/亩		补偿金额
一般耕地	1.16 亩	17500 (26000-8500) 元/亩	20300	补偿金额
灌木林地	亩	1300 (3000-1700) 元/亩		补偿金额
合计	1.16 亩		20300	

（二）青苗、地上附着物补偿
按照固原市人民政府关于印发《固原市规划区内集体土地上房屋征收与补偿指导价》（固政发〔2015〕68号）和《固原市人民政府关于公布固原市市辖区征地补偿标准的通知》（固政发〔2016〕77号）规定的标准执行。

三、补偿费用
两项补偿费用总计人民币 20300 元整（大写：贰万零叁佰元整）。

三、支付对象、支付方式
本征收土地自依法批准之日起 个月内，由甲方一次性付清涉及农户的征收土地补偿、青苗及地上附着物补偿款全部费用。

四、土地交付使用要求
甲方支付给乙方全部征地补偿费用后 日内，乙方应清理完青苗及地上附着物，净地交给甲方。

五、乙方应当将土地补偿费用的收支状况向本农村集体经济组织成员公布，接受本农村集体经济组织成员和有关部门的监督。

六、本协议经双方代表签字后生效，双方必须共同遵守。

七、本协议一式 份，甲、乙双方各执 份。

甲方：原州区官厅镇人民政府
代表签字：[签字] 1.16 亩 补偿 20300 元

乙方：官厅镇（镇）沙湾村。
代表签字：刘玉成

签订日期：2021年 5月 21日

征收土地协议书

征地方：原州区官厅镇（以下简称甲方） 001-11
被征地方：官厅镇沙湾村二组（以下简称乙方）
根据官厅镇至原州区公路建设项目建设的需要，经原州区人民政府研究决定，征收乙方位于官厅镇沙湾村二组范围内的集体土地。依照《中华人民共和国土地管理法》《宁夏回族自治区土地管理条例》等规定，经甲、乙双方协商，现就土地征收有关事宜达成协议如下：

一、征收土地范围
甲方征收乙方土地位于官厅镇沙湾村二组范围内的集体土地，东至范围：刘玉成以南，刘玉成以北，刘玉成以东，刘玉成以西。

二、征收土地面积、青苗和地上附着物数量、征地补偿标准和补偿金额
被征收土地的权属、地类、面积及青苗、地上附着物等已经双方确认。

（一）征地补偿
按《自治区人民政府关于公布自治区征收农用地区片综合地价的通知》（宁政发〔2020〕8号）和《原州区人民政府关于进一步规范农用地征收工作的通知》（固政发〔2021〕4号）规定的标准执行。具体补偿情况如下：

名称	数量	补偿标准	补偿金额	备注
基本农田	亩	20100 (28600-8500) 元/亩		补偿金额
建设用地	亩	17500 (26000-8500) 元/亩		补偿金额
一般耕地	1.16 亩	17500 (26000-8500) 元/亩	20300	补偿金额
灌木林地	亩	1300 (3000-1700) 元/亩		补偿金额
合计	1.16 亩		20300	

（二）青苗、地上附着物补偿
按照固原市人民政府关于印发《固原市规划区内集体土地上房屋征收与补偿指导价》（固政发〔2015〕68号）和《固原市人民政府关于公布固原市市辖区征地补偿标准的通知》（固政发〔2016〕77号）规定的标准执行。

征收土地协议书

征地方：原州区官厅镇（以下简称甲方） 001-11
被征地方：官厅镇沙湾村二组（以下简称乙方）
根据官厅镇至原州区公路建设项目建设的需要，经原州区人民政府研究决定，征收乙方位于官厅镇沙湾村二组范围内的集体土地。依照《中华人民共和国土地管理法》《宁夏回族自治区土地管理条例》等规定，经甲、乙双方协商，现就土地征收有关事宜达成协议如下：

一、征收土地范围
甲方征收乙方土地位于官厅镇沙湾村二组范围内的集体土地，东至范围：刘玉成以南，刘玉成以北，刘玉成以东，刘玉成以西。

二、征收土地面积、青苗和地上附着物数量、征地补偿标准和补偿金额
被征收土地的权属、地类、面积及青苗、地上附着物等已经双方确认。

（一）征地补偿
按《自治区人民政府关于公布自治区征收农用地区片综合地价的通知》（宁政发〔2020〕8号）和《原州区人民政府关于进一步规范农用地征收工作的通知》（固政发〔2021〕4号）规定的标准执行。具体补偿情况如下：

名称	数量	补偿标准	补偿金额	备注
基本农田	亩	20100 (28600-8500) 元/亩		补偿金额
建设用地	亩	17500 (26000-8500) 元/亩		补偿金额
一般耕地	1.16 亩	17500 (26000-8500) 元/亩	20300	补偿金额
灌木林地	亩	1300 (3000-1700) 元/亩		补偿金额
合计	1.16 亩		20300	

（二）青苗、地上附着物补偿
按照固原市人民政府关于印发《固原市规划区内集体土地上房屋征收与补偿指导价》（固政发〔2015〕68号）和《固原市人民政府关于公布固原市市辖区征地补偿标准的通知》（固政发〔2016〕77号）规定的标准执行。

三、补偿费用
两项补偿费用总计人民币 20300 元整（大写：贰万零叁佰元整）。

三、支付对象、支付方式
本征收土地自依法批准之日起 个月内，由甲方一次性付清涉及农户的征收土地补偿、青苗及地上附着物补偿款全部费用。

四、土地交付使用要求
甲方支付给乙方全部征地补偿费用后 日内，乙方应清理完青苗及地上附着物，净地交给甲方。

五、乙方应当将土地补偿费用的收支状况向本农村集体经济组织成员公布，接受本农村集体经济组织成员和有关部门的监督。

六、本协议经双方代表签字后生效，双方必须共同遵守。


七、本协议一式 份，甲、乙双方各执 份。

甲方：原州区官厅镇人民政府
代表签字：[签字] 1.16 亩 补偿 20300 元


乙方：官厅镇（镇）沙湾村。
代表签字：[签字]

签订日期：2021年 5月 19日


LA agreements of Guyuan-Xiji Road (Guanting-Yuanzhou section)(new standard)

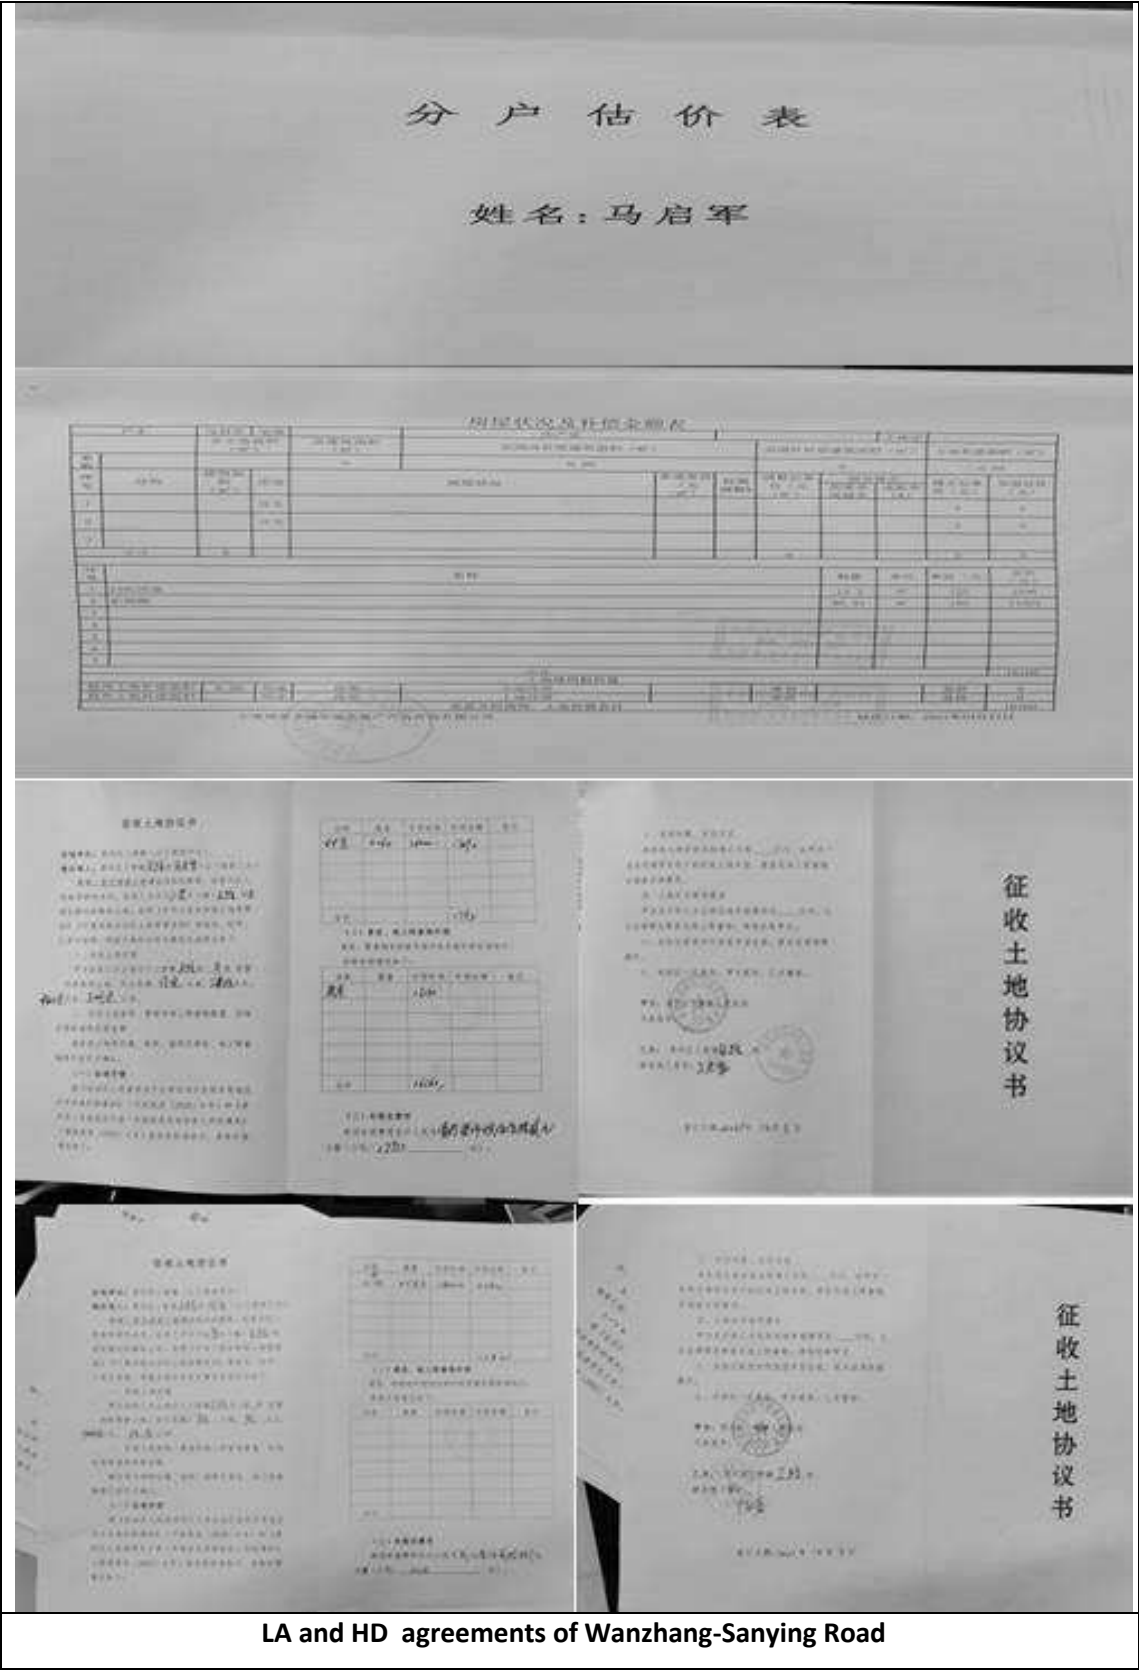

LA and HD agreements of Wanzhang-Sanying Road



LAR compensation payment voucher of Wanzhang-Sanying Road



LA compensation agreements of Xiji County

[illegible][illegible][illegible]




The image shows a large, multi-page document, likely a technical manual or a large table, spread out on a surface. The document is written in Chinese. The top of the document has a header with the title "城市轨道交通工程" (Urban Rail Transit Engineering) and other information. The main body of the document consists of multiple columns of text and tables, with some tables containing numerical data. The document appears to be a detailed technical specification or a large data table for a project.

LA compensation payment records of Xiji County

国库集中支付凭证

第: Z24_2021_0019723 号

日期: 2021年08月09日




付款人	全称 西吉县财政局 账号 5002073200041 开户行 宁夏西吉农村商业银行股份有限公司营业部	收款人	全称 西吉县王民乡人民政府 账号 29423001040000082 开户行 中国农业银行西吉支行兴隆营业所	
支付金额 人民币(大写)	柒仟伍佰柒拾柒元整		金额(小写)	¥7,577.00
单位	012001西吉县交通运输局本级	主管部门		
功能科目	2140104公路建设	结算方式	电子转账支付	
用途 2140104公路建设工程项目征收土地地差补偿资金				
 支付印章			 复核	业务专用章 对方科目 记账员:

注: 1. 此凭证与代理银行其他银行间支付凭证合并使用, 凭证号在年度内从00001号开始连续编号。
 2. “用途”按实际支出用途填写。

国库集中支付凭证

第: Z24_2021_0019647 号

日期: 2021年08月09日




付款人	全称 西吉县财政局 账号 5002073200041 开户行 宁夏西吉农村商业银行股份有限公司营业部	收款人	全称 西吉县台堡镇人民政府 账号 29507001040000015 开户行 农业银行西吉支行台堡分理处	
支付金额 人民币(大写)	捌拾万零叁仟零柒拾元整		金额(小写)	¥800,070.00
单位	012001西吉县交通运输局本级	主管部门		
功能科目	2140104公路建设	结算方式	电子转账支付	
用途 2140104公路建设工程项目征收土地地差补偿款				
 支付印章			 复核	业务专用章 对方科目 记账员:

注: 1. 此凭证与代理银行其他银行间支付凭证合并使用, 凭证号在年度内从00001号开始连续编号。
 2. “用途”按实际支出用途填写。

国库集中支付凭证

第: Z24_2021_0019646 号

日期: 2021年08月09日




付款人	全称 西吉县财政局 账号 5002073200041 开户行 宁夏西吉农村商业银行股份有限公司营业部	收款人	全称 西吉县平峰镇人民政府 账号 29507001040000015 开户行 西吉县农行平峰支行	
支付金额 人民币(大写)	壹佰肆拾叁万陆仟伍佰柒拾柒元整		金额(小写)	¥1,436,500.00
单位	012001西吉县交通运输局本级	主管部门		
功能科目	2140104公路建设	结算方式	电子转账支付	
用途 2140104公路建设工程项目征收土地地差补偿款				
 支付印章			 复核	业务专用章 对方科目 记账员:

注: 1. 此凭证与代理银行其他银行间支付凭证合并使用, 凭证号在年度内从00001号开始连续编号。
 2. “用途”按实际支出用途填写。

国库集中支付凭证

第: Z24_2021_0019262 号

日期: 2021年08月05日




付款人	全称 西吉县财政局 账号 5002073200041 开户行 宁夏西吉农村商业银行股份有限公司营业部	收款人	全称 西吉县西滩乡人民政府 账号 29423001040000422 开户行 中国农业银行股份有限公司西吉城郊支行	
支付金额 人民币(大写)	伍拾陆万叁仟柒佰陆拾捌元整		金额(小写)	¥563,768.00
单位	012001西吉县交通运输局本级	主管部门		
功能科目	2140104公路建设	结算方式	电子转账支付	
用途 2140104公路建设工程项目征收土地地差补偿资金				
 支付印章			 复核	业务专用章 对方科目 记账员:

注: 1. 此凭证与代理银行其他银行间支付凭证合并使用, 凭证号在年度内从00001号开始连续编号。
 2. “用途”按实际支出用途填写。

国库集中支付凭证

第: Z24_2021_0019261 号

日期: 2021年08月05日

付款人	全称 西吉县财政局 账号 5002073200041 开户行 宁夏西吉农村商业银行股份有限公司营业部	收款人	全称 西吉县兴平乡人民政府 账号 5002674500029 开户行 西吉农村商业银行城郊支行	
支付金额 人民币(大写)	玖拾玖万伍仟壹佰陆拾捌元整		金额(小写)	¥995,168.00
单位	012001西吉县交通运输局本级	主管部门		
功能科目	2140104公路建设	结算方式	电子转账支付	
用途 2140104公路建设工程项目征收土地地差补偿资金				
 支付印章			 复核	业务专用章 对方科目 记账员:

注: 1. 此凭证与代理银行其他银行间支付凭证合并使用, 凭证号在年度内从00001号开始连续编号。
 2. “用途”按实际支出用途填写。

LA compensation payment voucher of Xiji County

国库集中支付凭证
第: Z25 2021 0013406 号
日期: 2021年08月13日
单位: 元
收款人: 彭阳县交通运输局代发资金专户
支付金额: 壹佰壹拾叁万陆仟零肆拾元整
单位: 016001彭阳县交通运输局
功能科目: 2140104公路建设
结算方式: 电子转账支付

注: 1. 此凭证与代理银行其他银行间支付凭证合并使用, 凭证号在年度内从00001号开始连续编号。
2. “用途”按实际支出用途填写。

国库集中支付凭证
第: Z25 2021 0013421 号
日期: 2021年08月11日
单位: 元
收款人: 彭阳县交通运输局代发资金专户
支付金额: 捌佰零捌万伍仟陆佰叁拾柒元玖角整
单位: 016001彭阳县交通运输局
功能科目: 2140104公路建设
结算方式: 电子转账支付

注: 1. 此凭证与代理银行其他银行间支付凭证合并使用, 凭证号在年度内从00001号开始连续编号。
2. “用途”按实际支出用途填写。

LA and HD compensation payment voucher of Pengyang County

彭阳县孟柳椿树岔至城阳杨坪公路征地拆迁兑现花名册

序号	所在村组	身份证号	开户银行	银行账号	拆迁补偿	安置补偿	支付金额	备注
合计	大阳: 壹佰壹拾叁万陆仟零肆拾元整				81	8134325.0		
1	何志超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	0	8134325.0	8134325.0	
2	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	0	8134325.0	8134325.0	
3	杨建武 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	0	8134325.0	8134325.0	
4	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	0	8134325.0	8134325.0	
5	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	0	8134325.0	8134325.0	
6	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	0	8134325.0	8134325.0	
7	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	0	8134325.0	8134325.0	
8	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	0	8134325.0	8134325.0	
9	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	0	8134325.0	8134325.0	
10	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	0	8134325.0	8134325.0	
11	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	0	8134325.0	8134325.0	
12	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	0	8134325.0	8134325.0	
13	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	0	8134325.0	8134325.0	
14	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	0	8134325.0	8134325.0	
15	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	0	8134325.0	8134325.0	
16	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	0	8134325.0	8134325.0	
17	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	0	8134325.0	8134325.0	
18	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	0	8134325.0	8134325.0	
19	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	0	8134325.0	8134325.0	
20	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	0	8134325.0	8134325.0	

椿树岔至城阳杨坪项目建设用地及房屋等附着物征收补偿兑现花名册 (第一批)

序号	所在村组	身份证号	开户银行	银行账号	土地补偿	附着物和青苗补偿	拆迁补偿	安置补偿	支付金额	备注
合计	大阳: 捌佰零捌万伍仟陆佰叁拾柒元玖角整				1037733.18	10821150.0	651606.0	61110.0	8085609.18	
1	赵国法 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	17500.0	18000.0	0.0	0.0	19500.0	
2	李发海 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	8143.0	1440.0	0.0	0.0	9583.0	
3	杨建武 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	10000.0	0.0	0.0	0.0	10000.0	
4	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	22400.0	4300.0	0.0	0.0	26700.0	
5	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	46500.0	0.0	0.0	0.0	46500.0	
6	杨建武 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	11410.0	650.0	0.0	0.0	12060.0	
7	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	6200.0	0.0	0.0	0.0	6200.0	
8	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	3422.0	0.0	0.0	0.0	3422.0	
9	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	0.0	0.0	0.0	0.0	0.0	
10	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	12100.0	0.0	0.0	0.0	12100.0	
11	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	3784.0	0.0	0.0	0.0	3784.0	
12	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	3776.0	0.0	0.0	0.0	3776.0	
13	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	51400.0	0.0	0.0	0.0	51400.0	
14	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	47034.0	0.0	0.0	0.0	47034.0	
15	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	25500.0	0.0	0.0	0.0	25500.0	
16	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	48672.0	0.0	0.0	0.0	48672.0	
17	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	3300.0	0.0	0.0	0.0	3300.0	
18	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	4370.0	0.0	0.0	0.0	4370.0	
19	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	6050.0	0.0	0.0	0.0	6050.0	
20	李作超 孟柳椿树岔村	6122261196001000211	黄河农村商业银行	6122261196001000211	34300.0	0.0	0.0	0.0	34300.0	

LA and HD compensation records of Pengyang County

Appendix 3: Resettlement Status of AHs in Yuanzhou District

Appendix 3-1: Destination Impacts and Resettlement Status of AHs in Yuanzhou District

No.	Town	village	Name of head of household (HD)	Impact degrees (1, Partial demolition; 2, complete demolition)	Resettlement Status (1) Living in the remaining houses on original site; (2) Living in other houses; (3) purchase new house in other site; (4) construct new houses on other site)	Resettlement status (1, moved in; 2, pending)
Guyuan-Xiji Road (Guanting-Yuanzhou section)						
1	Guanting	Chengershan	Ma A	2	3	1
2	Guanting	Chengershan	Li B	2	3	1
3	Guanting	Miaotai	Ma C	2	2	1
4	Guanting	Chengershan	Zhou D	2	2	1
5	Guanting	Chengershan	Jiang E	1	2	1
6	Guanting	shizhuang	Du F	2	2	1
7	Guanting	Liudian	Wang G	1	2	1
8	Guanting	Chengershan	Li H	2	2	1
9	Guanting	Chengershan	Li I	2	2	1
10	Guanting	Chengershan	Tang J	1	2	1
11	Guanting	Guanting	Hai K	1	2	1
12	Guanting	Guanting	Ma L	2	2	1
13	Guanting	Liudian	Hai M	1	2	1
14	Guanting	Liudian	Hai N	2	4	1
15	Guanting	Liudian	Ma O	1	2	1
16	Guanting	Liudian	Luo P	2	2	1
17	Guanting	Liudian	Jin Q	2	3	1
18	Guanting	Chengershan	Wang R	2	2	1
19	Guanting	Chengershan	Lu S	2	2	1
20	Guanting	Chengershan	Li T	2	1	1
21	Guanting	Liudian	Jin U	2	2	1
22	Guanting	刘店村	Wu V	2	1	1
23	Guanting	Guanting	Lu W	2	1	1
24	Guanting	Guanting	Hai X	2	1	1
25	Guanting	Guanting	Hai Y	2	2	1
26	Guanting	Guanting	Hai Z	2	1	1
27	Guanting	Chengershan	Du A1	1	2	1
Wanzhang-Sanying Road						
1	Sanying	Malu	Ma B1	1	1	1
2	Sanying	Malu	Yang C2	1	1	1
3	Sanying	Malu	Yang D3	1	1	1
4	Sanying	Malu	Ma E4	1	4	1
5	Sanying	Malu	Yang F5	1	1	1
6	Sanying	Malu	Dongyuan G1	1	1	1
7	Zhaike	Datai	Yan H1	1	1	1



Resettlement Status of AHs in Yuanzhou District
