

# Environmental Monitoring Report

---

Semestral Report  
August 2016

## BAN: Financing Brick Kiln Efficiency Improvement Project – Tradexcel Auto Bricks Limited

Prepared by Environment Specialist for the People's Republic of Bangladesh and the Asian Development Bank.

## **CURRENCY EQUIVALENTS**

(as of 30 June 2016)

Currency unit	–	taka (Tk)
Tk 1.00	=	\$0.0127632419
\$1.00	=	Tk 78.350000

## **NOTES**

- (i) The fiscal year (FY) of the Government of Bangladesh ends on 30 June. FY before a calendar year denotes the year in which the fiscal year ends, e.g., FY2011 ends on 30 June 2011.
- (ii) In this report, "\$" refers to US dollars.

This environmental monitoring report is a document of the borrower. The views expressed herein do not necessarily represent those of ADB's Board of Directors, Management, or staff, and may be preliminary in nature.

In preparing any country program or strategy, financing any project, or by making any designation of or reference to a particular territory or geographic area in this document, the Asian Development Bank does not intend to make any judgments as to the legal or other status of any territory or area.

## Post Implementation Environmental Monitoring Report

### Tradexcel Auto Bricks Limited

Angutia, Mirzapur, Gazipur



Prepared by Mohammad Reazuddin  
ADB Environment Consultant  
Under TA 8197

Dhaka

August, 2016

## **Table of Content**

<b>Chapter Name</b>	<b>Page No</b>
<b>1. Project Background</b>	01
1.1 Purpose & objective	02
<b>2. General Information of the Sub-Project</b>	02
2.1 Subproject process description	03
2.2 Subproject legal requirement	04
<b>3. Methodology &amp; Approach for Post Implementation Monitoring</b>	05
3.1 Review of all legal & technical documents	05
3.2 Site visit/ inspection & consultation	05
<b>4. Current development status of the subproject</b>	06
<b>5. Presentation of Post Implementation Monitoring findings (Status of implementation of environmental compliances)</b>	07
<b>6. Corrective Action Plan</b>	09
<b>7. Conclusion</b>	11
 <b>Attachments</b>	
1. Pictures taken during site visit	12

**Acronym**

ADB	-	Asian Development Bank
DOE	-	Department of Environment
EC	-	Environmental Clearances (EC)
EDD	-	Environmental Due Diligence
EMP	-	Environmental Management Plan
FCK	-	Fixed Chimney Kiln
GDP	-	Gross Domestic Product
GOB	-	Government of Bangladesh
HHK	-	Hybrid Hoffman Kiln
HSBK	-	Horizontal Shaft Brick Kiln
IFCK	-	Improved Fixed Chimney Kiln
IZZK	-	Improved Zig Zag Kiln
OSH	-	Occupational Safety & Health
PFI	-	Participating Financial Intermediary
PPE	-	Personal Protective Equipment
TK	-	Tunnel Kiln
VSBK	-	Vertical Shaft Brick Kiln

## **1: Project Background**

Brick kilns are major sources of greenhouse gas in Bangladesh, emitting annually 6 to 9 million tons of CO<sub>2</sub>. Such high levels of emissions are a result of the use of age-old technologies and substandard fuels such as high sulphur coal, tires and wood used in the kilns.

To meet the increasing demand, brick fields are mushrooming all over the country with heavy concentration at the outskirts of urban area. This situation is being exacerbated by the growth of new brickfields every year., more and more paddy fields are being converted to brick fields thus putting tremendous pressure on the farm land depletion can have alarming prospect for food security. Topsoil from agricultural lands, river floodplains are used for making the green bricks which is burnt later at the kilns. More over wood fuel is used as a secondary fuel for Brick making of the country. Most notable is the impact of Brick making on land degradation and deforestation. The haphazard growth of the brick fields is completely unsustainable

Despite its highly polluting and energy-intensive feature, the FCK continues to be the dominant technology. Other technologies such as the IFCK, IZZK, HSBK, VSBK, HHK and TK are substantially cleaner, consuming less energy and emitting lower levels of pollutants and greenhouse gases but their use is limited. These technologies are still being piloted though and are, therefore, at an early adoption stage; their technological efficiency and financial viability still need larger scale demonstration. The FCK technology, a sub-optimal one, and the hand moulding practice of making green bricks are both unsustainable and do not lend themselves to producing consistently good quality and well-shaped bricks. They also cause significant negative externalities. The industry is, in short, in need of a transformative change, change that will improve operational efficiency and make it less polluting, less wasteful and more resource efficient. This transformation process can be used to improve production efficiency, product quality and green downstream uses providing socially and environmentally sustainable “green jobs” that can fuel economic growth.

ADB proposed a financial package project consisting of two loans to brace the on-going technology dissemination efforts. The financial package contained in the Bangladesh Brick

Sector Improvement Project is designed to support commercial financing of new technology kilns by providing loans to entrepreneurs through participating commercial banks (PFIs).

The loans to the government are intended to establish a credit facility of \$50 million equivalent in local currency at Bangladesh Bank (Central bank) for relending to participating financial intermediaries for the construction of more energy-efficient and environmentally superior brick kilns, The funds are to be used the purpose of financing upgrades and constructing more energy-efficient and environmentally superior kilns, The two components of the credit facility are

- (i) Financing the upgrading of existing FCK kilns to a transitional design to preserve sector welfare while immediately reducing pollution, and
- (ii) To finance and promote the most advanced brick kiln technologies in brick making and to demonstrate.

**Tradexcel Auto Bricks Ltd** is one of the sub-projects that received the finance from ADB in the Advanced Brick Technology Category.

### **1.1 Purpose & Objective**

The purpose of the report is to record the post implementation environment compliance status of Tradexcel Auto Bricks Ltd subproject and to suggest a corrective action plan against non-compliant issues.

### **2. General Information of the Sub-Project**

Tradexcel Auto Bricks Limited, situated at Mouza: Angutia, Upazila: Gazipur Sadar, District: Gazipur, Bangladesh.

The general information of Tradexcel Auto Bricks Limited are furnished in the following table:

**Table 2.1: General Information on Tradexcel Auto Bricks Ltd.**

1. Name of the Company	<b>Tradexcel Auto Bricks Limited</b>
2. Name of the entrepreneur	Rezwan Rahman
3. Contact Address	Green Square (4th Floor), House # 1/B, Road # 8, Gulshan -1, Dhaka-1212, Bangladesh
4. Name of the Brick Kiln	Tradexcel Auto Bricks Limited
4.1 Trial Production Date	March 2016

4.2 Start of Commercial Production	20 <sup>th</sup> May 2016
5. Type of the Brick Kiln	Tunnel Kiln (TK)
5.1 Rated Capacity Production (Daily)	80,000
5.2 Current Production (Daily)	80,000 (per shift 40,000)
6. Project Investment	70 Crore
7. Location Address of the Brick Kiln	Angutia, Mirzapur, Gazipur
8. Current office address	Green Square (4 <sup>th</sup> Floor), House # 1/B, Road # 8, Gulshan -1, Dhaka-1212, Bangladesh
9. Telephone/Fax	Tel:+88028833180 Fax: +88028833104
10. E-mail	rr@tgl.com.bd

## 2.1 Subproject Process Description

The project design combines a highly efficient kiln technology, the Tunnel Kiln (TK) with a unique technique of forming green bricks: powdered coal is injected for internal combustion. This approach results in lower energy usage, higher quality bricks and reduced air pollution. Bricks of any size, shape (including perforated and hollow brick) and pigmentation can be produced at the plant with minor modifications. All bricks will be of uniform quality and will meet international standards for strength, quality and appearance.

The plant will produce 80,000 bricks of size 240 mm x 120 mm x 70 mm daily. The main features are as follows: 95% intestine combustion, raw material preparation with roller mill, shaping with vacuum extruder, tunnel drying and firing with annular kiln. Annual working days have been assumed to be of 300 days. Raw material preparation will be conducted each day in 2 shifts of 7.5 hours. Drying and firing in 3 shifts each of 8 hours. The raw materials (soil) mostly shall be collected from digged ponds and river beds.

Tunnel Kilns are most common in developed countries, since their intervention tunnel kilns have now become highly automated and are for large brick production, but unlike the Hybrid Hoffman Kiln, the fuel used is coal. The kiln can be made from firebricks or from green bricks. In the latter event, the green bricks get “cooked” during kiln operation. The inner kiln lining is made from refractory bricks and then plastered over by refractory cement. Clay is premixed with powdered coal and then extruded to produce the green bricks. This is a unique process and fundamental to the energy efficiency. Almost 98% of the total energy required is injected into the bricks and only about



2% is fed externally into the firing chamber to assist firing in the kiln. Most of the fuel mixed into the bricks, over 95%, of which is completely burnt during firing.

For the production process, the clay is excavated by hydraulic excavator or by hand from nearby river beds, pond digging and transported to the plant stacking yard by trucks. The clay is then crushed by means of roller mills, then by double-shaft mixer where water is added in such a manner as to ensure moisture content of 15%

The tempered material is fed into a vacuum extruder for continuous column production. The column is then cut with Cutter column and Cutter green to the required size. The green brick is set on drying cart by manual loading for drying.

The green bricks are then manually loaded on to the drying cart which is then transported into the drying tunnel by means of a hydraulic pusher. Hot air for drying is funneled into the tunnel from the tunnel kiln. The drying cycle is about 26 hours.

The dried green bricks are unloaded manually into the Tunnel kiln. The speed of the firing is 1.25m/h at a Sintering temperature of about 950°C -1050 °C. The fired brick are unloaded and conveyed manually in carts to the stacking yard.

## **2.2 Subproject Legal Requirement**

### **I. National Regulatory Framework**

Bangladesh environment Conservation Act'95 is the key Act in the environmental arena. Under this Act, it requires that no industry or project can be set up in the country without the clearance from Department of Environment (DoE). Bangladesh Environment Conservation Rules'97 provides the procedures how to obtain the environment clearance from DoE. According to this Rule, brick manufacturing projects fall under the "**Orange B Category**". According to ECR 1997, the project sponsor prepared a comprehensive Initial Environmental Examination (IEE) report including an Environmental Management Plan (EMP) and submitted those to DoE for obtaining Site Clearance and Environmental Clearance. **Brick Kiln Act 2013** is the latest legislation that the brick kiln owners has to comply. It regulates the technology and type of the kiln, location characteristics, source of soils/ earth, fuels etc.

### **II. ADBs Safeguards Policy and Requirements**

ADB's Safeguard Policy Statement (2009) is a consolidated policy framework setting out policy objectives, principles and requirements for three safeguard areas: environmental, involuntary resettlement, and indigenous people.

The ADB requires environmental assessment of all project loans, program loans, sector loans, sector development program loans, financial intermediation loans, and private sector investment operations as per Environmental Operational Directives (2013-2020).

Environmental assessment is a process rather than a one-time report, and includes necessary environmental analyses and environmental management planning that take place throughout the project cycle.

### **III. Bangladesh Bank's Commitment**

Bangladesh Bank's cherished goal is to achieve sustainable development in the overall economy. In the energy sector, it promotes cleaner and more environmentally friendly technologies, and thus is committed to avoid and mitigate adverse environmental impacts, if any, resulting from the projects it finances.

Bangladesh Bank has agreed upon with Environmental and Social Management System (ESMS) of ADB and committed that all sub projects financed by BB through ADB Letter of Credit (LoC) would be compliant to ADB Safeguard Policy Statement (SPS) 2009.

Currently, Bangladesh Bank is considering to finance the proposed subproject through the ADB LoC, therefore an Environmental Safeguard Due Diligence (ESDD) of the proposed subproject has been warranted.

### **3. Methodology & Approach for Post Implementation Monitoring**

Post Implementation Environmental Monitoring was carried out in accordance with the guidance provided in the ESMS of ADB. These include: 1) review of all legal and technical documents and 11) site visit/ inspection of the sub project and stakeholder consultation.

#### **3.1 Review of all legal & technical documents**

- Review of Initial Environment Examination (IEE) report in favour of the sub project and Environment Management Plan (EMP) & Monitoring Plan (MP) suggested in Environmental due Diligence Report (EDDR)
- Review of recommendations made in the Environmental Due Diligence (EDD) report.
- Review of suggested Monitoring Plan laid down in the EDD.

- Review of updated Regulatory Documents including Renewal Clearance Certificates from DOE.
- Review of monitoring results (if any).

### **3.2 Site visit inspection & consultation**

#### Visit to the plant

As a part of “loan 2865/2866 Ban: Financing Brick Kiln Efficiency implementation Project and TA 8197-BAN Supporting Brick Sector Development Program – Fielding Loan Review Mission (12-30 June 2016,” the visit took place on 22.6.2016. The visit was organized in coordination with Bangladesh bank and PFI.

The Environment Consultant paid attention to the following environmental issues, in particular during the day long visit.

- Take a round in the operation of the plant and see whether the recommendations made in the EDD report were implemented or not.
- Inspect all the machineries and equipment and their log-books.
- Inspect the quality of the bricks.
- Inspect the clay store depot and coal store depot as well as carrying conditions of clay and coal.
- Observe the noise from generator, dust generation from different processes, smoke emission from the chimney and the status of PPE usage.
- Observe overall environment management including solid & liquid wastes, sanitation facilities etc
- Observe landscaping & greening efforts

#### **Consultation with Stakeholders**

- Discussion with the sector specific team with Bangladesh Bank involved in the appraisal and loan processing of the sub project.

- Consultation with the owner/plant manager and staff and workers about the need and scope of safeguard
- Discussion with the neighbouring people.

#### **4. Current development status of the subproject**

Entire construction work including installation of kiln & dryer have been completed. It's now a full operational plant with an efficient management team. Commercial production has started since May-2016). It has a total strength of staff & workers about 175. Management of the subproject is providing accommodation facilities (built & rented) to most of its key staff & workers. It has reached to its rated capacity (according to the management) within this short period and the quality of the bricks appears excellent.

#### **5. Presentation of Post implementation monitoring findings (Status of implementation of Environmental Compliances)**

In the post implementation audit report, some gaps were identified on few environmental aspects. In below table 5.1, the status of implementation has been depicted:

Table 5.1: Status of implementation of Environmental Compliances

Aspect	Issues	Comment/Suggestion made in the EDDR	Compliance Status	Reasons of inadequacy
<b>A. Regulatory Compliance</b>	a) NOC from Local administration b) Site Clearance from DoE c) Environmental Clearance Certificate (ECC) from Department of Environment (DoE) d) Brick Burning License from the Office of the Deputy Commissioner	The sub-project meets the requirements of appropriate Bangladesh legislations in consideration of obligations and guidelines from Regulatory Authorities	Fully Complied	NA

Aspect	Issues	Comment/Suggestion made in the EDDR	Compliance Status	Reasons of inadequacy
<b>B. Environment Management</b>	a) Solid waste	i. solid waste to be segregated properly ii. waste clay, misshaped or broken under burnt or over burnt bricks to be sold to the traders	Fully Complied	NA
	b) Noise & vibration	Adequate abatement measures for generator noise	Fully Complied	NA
	c) Air pollution	a) High grade coal to be used b) Well planned water spraying system in dust pollution places	a. Fully Complied b. Partially complied	Adequate water spray is not done
<b>C. On Site Environment Management</b>	a) Coal transportation & grinding	Coal transportation to be made in covered truck. Unloading and coal grinding are to be carried out in closed shed	Fully complied	
	b) Clay transportation & storing	Clay transportation to be done in covered trucks and storing to be done in under shade	Not Complied	Clay transportation is done in open trucks and Storing is done in open shade
	c) Landscaping & greening	Create buffer zone and planting trees.	Fully complied	
<b>D. Occupational Health &amp; Safety</b>	a) Supply & use of PPE	Protective clothing, goggles, helmets, shoes and accessories to be adequately provided to the workers.	Partially complied	There are supplies of PPE. But, it is rarely used. No enforcement from the authority
	b) Sanitation diseases hazard	Provision of drinking water, separate toilets for male and female workers	Fully complied	NA

Aspect	Issues	Comment/Suggestion made in the EDDR	Compliance Status	Reasons of inadequacy
	c) Dusts inhalation hazard	Strict enforcement on the use of PPE's including awareness raising	Not Complied	Lack of enforcement from the authority
	d) Accident risks in work place	Periodic drill and use of protective gears & clothing	Not Complied	The drills don't happen and workers are not equipped with PPE, there are likely chances of accident
	e) Noise & vibration hazard	Adequate abatement measures for generator noise	Fully complied	NA
<b>E. Air Quality Monitoring</b>	Measurement of emissions of particulate matters & flue gases ( SPM, PM <sub>10</sub> , PM <sub>2.5</sub> , CO, NO <sub>x</sub> )	Develop a plan and arrangements for regular monitoring of air quality and occupational health issues	Not Complied	There is no facility available to them for the purpose
<b>F. Maintenance of Equipment</b>	Regular maintenance and repair of kiln, dryer & equipment	Implementation of a schedule for regular maintenance and repair of kiln, dryer & equipment	Fully complied	NA
<b>G. Institutional Arrangements</b>	a) Deployment of adequate human resources	Recruitment of adequate human resources for brick kiln operation and EHS management	Fully complied	
	b)Deployment of financial resources for environment management and occupational health & safety (OHS)	Adequate financial resources for environment management and occupational health & safety (OHS)	Fully complied	
<b>H. Employment</b>	a) Local	Local employment	Fully	NA

Aspect	Issues	Comment/Suggestion made in the EDDR	Compliance Status	Reasons of inadequacy
<b>and Business Opportunities</b>		and business to be promoted	complied	
	b) National	To produce standard quality bricks	Fully complied	NA
<b>I. Impact on Neighbourhood</b>	a) Severance	Appropriate traffic management for the incoming and outgoing trucks	Fully complied	No complains from the neighbourhood
	b) Air pollution	Emission tests to be carried out	Not complied	No interest to carry out tests

## **6. Corrective Action Plan**

Corrective action plan for all the PARTIALLY COMPLIED and NOT COMPLIED issues (listed in the above table 5.1) are suggested as follows:

Table 6.1: Correct Action Plan for different non-compliance environmental issues

Issues	Comment/Suggestion made in the EDDR	Reasons of inadequacy	Corrective Measures	Required committed time period
a) Air pollution	a) Well planned water spraying system in dust pollution places	a) Adequate water spray is not done	a)Implement adequate water spray in the dust generation place / The problem of dust emission in the production process are to be tackled through installing appropriate air treatment plant (ATP)	30 Dec 2016
b) Clay transportation & storing	Clay transportation to be done in covered trucks and storing to be done in under shade	Clay transportation is done in open trucks and Storing	Transport Clay in covered trucks and	Do


Issues	Comment/Suggestion made in the EDDR	Reasons of inadequacy	Corrective Measures	Required committed time period
		is done in open shade	store under the shade	
c) Supply & use of PPE	Protective clothing, goggles, helmets, shoes and accessories to be adequately provided to the workers.	There are supplies of PPE. But, it is rarely used. No enforcement from the authority	Develop a team to look after & enforce EHS measures	Do
d) Dusts inhalation hazard	Strict enforcement on the use of PPEs	There are supplies of PPE. But, it is rarely used. No enforcement from the authority	Develop a team to look after & enforce EHS measures	Do
e) Accident risks in work place	Preparedness drill to be done on a regular basis and PPEs are to be used	Drills don't take place and workers are not equipped with PPE,s	Develop a team to look after & enforce EHS measures	Do
f) Emission of particulate matters & flue gases ( SPM, PM <sub>10</sub> , PM <sub>2.5</sub> , CO, NO <sub>x</sub> )	Develop a plan and arrangements for regular monitoring of air quality and occupational health issues	Emissions tests have not been carried out.	Conduct environmental monitoring according to EDDR's EMP	30 June 2017

## **7. Conclusions**

The sub-project is in full regulatory compliance. The emission level through the exhausts of the sub-project has been observed to be minimal. It is expected to meet the regulatory standard limit. It is also doing fairly good in terms of overall environmental management and occupational health & safety (OHS). Suggested EMP & OHS plans are in the process of implementation. However, suggested air quality monitoring plan is yet to be taken care of.




**Sub-project in pictures during site visit**

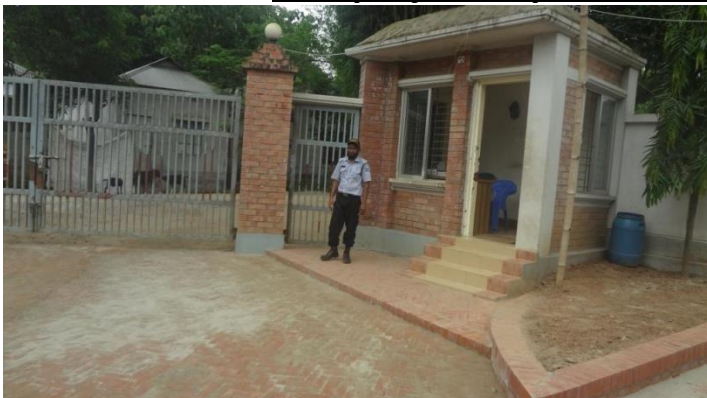

← Security Guard at the front gate


Dryer for the green bricks



Green Bricks entrance and exit  
in Dryer by mechanical control  
panel




Manual Stacking of Dried  
Bricks for firing



Automatic coal feeding in the  
Kiln



Top of Tunnel Kiln (Brick Firing)

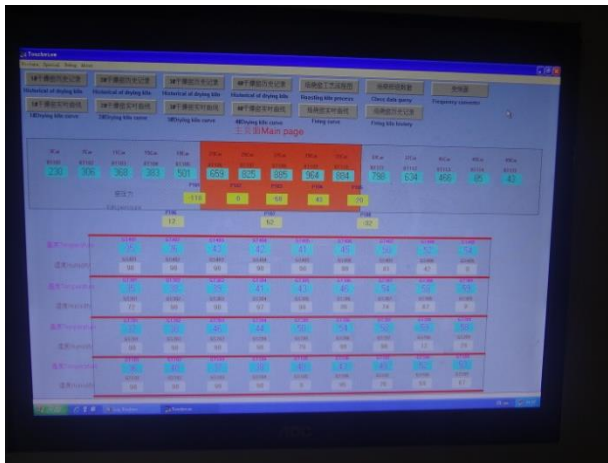


Snap shot of table and curve of tunnel kiln temperature (firing tunnel) from the control room




Finished Brick stack yard




Hollow Brick stack



Fire extinguisher mounted on the wall



Proper guard rail for the operator working at height



← Accommodation for the employees in the factory premises

Accommodation arrangement for the workers at rented houses



Discussion with the entrepreneur during the site visit
